



profonanpe

recursos para la naturaleza

# Profonanpe

---

The environmental fund of Peru

## Vision

---

Be the main partner in Latin America for the implementation of the environmental agenda



profonanpe  
recursos para la naturaleza

# What do we do?

## A private non-profit entity



Fundraising and administration of financial resources

1



Execution of programs and projects

2



Conservation of biodiversity, mitigation and adaptation of climate change.

3



# Projects



**+85%**  
16 projects

**Execution in almost all subnational regions of the country**

# Adapting to Impacts of Climate Change on Peru's Coastal Marine Ecosystem and Fisheries



- Main goal: To support the Peruvian Government in the reduction of vulnerability in the coast communities facing the impacts of climate change in the coastal marine ecosystems and its fishery resources.



# Components

1

Interventions in pilot strategic sites to improve resilience of target coastal communities

2

Efficiente surveillance and prediction system supporting fisheries adaptive management

3


Capacity building and KM system for implementing EBA and the EAF

4


Management policies, regulations and measures promoting resiliency



# Challenges and actions during COVID 19

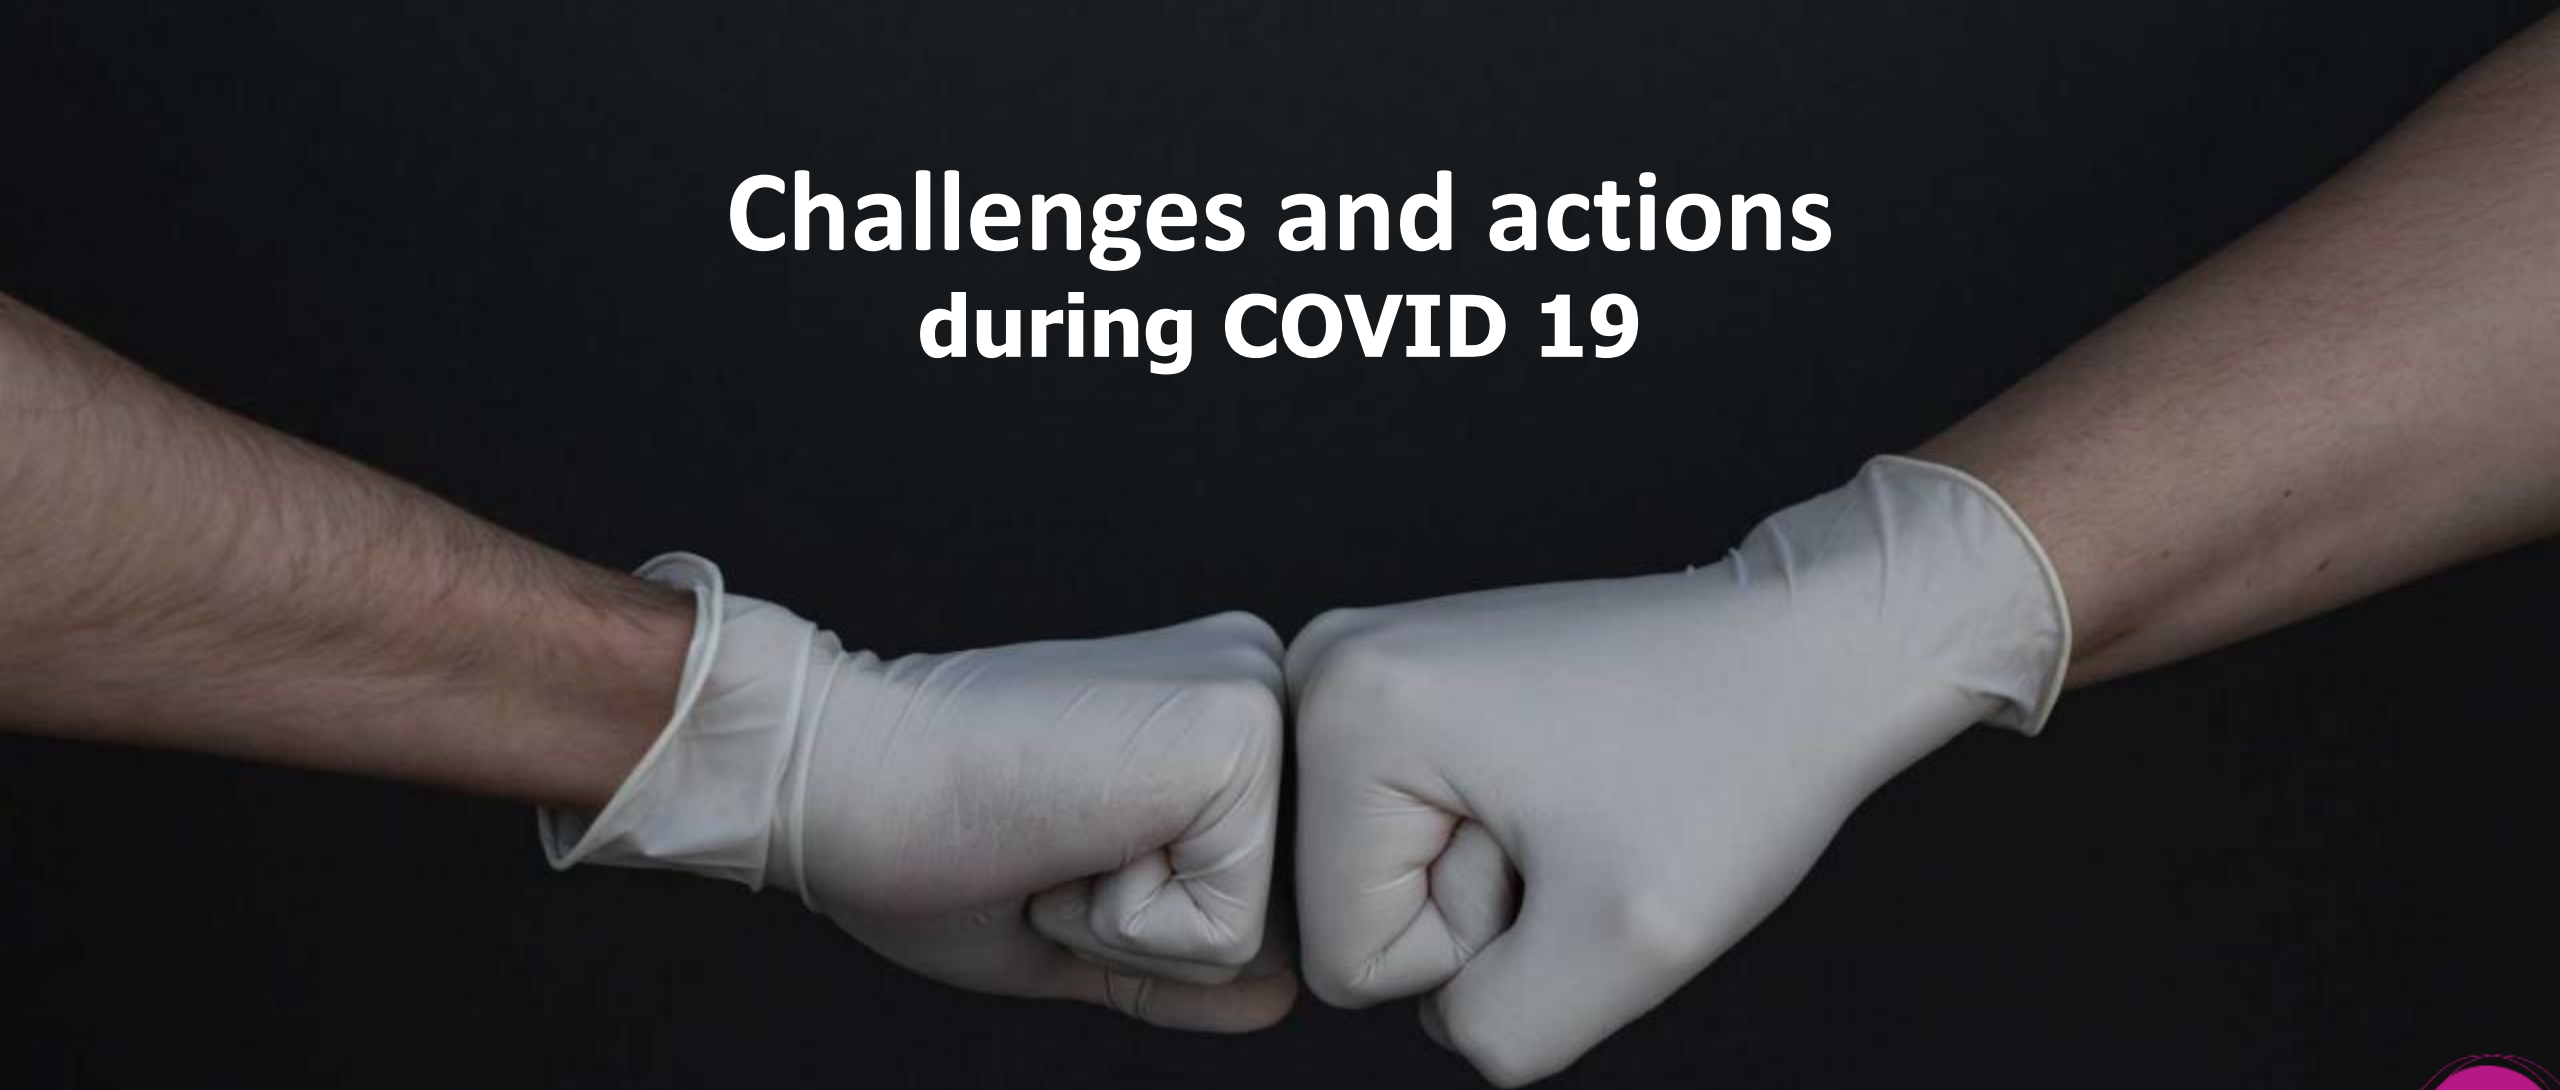


## Changes experienced



- Assumptions that nobody expected
  - Basic needs of the prioritized beneficiaries (fisheries).
  - New ways of living (social distancing).
  - Lockdown (107 days) and sanitary emergency.
  - Economic recession.
- All the activities in the ground stopped.



# Starting point



# What we did?

1



Clustering of activities specially consultancies

2



Support beneficiaries with safety equipment

3



Organize and support itinerary markets

4



Development of biosecurity protocols for the Project

5



Reprogram the AOP: # of travels and workshops

6



Evaluate the timeline of the project

# Itinerary markets: empowering women



## Current actions



- **Accelerate all activities** that were paralyzed or delayed as a result of the pandemic.
- Accelerate the **calls and contracts of the thematic packages** in a way that allows improving the technical execution of the project.
- Develop the activities within the **norms for pandemic control** at the national level, following established protocols and the use of adequate equipment by both project staff and beneficiaries.
- Evaluate the **possibility of a temporary extension** for the implementation of project activities.





profonanpe

recursos para la naturaleza
