



ADAPTATION FUND

AFB/PPRC.36/Inf.1
15 September 2025

Adaptation Fund Board
Project and Programme Review Committee
Thirty-sixth Meeting
Bonn, Germany, 7-8 October 2025

PROPOSAL FOR INDONESIA (3)



ADAPTATION FUND

ADAPTATION FUND BOARD SECRETARIAT TECHNICAL REVIEW OF PROJECT/PROGRAMME PROPOSAL

PROJECT/PROGRAMME CATEGORY: Regular Size Full Proposal

| | |
|------------------------------------|--|
| Country/Region | : Indonesia, Asia & Pacific |
| Project Title | : Village Based Coastal Adaptation and Resilience in Lombok Province of West Nusa Tenggara |
| Thematic Focal Area | : Coastal management |
| Implementing Entity | : Kemitraan – Partnership for Governance Reform |
| Executing Entities | : Lombok Climate Change Consortium (LC3) |
| AF Project ID | : AF00000307 |
| IE Project ID | : Requested Financing from Adaptation Fund (US Dollars): 998,739 |
| Reviewer and contact person | : UnaMay Gordon Co-reviewer(s) : |
| IE Contact Person | : Eka Melisa |

Technical Summary

The project “Village Based Coastal Adaptation and Resilience in Lombok Province of West Nusa Tenggara” aims to implement a coastal village-based climate adaptation and resilience project on Lombok Island, while achieving three goals, namely: 1) Developing village-based local climate resilience institutionalization mechanisms in the coastal area of West Lombok, 2) Improving community livelihoods that are resilient and adaptive to climate change, and 3) Increasing the carrying capacity of ecosystems and the environment of coastal areas in strengthening the sustainability of adaptation and climate resilience. This will be done through the three components below:

Component 1: Increased and established awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts (USD 291,751);

Component 2: Improved and established adaptive capacity for rural coastal community to climate-induced hazards (USD 264,836);

Component 3: Improve resilience of coastal ecosystem to strengthen community livelihood resources (USD 300,721).

Requested financing overview:

Project/Programme Execution Cost: USD 62,189

Total Project/Programme Cost: USD 858,308

Implementing Fee: USD 78,242

Financing Requested: USD 998,739

The initial technical review raised some issues, such as the need to provide further information on the comprehensive description of the suite of adaptation interventions, the potential cost-effectiveness and project’s compliance with the Fund’s Environmental and Social Policy, among others, which are yet to be demonstrated or strengthened, as is discussed in the number of Clarification Requests (CRs) and Corrective Action Requests (CARs) raised in the review.

The second technical review finds that some issues have been clarified, while others pertaining to a clarification of whether the suite of adaptation options have been fully identified and issues related to the project’s compliance with the Fund’s ESP are yet to be demonstrated, as is discussed in the remaining CRs and CARs not addressed below.

The third technical review finds that some issues have been clarified but others still require clarification such as the Environmental and Social Principles, risk framework, alignment with results areas of the fund and the Environmental and Social Management Plan as discussed in the remaining CRs and CARs raised in the review.

Date:

22 August 2025

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|---------------------|---|--|--|---|
| Country Eligibility | 1. Is the country party to the Kyoto Protocol and/or the Paris Agreement? | Yes. | - | - |
| | 2. Is the country a developing country particularly vulnerable to the adverse effects of climate change? | Indonesia is vulnerable to the adverse effects of climate change, and the project target area – west Nusa Tenggara - is vulnerable to climate-induced disasters such as tidal flooding, abrasion and landslides. | - | - |
| Project Eligibility | - Has the designated government authority for the Adaptation Fund endorsed the project/programme ? | Yes. An Endorsement letter is included in the proposal is dated 5 August 2022 and signed by the DA on record | - | - |
| | - Does the length of the proposal amount to no more than One hundred (100) pages for the fully-developed project document, and one hundred (100) pages for its annexes? | Yes. | - | - |
| | - Does the project / programme support concrete | Not cleared. | | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|--|---|
| | <p>adaptation actions to assist the country in addressing adaptive capacity to the adverse effects of climate change and build in climate resilience?</p> | <p>The project seeks to develop a village-based climate resilient institutionalization mechanism in targeted villages in West Lombok, improve community livelihoods and sources of income for vulnerable people and increase the carrying capacity of coastal ecosystems. This will be achieved by strengthening the local governance on climate-induced disaster risk management in coastal areas, by applying models of coastal adaptation and rehabilitation of coastal ecosystems in the selected communities. However, the climate adaptation models on the selected sites are generic and specific adaptation models will be developed based on the community climate risk analysis.</p> <p>The project mentions that the occurrence of tidal flooding has always been repeated in the last 20 years, with efforts to reduce tidal flooding' impacts by various parties not being effective. CR1: Please clarify how the project will ensure successful and sustainable impacts in reducing tidal flooding, given the</p> | <p>CR1: Not cleared. Please clarify how the project will support the climate action plan of the provincial government for 2019-2023. Additionally clarify if a new action plan has been developed and how the project is aligned to it.</p> | <p>CR1: Cleared as per paragraph 18, page 9.</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|--|--|---|
| | | <p>ineffectiveness of previous efforts over the past 20 years. Specify what will be done differently in this project to guarantee lasting results.</p> <p>CAR1: Kindly consider including a theory of change that clearly demonstrates how the proposed activities address the identified climate change threats. This will enhance the cohesion and logical flow between project components.</p> <p>It is noted that the project target villages are already part of the governmental programs: Proklim, Tourism or Disaster resilience.</p> <p>CR2: Please clarify how Outputs 1.1 and 1.2 will complement existing governmental programs such as Proklim, Tourism, and Disaster Resilience, which already target the project villages.</p> <p>CR3: Provide a strong justification for conducting the village-level climate risk analysis during project implementation rather than during the project design</p> | <p>CAR1: Cleared, As per TOC included in page 11.</p> <p>CR2: Cleared. This project will facilitate stakeholder forums and implement essential climate actions not addressed by government programs or existing initiatives in non-targeted villages Please provide relevant clarification also in the project document.</p> <p>CR3: Cleared. The analysis has been conducted during project design stage but detailed consultations will be carried out during implementation.</p> | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|---|---|---|
| | | <p>phase. Please explain the rationale and expected benefits of this timing.</p> <p>A generic suite of adaptation actions is included under output 2.2 (silvofisheries; climate smart land farming; infrastructure for ecotourism village).</p> <p>CR4: Please clarify whether the suite of adaptation actions listed under Output 2.2 (e.g., silvofisheries, climate-smart farming, and ecotourism infrastructure) and Output 3.2 (business opportunities identified through a study) is exhaustive. If not, kindly specify the process for identifying additional actions during implementation.</p> | <p>Please provide relevant clarification also in the project document.</p> <p>CR4: Cleared, As per additional information provided on page 16.</p> | |
| | <p>- Does the project / programme provide economic, social and environmental benefits, particularly to vulnerable communities, including gender considerations, while avoiding or mitigating negative impacts, in</p> | <p>Not cleared.</p> <p>The project includes information on the expected benefits in all the different dimensions. The intervention is expected to increase the income of fisherman and farmers and to provide improve the environment around the areas affected by tidal floods, through green and</p> | | <p>-</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|---|---|
| | <p>compliance with the Environmental and Social Policy and Gender Policy of the Fund?</p> | <p>gray measures (mangrove plantation and retaining embankments).</p> <p>CR5: Please justify why the project does not anticipate benefiting an equal number of men and women. Kindly explain how the benefits will be equitably distributed among vulnerable households and individuals.</p> <p>CR6: This section refers to the development of various processed products by prioritizing fewer chemicals or organic products. Please provide more detail on the “processed products” referred to in the proposal, including the types of products envisioned and the facilities or infrastructure required for their development.</p> | <p>CR5: Cleared, As per additional information provided on page 18. Most of the affected livelihoods are male dominant, according to the results of the gender assessment.</p> <p>CR6: Cleared, As per information provided on page 16, paragraph 30.</p> | |
| | <p>- Is the project / programme cost effective?</p> | <p>Not cleared.</p> <p>The proposal provides a logical explanation of the selected scope and approach; however, the cost effectiveness should also be demonstrated from a</p> | | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--|---|--|--|
| | | <p>sustainability viewpoint and alternative options from the ones proposed in the project, should be included.</p> <p>CR7: Please clarify how the project demonstrates cost-effectiveness from a sustainability perspective. Provide specific examples or evidence to support this claim.</p> <p>CAR2: Kindly include a detailed description of alternative options to the proposed measures, with a comparison to justify the selection of the chosen approach. This will strengthen the assessment of the project's cost-effectiveness.</p> | <p>CR7: Not cleared. Please clarify how the proposed approach is cost-effective also from a sustainability perspective.</p> <p>CAR2: Cleared. An analysis of alternative options to the proposed project solutions, has been provided in table 9 and 10.</p> | <p>CR7: Cleared as per paragraphs 50 – 55 on pages 22-25.</p> |
| | <p>- Is the project / programme consistent with national or sub-national sustainable development strategies, national or sub-national development plans, poverty reduction</p> | <p>Yes.</p> <p>The proposal is aligned with national and sub-national sustainable development strategies, such as: the sustainable development strategy, NAP, Indonesia Communication on Adaptation, different presidential/ministerial and</p> | <p>-</p> | <p>-</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--|--|--|--|
| | strategies, national communications and adaptation programs of action and other relevant instruments? | gubernatorial regulations related to environment and climate change adaptation. The project is also relevant to supporting the NDC at local scale. | | |
| | - Does the project / programme meet the relevant national technical standards, where applicable, in compliance with the Environmental and Social Policy of the Fund? | <p>No.</p> <p>The proposal lists relevant national technical standards it does not provide the linkage to specific project activities nor states how their compliance will be met.</p> <p>CAR3: Please include information on how compliance with the national technical standards listed will be met, in addition, provide information on the relevance of the national standard listed to specific project activities. Include the steps taken to comply with the technical standard and explain how the authorization/clearance granted for the project would be implemented.</p> | <p>CAR3: Not cleared. The proposal now includes a list of regulations and policies and states that the project activities will comply with these, but kindly include also information on how these technical standards will be met.</p> | <p>CAR3: Not cleared.</p> <p>The amendments as per paragraph 60 on pages 26-27, and Table 13 on pages 27-28 are noted.</p> <p>However, please clearly indicate the compliance, procedures and authorising offices for each regulation.</p> |
| | - Is there duplication of project / programme with | No. | - | - |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|--|---|
| | other funding sources? | The proposal outlines the linkages and synergies with all the relevant overlapping projects, including areas of complementarity and how the project will draw lessons from earlier initiatives. The list of initiatives taking place in the project target areas, includes the timeline of project implementation, project objective and funding source. | | |
| | - Does the project / programme have a learning and knowledge management component to capture and feedback lessons? | Yes , the project includes activities to strengthen communities and local actors' capacities and products to disseminate information and knowledge, these are listed in table 13 of the project document. | - | - |
| | - Has a consultative process taken place, and has it involved all key stakeholders, and vulnerable groups, including gender considerations in compliance with the Environmental and Social Policy | Not cleared. It appears that consultations were conducted primarily for the development of the concept note, with no evidence of additional consultations for the fully developed proposal. Furthermore, the most recent consultation took | | - |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--------------------------------|---|--|---|
| | and Gender Policy of the Fund? | <p>place over a year ago. Kindly note that meaningful consultations should be carried out at each stage of the project proposal development process.</p> <p>CAR4: Kindly move paragraphs 51 to 53 to the Gender Assessment section for better alignment.</p> <p>CR8: The outcomes of the consultations are not reported in the project proposal. Please specify how the outcomes of consultations have been incorporated into the project design, particularly the concerns of vulnerable groups and women.</p> <p>CR9: Please clarify if consultations with central government took place. It seems that district level authorities have been consulted, but there is no mention on authority at the central level.</p> <p>CAR5: Please include a report documenting the</p> | <p>CAR4: Cleared.</p> <p>CR8: Cleared. As per additional information provided on page 22 paragraph 47.</p> <p>CR9: Cleared.</p> <p>CAR5: Cleared. The proposal now includes information on the</p> | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|---|---|
| | | consultative process. This needs to contain: <ol style="list-style-type: none"> 1. A list of stakeholders consulted (with rationale for selection, roles, and dates of consultation). 2. A description of consultation techniques tailored to target groups. 3. Key findings, including suggestions and concerns raised during consultations. | consulted groups with dates of consultations and key findings/outcomes of these consultations as described in table 4 on page 34. | |
| | <ul style="list-style-type: none"> - Is the requested financing justified on the basis of full cost of adaptation reasoning? | <p>Cleared.</p> <p>The proposal demonstrates that the project activities are relevant in addressing its adaptation objectives and the additionality of the proposed project compared to a baseline scenario is sufficiently justified.</p> | - | - |
| | <ul style="list-style-type: none"> - Is the project / program aligned with AF's results framework? | <p>Yes, the project indicates alignment with the Fund's SRF.</p> | - | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|---|---|
| | <p>- Has the sustainability of the project/programme outcomes been taken into account when designing the project?</p> | <p>The project outlines how institutional arrangements will support the sustainability of the project interventions, however there is no information with regard to the social, and environmental sustainability.</p> <p>CR10: Please provide information on the mechanism to ensure that the adaptation benefits can be sustained over time and potentially replicated or scaled-up after the project's finalization.</p> <p>CR11: Please describe the specific arrangements for sustaining adaptation measures, such as mangrove plantations (growth monitoring) and hard infrastructure maintenance. Include details on the roles of stakeholders involved in these arrangements.</p> | <p>CR10: Cleared. As per additional information provided on page 40. The project aims to collaborate also with non-state actors through MOUs to support sustainability of the proposed options.</p> <p>CR11: Cleared. As per additional information provided on page 30 Paragraphs 62 and Table 13.</p> | |
| | <p>- Does the project / programme provide an overview of environmental and</p> | <p>Not cleared. The environmental and social screening identifies a</p> | | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|---|---|---|
| | <p>social impacts / risks identified, in compliance with the Environmental and Social Policy and Gender Policy of the Fund?</p> | <p>couple of risks that the project presents, however the screening is not comprehensive. If the suite of adaptation interventions has not been fully identified (magnitude, location), then the project presents USPs. In this sense the environmental and social risk screening needs to include all cumulative, direct and indirect risks related to project activities/suite of possible adaptation options identified so far.</p> <p>CR12: Please clarify whether the project includes Unidentified Sub-Projects (USPs). If so, kindly justify their inclusion, as these are acceptable only in exceptional cases.</p> <p>CAR6: Please revise the environmental and social risk screening to include all cumulative, direct, and indirect risks associated with project activities. For example, consider potential invasive species risks in mangrove plantations and</p> | <p>CR12: Not Cleared. The clarification refers to the execution arrangements and does not confirm whether all the project activities have been fully identified, thus not including USPs.</p> <p>CAR6: Not cleared. The proposal now includes a few identified risks but the list should be more comprehensive. Please consider all cumulative, direct and indirect risks. For example, the embankment construction</p> | <p>CR12: Not cleared.</p> <p>The amendments as per pages 79-80, the proponent indicated that there will be no USP during project implementation.</p> <p>CAR6: Not cleared.</p> <p>Table 19 is incomplete. Please ensure it is aligned with the narrative below.</p> <p>Please refer to the AF ESP Guidelines and update Table 19. As per guidelines, note that some principles always apply: Principle 1 Compliance with Law, Principle 4 and Principle 6. X is for instances in column 2</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|--|--|---|
| | | <p>impacts on natural habitats from embankment construction (2km).</p> <p>CAR7: Kindly conduct a comprehensive environmental and social impact assessment (ESIA) that:</p> <ol style="list-style-type: none"> 1. Identifies all potential direct, indirect, transboundary, and cumulative impacts of the project. 2. Recommends measures to avoid, minimize, manage, or mitigate these impacts. | <p>might lead to risks related to protection of natural habitats and conservation of biological diversity.</p> <p>In addition, please add to the project document all the identified risks for mangrove plantation which were reported as a response in the review sheet.</p> <p>CAR7: Not Cleared</p> <p>Please note that undertaking an ESIA is mandatory if the environmental and social risk screening identifies major risks for any of the ESP principles, in compliance with the Fund' ESP.</p> <p>We understand that for 2,350 meters of embankment construction, national regulations do not require an ESIA but rather a "require UKL-UPL</p> | <p>where no further assessments are required. The risk level (low, medium, high) should be included in column 3 along with the mitigation measure that will be taken to address any risk. Please https://www.adaptation-fund.org/wp-content/uploads/2016/07/ESP-Guidance_Revised-in-June-2016_Guidance-document-for-Implementing-Entities-on-compliance-with-the-Adaptation-Fund-Environmental-and-Social-Policy.pdf</p> <p>CAR7: Cleared as per 79-81 on page 38 However, more information is required as embankments improvements are still associated with risks. Therefore, further elaboration on risk mitigation measures is required.</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|---|---|---|
| | | <p>AR8: Please expand the Gender Assessment to include a Gender Action Plan report that outlines specific gender-responsive actions and monitoring indicators.</p> | <p>licensing”. It is noted that this document identifies all the impacts that could occur and highlights environmental management and monitoring efforts to minimize impacts and that currently the compilation of this document has been deferred to project implementation. Please note that this would need to be developed as part of the project formulation, to demonstrate compliance with the Fund’s ESP.</p> <p>CAR8: Not cleared.</p> <p>Information has been provided on page 22, however please convert it into a table format and include headings for indicators; targets; monitoring arrangements. In addition, provide clarification on the alignment of the Gender Action Plan with the outcomes stemming from the Gender Assessment.</p> | <p>CAR8: Cleared as a Gender Action Plan has been included.</p> <p>Note: Please include an active Table of Content to facilitate easy navigation and reading of the document.</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------------------|--|---|--|---|
| Resource Availability | 1. Is the requested project / programme funding within the cap of the country? | Yes. | - | |
| | 2. Is the Implementing Entity Management Fee at or below 8.5 per cent of the total project/programme budget before the fee? | Yes, the IE fee amounts to 8.5% of the total project budget before the IE fee. | - | - |
| | 3. Are the Project/Programme Execution Costs at or below 9.5 per cent of the total project/programme budget (including the fee)? | Yes, the project execution costs amount to 6.3% of the total project budget. | - | - |
| Eligibility of IE | 1. Is the project/programme submitted through an eligible Implementing Entity that has been accredited by the Board? | Yes. | - | - |
| Implementation Arrangements | 1. Is there adequate arrangement for project / programme | Not cleared. The implementation arrangements include a clear description of the roles | | CAR9 (re-opened): Please clarify if funds will be transferred directly to Lombok Climate Change Consortium (LC3). This is critical since at |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|---|--|--|
| | management, in compliance with the Gender Policy of the Fund? | <p>and responsibilities of the stakeholders involved in the project and includes provisions to support gender mainstreaming. However, project cover page specifies that “Lombok Climate Change Consortium (LC3)” is the executing entity for this project. However, paragraph 68 states that Kemitraan will be the executing entity.</p> <p>CAR9: Please remove the inconsistency regarding the executing entity and be advised that if Kemitraan acts as EE, the project execution costs need to be capped at 1.5% of the total project cost, therefore amend the project execution cost as necessary. A justification for this type of implementation arrangement, which is possible on an exceptional basis, needs also to be provided. In addition, deviation above the 1.5% cap is possible on an exceptional basis, however,</p> | <p>CAR9: Cleared. As per revisions made on page 59 and throughout the proposal. Kemitraan will not act as Executing Entity.</p> | <p>legal agreement stage only the named EE will be name in the document.</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|---|--|---|
| | | strong justifications need to be provided as well. | | |
| | 2. Are there measures for financial and project/programme risk management? | <p>The project includes the major risks and outlines mitigation measures to address them, however a monitoring plan is not included.</p> <p>CAR10: As part of the set of proposed mitigation measures include also the responsible actors and the monitoring frequency if relevant.</p> <p>CAR11: Please remove the risks under the category “project implementation” as those refer to environmental risks as opposed to management risks and include these considerations in the environmental and social risk screening section.</p> | <p>CAR10: Not cleared. In table in section B, please add also the responsible institution for monitoring the application of mitigation measures.</p> <p>CAR 11: Cleared. Environmental and social risks have been removed from table in section B.</p> | <p>CAR10: Not cleared. 1. In the column labelled Responsible Person, it lists roles such as Finance Officer etc. 2. Please also indicate which entity this person is associated with. 3. Please indicate the frequency of monitoring. Will it be annual, bi-annual or quarterly?</p> |
| | 4. Are there measures in place for the management of environmental and social risks, in line with the Environmental and | <p>Not cleared. The environmental and social management plan (ESMP) included in the proposal needs to be in line with the environmental and social risk screening and</p> | | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--|---|---|--|
| | Social Policy and Gender Policy of the Fund? | <p>need to include budgetary provisions for its implementation and a mechanism for consultation and adaptive management.</p> <p>CAR12: Please revise the Environmental and Social Management Plan (ESMP) to align with the revised environmental and social risk screening. Ensure the ESMP includes:</p> <ul style="list-style-type: none"> • Provisions for USPs (if applicable) to ensure compliance with the Environmental and Social Policy during implementation. <ul style="list-style-type: none"> • A mechanism for ongoing consultation and adaptive management. • Budgetary provisions for ESMP implementation. • Clear labeling of columns, replacing "possible risk" with "project activity" and "identified impact" with "identified risk." | <p>CAR12: Not cleared. The ESMP is not aligned with the findings of the environmental and social risk screening.</p> <p>In addition, the comment on the USPs remains valid and yet to be assessed.</p> | <p>CAR12: Not cleared.</p> <ol style="list-style-type: none"> 1. There appears to be misalignment between Annex 2: ESMP and Table 19 Checklist of Environment and Social Principles. For example, Table 19 and the narrative for Compliance with Laws indicate that no risks or impacts yet Annex 2 states the possible risks. 2. As per paragraphs 79-80, there will be no USPs, please ensure all activities are known and have identified locations. Otherwise this could affect environmental and social risk identification. |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|---|--|---|
| | | <ul style="list-style-type: none"> Updates to the grievance mechanism, including an EE email address, clarification of the complaint process, and a specified form for grievances. Please add as appropriate. In addition, in the grievance mechanism it is reported "<i>Complaints arising from stakeholders and the general public involved in the Executing Entity (EE) to be submitted to the Implementing Activities to be discussed together to find a way out. If consensus is not reached, a complaint can be submitted to the National Implementing Entity (NiE) using the form</i>". The sentence is a bit unclear. If | | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--|--|--|---|
| | | project stakeholders need to fill a complaint to the EE as first point of entry, please specify which form needs to be used. It seems that just the one to be address to Kemitraan is provided. | | |
| | 5. Is a budget on the Implementing Entity Management Fee use included? | <p>No. The budget in section G nor the separate excel file, include a breakdown of the IE fee.</p> <p>CAR13: Include in table in section G a breakdown of the IE fee.</p> | <p>CAR13: Cleared. The IE fee budget breakdown is included in the budget provided in excel.</p> | - |
| | 6. Is an explanation and a breakdown of the execution costs included? | <p>Not cleared. A breakdown of the project execution costs is just included in the separate excel file, kindly include it also in the main proposal in section G.</p> <p>CAR14: include a breakdown of the project execution costs as part of the detailed project budget.</p> | <p>CAR14: Cleared. The execution cost budget breakdown is included in the budget provided in excel.</p> | |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|---|--|
| | 7. Is a detailed budget including budget notes included? | <p>Not cleared.</p> <p>Yes, a detailed budget including details at activity level was submitted through a separate excel file.</p> <p>CR13: Please specify what the HO budget line stands for.</p> | <p>CR13: Cleared.</p> <p>As per amendment to budget on page 66-67 on the tracked changed version of the re-submission.</p> | |
| | 8. Are arrangements for monitoring and evaluation clearly defined, including budgeted M&E plans and sex-disaggregated data, targets and indicators, in compliance with the Gender Policy of the Fund? | <p>Not cleared.</p> <p>The M&E plan does not include provisions for the terminal evaluation nor for the baseline report.</p> <p>CAR15: Please include budget lines to cover the project baseline report and the terminal evaluation.</p> | <p>CAR15: Not cleared.</p> <p>Table in section D does not include budget lines to cover project baseline report and independent terminal evaluation.</p> | <p>CAR15:Not Cleared.</p> <p>Amendments as per Table 28 in Section G provides budget lines to cover project baseline report and independent evaluation are noted. However, please clarify if the GEDSI is for one component or the entire project. Also, please indicate who will be overseeing the Gender Action Plan.</p> |
| | 9. Does the M&E Framework include a break-down of how implementing entity IE fees will be utilized in the | <p>Not cleared.</p> <p>The M&E budget included in section D amounts to US\$ 187,728, which corresponds to 18.7% of the total project</p> | | <p>CAR16 (re-opened).</p> <p>1. The proposed budget allocates a total of USD 15,810 for the Baseline assessment, the Mid-Term Review and the Final Evaluation. This represents 1.6 % of the total project</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|----------------------------------|--|--|--|
| | supervision of the M&E function? | <p>budget. The M&E Plan has to be budgeted with breakdown of IE fees for supervision of M&E function.</p> <p>CAR16: Include M&E costs as part of the IE fees for supervision of the M&E function.</p> | <p>CAR16: Cleared. As per revised detailed budget in excel.</p> | <p>cost. Kindly revise these figures in all relevant sections of the proposal to ensure it is min at 5% of the total project cost, which is the recommended range for projects of this size (see table 3 in https://www.adaptation-fund.org/wp-content/uploads/2023/10/AFB.EFC.32.7_Evaluation-Policy-Budget-Implication_clean.pdf)</p> <ol style="list-style-type: none"> 2. Reference to the Project Completion Summary (mandatory reporting requirement - see https://www.adaptation-fund.org/projects-programmes/project-performance/) is missing from Part III.D. Please kindly add it. 3. While the project includes an ESMP describing environmental and social risk management measures, the M&E plan does not include any reference to ESMP monitoring during implementation. Please revise the M&E plan to ensure that it addresses management of the environmental and social risks identified, and that dedicated budgetary provisions are made in the detailed budget for implementation of the ESMP. |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|---|--|--|---|
| | <p>10. Does the project/programme's results framework align with the AF's results framework? Does it include at least one core outcome indicator from the Fund's results framework?</p> | <p>Not cleared.</p> <p>The results framework presents quantified expected results and baseline data, however there are some discrepancies between indicators and targets units of measurement and gender responsive targets disaggregated by sex need to be included.</p> <p>CAR17: The alignment with the AF strategic results framework (table in section F) is inconsistent with the project alignment reported in section A paragraphs 22 to 24, which state that the project is aligned with outcomes 1,3,4,5 and 6 of the AF SRF. Table in section F instead reports alignment just to outcomes 2, 3 and 5. In addition, please indicate the total amount invested for each output in addition to outcome level.</p> | <p>CAR 17: Not Cleared. There is still inconsistency between the figure of the theory of change and table in section F.</p> <p>CAR18: Not cleared.</p> | <p>CAR 20 (NEW):</p> <ol style="list-style-type: none"> 1. Add the three Project Objectives (listed in the "Project/Programme Components and Financing" section) to the project results framework. The Project Objective(s) describe the overall purpose of the project interventions, which includes the intended physical, financial, institutional, social, environmental, or other results that the project interventions is expected to achieve or to which it is expected to contribute. 2. Add Project Objective Indicator(s) to the project results framework. These indicators should capture the overall results that the project interventions are expected to achieve. 3. Although the Gender Action Plan provides a set of gender-specific indicators and targets, those are not reflected in the project results framework. Please ensure that the project results framework captures the indicators and associated targets included in the Gender Action Plan. |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|--|---|--|
| | | <p>CAR18: Under project component 2, the indicators are measured as “number of”, whereas the targets are reported in percentages, please ensure consistency preferably revising the targets with quantifiable ones. For all targets indicate the number of women benefitting. Under output 3.2 for the indicator “number of project beneficiaries trained” please revise the target to have the same unit of measurement and include gender disaggregation.</p> <p>CAR19: Annex 7 present the list of core indicators to which the project will report to, however some of those listed are not core indicators. Please remove those as relevant, by referring to the AF’s results framework available here: https://www.adaptation-fund.org/wp-content/uploads/2019/10/Adaptation-Fund-Strategic-Results-Framework-</p> | <p>Please make the amendment at Table 18 under Component 2 under the Target column.</p> <p>CAR19: Not Cleared. There are indicators which are not core indicators and are not relevant in that section. Please recall the that AF core indicators are (1) Number of beneficiaries; (2) Early Warning System; (3) Assets Produced, developed; Improved, or Strengthened;(4) Increased income, or avoided decrease in income or (5) Natural Assets Protected or Rehabilitated.</p> | <p>CAR17: Not cleared. The alignment table provided in part III.F must be revised in accordance with the guidance provided in Annex 5 of the OPG (refer to the example on p.16). The template currently used in the funding proposal differs from the one included in Annex 5.</p> <p>Please revert to the correct template, ensuring that the original headings remain unchanged. More specifically: - Upper section of the table: i) In the "Project Objective(s)" column, please enter the three Project Objectives listed in the "Project/Programme Components and Financial" section; ii) in the "Project Objectives indicator(s)" column, enter the Project Objectives Indicator(s) to be added to the results framework (see above CAR);</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|--|--|---|
| | | Amended-in-March-2019-2.pdf | | <p>iii) for each Project Objective indicator, select only the most appropriate Fund Outcome and enter it in the "Fund Outcome" column;</p> <p>iv) for each Fund Outcome listed, select only the most relevant Fund Outcome Indicator and enter it in the "Fund Outcome Indicator" column; v) enter the grant amount for each Fund Outcome selected in the "Grant Amount (USD)" column, ensuring that the total equals the project activity cost (USD 858,308);</p> <p>- Lower section of the table:</p> <p>i) list the three project outcomes identified in the project results framework in the "Project Outcome(s)" column, along with their respective outcome-level indicators in the "Project Outcome Indicator(s)" column;</p> <p>ii) for each Project Outcome indicator, select only the most relevant corresponding Fund Output and enter it in the "Fund Output" column;</p> <p>iii) choose only the most relevant Fund Output Indicator for each Fund Output selected and enter it in the "Fund Output Indicator" column; and</p> <p>iv) input the grant amount for each Fund Output selected in the "Grant Amount</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|--|--|---|
| | | | | <p>(USD)" column, ensuring that the total equals the project activity cost of USD 858,308.</p> <p>- Ensure that all Fund Outcomes associated with the Fund Outputs listed in the lower section are also reflected in the upper section of the table.</p> <p>CAR18: Not cleared. In Table 26, please ensure targets are gender disaggregated e.g. be sure that number of women or women's organisations benefiting are included in all targets, as appropriate.</p> <p>CAR19: Not cleared. For each AF Core Indicators relevant to the project interventions (i.e., "Number of beneficiaries", "Assets Produced, Developed, Improved, or Strengthened" and "Natural Assets Protected or Rehabilitated"), please replace the tables</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|--|---|--|---|
| | | | | <p>included as Annex 7 by the Core Indicators table(s) available on pp.10-14 of the document "Methodologies for reporting Adaptation Fund core impact indicators". Kindly ensure that "Baseline" and "Target at project approval" columns are duly completed in each table, and ensure that the figures provided in the tables align with those included in the project results framework. While filling out the "Number of beneficiaries" core indicator table, efforts should be made to disaggregate the direct and indirect beneficiaries by youth (age 15-24).</p> |
| | <p>11. Is a disbursement schedule with time-bound milestones included?</p> | <p>Not cleared. The proposal includes a disbursement schedule including time-bound milestones relative to project inception and the annual reporting requirement. CAR20: Please revise the project milestones date, as now the proposal reports</p> | <p>CAR20: Cleared.</p> | <p>CAR20 (re-opened) Please remove the schedule start date row in the disbursement schedule.</p> |

| Review Criteria | Questions | Comments First Technical Review (8 November 2024) | Comments Second Technical Review (24 February 2025) | Comments Third Technical Review (22 August 2025) |
|-----------------|-----------|---|--|---|
| | | that the project is supposed to start in August 2024. | | |



FULLY DEVELOPED PROPOSAL FOR SINGLE COUNTRY

PART I: PROJECT/PROGRAMME INFORMATION

Title of Project/Programme : Village Based Coastal Adaptation And Resilience In Lombok Province Of West Nusa Tenggara

Country : Lombok Climate Change Consortium (LC3)

Thematic Focal Area : Indonesia

Type of Implementing Entity : National Implementing Entity

Implementing Entity : Kemitraan – Partnership for Governance Reform

Executing Entities : Lombok Climate Change Consortium (LC3)

Amount of Financing Requested : 998,739 (in U.S Dollars Equivalent)

Letter of Endorsement (LOE) signed: Yes No

NOTE: The LOE should be signed by the Designated Authority (DA). The signatory DA must be on file with the Adaptation Fund. To find the DA currently on file check this page: <https://www.adaptation-fund.org/apply-funding/designated-authorities>

Stage of Submission:

- This proposal has been submitted before including at a different stage (concept, fully-developed proposal)
- This is the first submission ever of the proposal at any stage

In case of a resubmission, please indicate the last submission date: 12/28/2025

Please note that fully-developed proposal documents should not exceed 100 pages for the main document, and 100 pages for the annexes.

Project/Programme Background and Context

Provide brief information on the problem the proposed project/programme is aiming to solve. Outline the economic social, development and environmental context in which the project would operate.

1. West Lombok is one of the districts that are vulnerable to tidal flooding' threats. Areas that are vulnerable to tidal flooding' threats are in Lembar and Sekotong subdistricts. Based on data the information system and the climate change vulnerability index (SIDIK) in 2018, West Lombok Regency is included in the vulnerability class 4 (vulnerable)¹. This is also reinforced by data Vulnerability Index Data Information System (VIDS) by MoEF (2018) and Disaster Risk Index (DRI) by the National Board for Disaster Management Report (2023). Referring to DRI (2023), there are 11,159 people will be exposed to extreme waves and abrasion in West Lombok with physical losses of up to USD 8.7 million and social losses of around USD 5.3 million as well as 115 hectares of the natural environment damaged with an estimated loss value of up to USD 0.5 million. The total value of losses from the tidal flood disaster in the affected areas reached USD 14.6 million. In addition, the Exposure and Sensitivity Index of West Lombok is included in the 'medium' category (VIDS, 2018) and the 'high' risk index for disaster threats according to the DRI (2021) as shown in Figure 1 below:

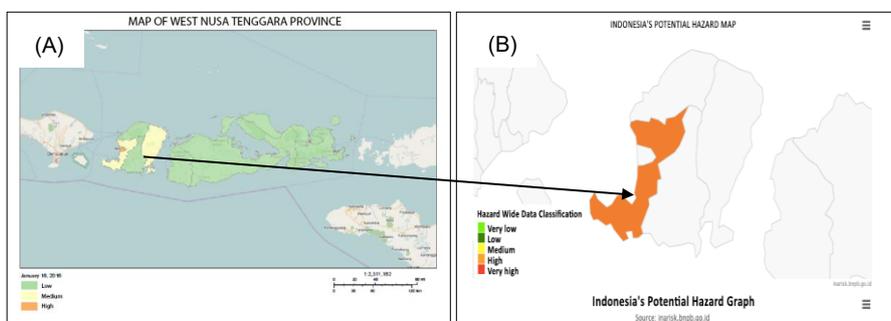


Figure 1. (A) Vulnerability category of West Lombok based on VIDS (2018) and (B) Vulnerability category of West Lombok (DRI, 2021)

2. According to the BMKG data series, there have been changes in rainfall, the number of rainy days, and air temperature over the last 10 years (NTB Climate Change Adaptation Plan, 2019). The range of rainfall in the Lembar and Sekotong Districts is between 1500-2500 mm/year. The air temperature was increased by an average of 0.2°C every 10 years, the number of rainy days decreased with greater rainfall intensity while increasing erratic rain cycle. Changes of these climatic parameters affected to sea anomalies and fluctuations in plant production which are sensitive to rainfall changes (Figure 2).

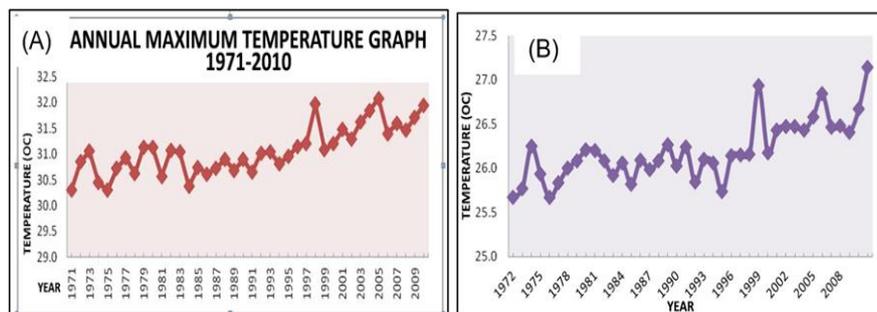


Figure 2. Graph of average temperature and average maximum temperature in 1971-2009
Source: Climatology Station of West Lombok, 2016

¹ <http://sidik.menlhk.go.id/>

- The figure above shows the trend of increasing temperature from 1971 to 2009 which averaged 0.5°C and the maximum temperature increase was around 0.8°C. There is also an increase of the cumulative temperature from 30.5°C in 1971 to 31.5°C in 2009. Thus, there has been increased of 1°C in temperature over the last 40 years. The increased temperature is relatively fast because according to Houghton (1997) that the time tolerance for an increase of 1°C in 100 years. It is predicted that the temperature has increased abnormally. How about the rainfall? If the temperature tends to increase, the rainfall looks to fluctuate (Figure 3).

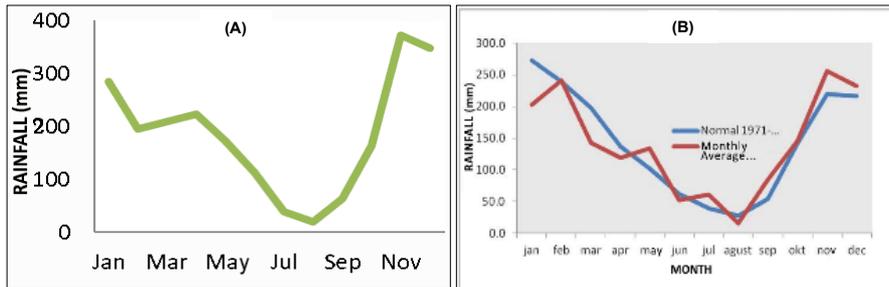


Figure 3. Average monthly rainfall in 1971-2010 (A) and average monthly rainfall in 2010 – 2020 (B)
Source: BMKG of West Lombok, 2021

- Based on the figure above, it shows that there is a tendency to increase the amount of rainfall over the last 10 years (B) rather than the previous 20 years (A). The highest amount of rainfall was in November which reached an average of 380 mm/month compared to the previous 20 years of around 280 mm/month. The implication of high rainfall can trigger flooding and affect the possibility of increased tidal intensity.
- Based on the IPCC's models, the Ministry of Environment-GTZ-WWF (2009) projected sea surface temperature on Lombok Island will increase by 3°C-3.5°C in 2100 with the assumption that sea level will rise between 60-70 cm with the most affected areas are City of Mataram and District of West Lombok. Under conditions of multiple hydro-oceanographic hazards (tide sea water + sea level rise + Niño-Southern Oscillation + storm waves), the submerged area of Lombok Island reaches 5,635 hectares. Markum et al (2008) also reported changes in the coastline of Lombok Island getting closer to the mainland by 2-10 m over the last 10 years (Figure 4).

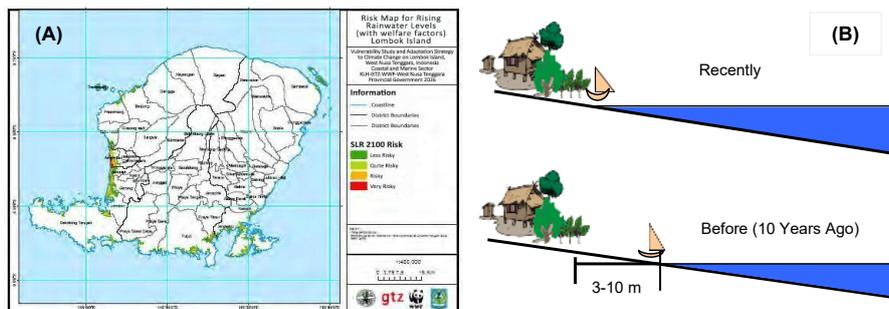


Figure 4. (A) Projection of affected-areas by sea level rise until 2100 (WWF, 2009) and an overview of 10-year coastline shift in Lombok Island (Markum et al, 2008).

- The coastal area of Lombok is the most vulnerable to the climate change impacts if linked with various phenomena such as physical changes of area, behavior changes in fishing by fishermen, and changes in livelihood patterns. Markum et al (2008) also reported changes in three coastal areas of Lombok Island, including Lembar, were indicated by 1) the distance from the shoreline to settlements is closer, 2) a decrease of days at sea by around 40% from the normal situation of 15-20 days per month due to high waves and tidal flooding, and 3) decreasing catches both in quantity and quality of fish while non-fisherman job opportunities are very limited.

7. There are two sub-districts that are very vulnerable to tidal flooding (rob) disasters in West Lombok Regency: Lembar and Sekotong. According to local people (key informants), rob occurs 2-3 a year that triggered by floods in a duration of more than 24 hours. The intensity of its impact is medium to high with a water level of 30-60 cm (RCRA, 2023). This hazard is repeated around November, February, and May (BPBD NTB, 2019). In fact, the current frequency of rob is monthly in 2-3 days during the full moon with a duration of 3-5 hours with low to moderate impact and seawater level reaches 10-30 cm until inundates settlements.



Figure 5. Tidal flooding in sub-district of Lembar on May 2022 and October 2023

8. At the village level in the two sub-districts, there are 4 (four) villages classified as being medium up to high risk of tidal flooding if referred to the vulnerability assessment (see table 1).

Table 1. Analysis of community-level risks to tidal flooding disaster in coastal areas at sub-districts of Sekotong and Lembar, district of West Lombok, Province of West Nusa Tenggara

| Sub-district | Name of Village | The condition of mangroves and their value for the community | The impact of tidal flood | The functioning of capital social | The level of climate change-induced risk based on livelihood assets |
|--------------|------------------|--|---------------------------|-----------------------------------|---|
| Sekotong | Cendi Manik | Very High | Moderate | Very High | Moderate |
| | Central Sekotong | Very High | High | High | Moderate |
| | West Sekotong | Moderate | High | High | High |
| Lembar | South Lembar | Very High | Very High | Very High | Very High |

Source: Rapid Climate Risk Assessment (2023)

9. Based on data the information system and the climate change vulnerability index (SIDIK) in 2018, there are 3 villages that have vulnerabilities with a fairly vulnerable category (score 3), including Cendimanik Village, West Sekotong and Central Sekotong, while South Lembar is included in the not vulnerable category (score 1). The 2018 SIDIK assessment is in line with the results of the Rapid Climate Risk Assessment. Based on the results of the interview, South Lembar Village has experienced an increase in vulnerability seen from the aspect of the impact of flash floods and the impact of climate change on people's livelihoods with community assessments in the high category (table 1).
10. Not only fishermen, the rob also impacted on farmers because it has inundated the area up to 300 m from the shoreline with an affected people around 350 households. Not only Fishermen, the rob also has an impact on farmers because it has inundated the area up to 300 m from the shoreline with the

affected population of around 350 families. Along the coastal areas of Lembar and Sekotong is agricultural lands with most of them are gardens and dry fields (70%), as well as the rest are rice fields (30%). The total agricultural area of the 6 coastal villages in Lembar and Sekotong is 1,461 ha or 10.5% of the total land area. The impact of tidal flooding (rob) estimated able to inundate about 20% or 292 ha covering settlements and agricultural land in coastal areas (gardens and rice fields). The value of losses suffered by farmers as rob-related reaches total of US\$ 175,000 per year due to rice harvest failure, damaged gardens, and livestock diseases. Losses were mainly suffered by villagers with high vulnerability (Figure 6).



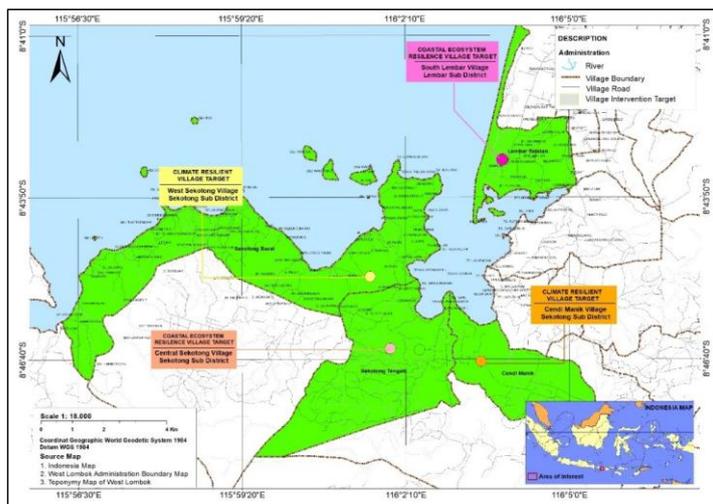


Figure 6. Map of project locations and intervention in West Lombok District

11. Village-based resilience is 'a condition' or 'order in which the community and its government can identify threats-related climate change impacts in their area and organize local resources to reduce vulnerability while increasing capacity to mitigate their climate-related risks. These capabilities will be implemented in village development planning and budgeting, which includes prevention, preparedness, disaster risk reduction, and capacity-building efforts for post-emergency recovery. The leading actor in initiating and implementing this CDRV is the village community, both men and women, by affirming vulnerable and marginalized groups at every activity. Refers to the results of Participatory Rapid Climate Risk Assessment, there are four (4) villages were viable to be project sites i.e. South Lembar, Cendi Manik, Central Sekotong, dan West Sekotong. The selection and determination villages were based on consideration of four (4) key aspects as follows: the condition and value of mangroves, the impact of tidal waves, the functioning of social capital, and the level of climate change-induced risk based on livelihood assets.
12. Village-based local climate resilience institutionalization adopts the mechanism of the Disaster Resilient Villages (Destana²) development as enacted in the Regulation of the Head of the National Disaster Management Authority (BNPB) No. 1/2020 with an emphasis on climate-induced disasters. The idea of Climate Disaster Resilient Villages (CDRV) directs to increase the community and government village's capacity to independently adapt and deal with climate-induced disaster threats and recover quickly from the adverse effects if a climate-induced disaster strikes them. The determination of districts as the project site is based on the Disaster Risk Index (BNPB, 2021). West Lombok was the third regency with the highest-risk index in West Nusa Tenggara Province (see graph 1). Furthermore, the identification of Lembar and Sekotong as targeted districts was based on the Vulnerability and Sensitivity Index (VSI) as published in the Vulnerability Index Data Information System by the Ministry of Environment and Forestry (2018). The VSIs of the two districts were higher than the average VSI of the districts in West Lombok (see graph 2).

² *Desa Tangguh Bencana (Disaster Resilient Villages)*

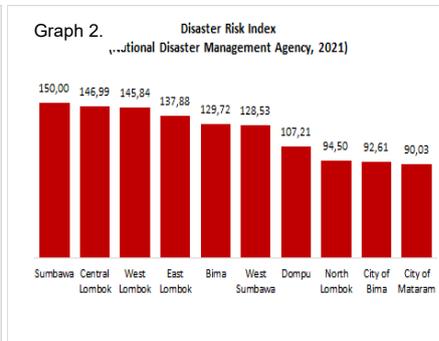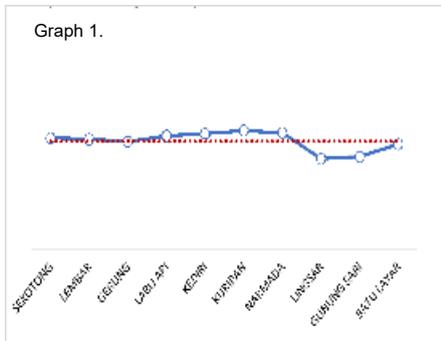

Source: Analyzed from DRI (BNPB, 2021) and SVI (2018)

13. Based on Rapid Climate Risk Assessment (RCRA) conducted in 2023 shows that each village has a different level of vulnerability based on 4 aspects of RCRA. A brief description of these aspects in each village as shown in the following matrix:

Table 2. Description and score level of vulnerability of these aspects in each village

| Villages | Key Aspects | | Score | Total |
|--------------|---|---|---------------|-------|
| South Lembar | The condition of mangroves and their value for the community | Mangroves are one source of income for communities around the coast. They catch crabs, shellfish, and fish under the mangroves and use them for fish farming or silvo-fisheries. Apart from that, they also made the mangrove area a beach tourist attraction, managed by the Tourism Awareness Group in collaboration with Village-Owned Enterprises. The community also relies on their income from mangrove nurseries. They sell seeds to some buyers, including the West Nusa Tenggara Province Watershed Management Agency for the Forest and Land Rehabilitation program. | Very High (5) | 20 |
| | The impact of tidal flood | Robts occur 2-3 times a year triggered by floods with a duration of 1-3 days and water levels reaching 30-60 cm which inundate settlements. The tidal flood impact is categorized as very high with the number of affected heads of families around 495 people who live in two (2) sub-villages. | Very High (5) | |
| | The functioning of capital social | The function of social capital is founded when community members act to mitigate and adapt to tidal flood disasters. In sub-village Cemara, the community constructed embankments independently, led by the local lead of the sub-village. The length reached approximately 2 km, with a height of 0.5 meters and is estimated to have cost US\$ 51,724.1 - 68,965.5 | Very High (5) | |
| | The level of climate change-induced risk based on livelihood assets | In February 2023, floods occurred in 5 (five) sub-villages South Lembar with 529 affected families and one child died because he was hit by wooden debris during the flood. | Very High (5) | |
| Cendi Manik | The condition of mangroves and their value for the community | Cendi Manik Village has quite a large mangrove area and the community uses it for more diverse purposes than other villages: mangrove tourism, shellfish and crab harvesting, silvo-fisheries, ponds, and beach tourism. Village Tourism Awareness Group manages mangrove ecotourism in collaboration with Village-Owned Enterprises. The community also carried out mangrove seeding and they sell seeds to government | Very High (5) | 16 |
| | The impact of tidal flood | Robts occur every month on 2-3 days during the full moon for 3-5 hours. The intensity of the tidal impact is classified as moderate, with water levels of 10-30 cm inundating settlements. There are 2 (two) affected-sub village with a total of 208 heads of families. | Moderate (3) | |

| Villages | Key Aspects | | Score | Total |
|------------------|---|--|---------------|-------|
| | The functioning of capital social | The function of social capital is founded when community members act to mitigate and adapt to tidal flood disasters. The Cendi Manik community is actively working together to repair the tidal embankment | Very High (5) | |
| | The level of climate change-induced risk based on livelihood assets | Risk of loss of milkfish ponds covering an area of approximately 25 hectares with a plot size range between 100 m2 to 400 m2. The level of loss due averages US\$ 517.2 per year. | Moderate (3) | |
| Central Sekotong | The condition of mangroves and their value for the community | The government and community of Central Sekotong village use the mangrove area as an ecotourism spot which is managed by Village Tourism Awareness Group in collaboration with Village-Owned Enterprises. In fact, Central Sekotong is the only village whose people are able to process mangrove seeds into mangrove coffee. | Very High (5) | 18 |
| | The impact of tidal flood | The community explains that the frequency of occurrence and impact of tidal floods has increased in the last 10 years. The distance between the settlement and the surrounding coastline is getting closer. Currently, the residential area is already on the shoreline. If the waves rise as high as 2 meters, sea water enters and floods the house. The tidal flood impact is categorized as high with the number of affected heads of families around 394 people who live in three (3) sub-villages. | High (5) | |
| | The functioning of capital social | The community has exceptional social capital to participate in activities related to the public interest. They will help each other when one of them is experiencing difficulties or when they have interests that must be fought for together. Community members still adhere strongly to social norms for harmony and order. | High (4) | |
| | The level of climate change-induced risk based on livelihood assets | Every time a tidal flood was occurred, fishermen not able to fishing to the sea, which results in lost time earning around 3-5 days a month or 60 days/year for each fisherman. If their average net income is US\$ 2.1-3.4 for every fishing, there is a loss of income of US\$ 124.1-206.9 per year/person | High (4) | |
| West Sekotong | The condition of mangroves and their value for the community | The condition of the mangrove forest is the same as the village of South Lembar, but its use by the community is slightly more diverse such as for tourism purposes, collecting shellfish/crabs, silvofisheries, and beach tourism. | Moderate (3) | 15 |
| | The impact of tidal flood | The frequency of occurrence and impact of tidal floods has increased in the last 10 years. The distance between the settlement and the surrounding coastline is getting closer. Currently, the residential area is already on the shoreline. If the waves rise as high as 2 meters, sea water enters and floods the house. The tidal flood impact is categorized as high with the number of affected heads of families around 429 people who live in two (2) sub-villages. | High (4) | |
| | The functioning of capital social | The community has exceptional social capital to participate in activities related to the public interest. They will help each other when one of them is experiencing difficulties or when they have interests that must be fought for together. Community members still adhere strongly to social norms for harmony and order. | High (4) | |
| | The level of climate change-induced risk based on livelihood assets | Every time a tidal flood was occurred, fishermen not able to fishing to the sea, which results in lost time earning around 3-5 days a month or 60 days/year for each fisherman. If their average net income is US\$ 2.1-3.4 for every fishing, there is a loss of income of US\$ 124.1-206.9 per year/person | High (4) | |

Source: *Rapid Climate Risk Assessment (2023)*

Socio Economic Context

14. Based on Rapid Climate Risk Assessment (2023), the total population of vulnerable villages by tidal flooding is 34,756 people (heavy affected 1,729 people (5%), moderately affected 5,213 people (15%), lightly affected 27,804 people (80%). Most of their income sources are fishermen (50%) and farmers (18%). For farmers, they are land owners, farm laborers, cattle farmers, and artisanal mining. Rice production in coastal areas is around 3-4 tons/ha or smaller than the upstream and middle areas of 4-6 tons/ha (NTB Provincial Agriculture Office, 2019). The low rice production as impact of lack water conditions which are influenced by tides and the intensity of tidal waves. The average tenure of agricultural land is only 0.2-0.5 ha with the total income of farmers around US\$ 600 – 1,014.0 per year including from livestock-raising and artisanal mining.
15. For fishermen, they are small fishermen with small canoes (using paddles) and middle fishermen with motorized canoes (ketinting). The income of fishermen is more uncertain than that of farmers. In normal seawater conditions, fishermen usually go to sea with a range of 15-20 days a month. If the waves are medium and high, the number of days at sea decreases. For small fishermen, they go to sea with an allocation of 6-12 hours. Currently, fishermen's productive days are decreasing. They have productive time between 6-7 months a year and the rest are mostly unemployed (Markum, 2008).

Table 3. Description of coastal community livelihood and estimated income in 6 affected villages by tidal flooding at sub-districts Lembar and Sekotong

| Jobs | Combination of income sources | Estimated Amount of Income (US\$) |
|-----------|---|-----------------------------------|
| Farmer | Land Farming – Livestock Raising | 600.00 |
| | Land Farming – Livestock Raising – Services | 931.00 |
| | Land Farming – Livestock Raising – Artisanal Mining | 1,014.00 |
| Fisherman | Fishing – Land Farming | 848.00 |
| | Fishing – Land Farming – Livestock Raising | 1,262.00 |
| | Fishing – Artisanal Mining | 1,076.00 |

Source: Rapid Climate Risk Assessment (2023)

16. The impact of the tidal flood is the loss of job opportunities for fishermen, the risk of crop failure and crop failure for farmers, damage to garden crops, and disease in livestock. Another impact is the disruption of school activities by reducing children's learning time at school for 2-5 days when the rob occurs, as well as causing various diseases or even triggering epidemics. There are seven (7) diseases that often appear due to tidal flood: leptospirosis, diarrhea, digestive tract diseases, upper respiratory tract infections, typhoid, skin diseases, dengue fever or malaria. Data from the Health Service of West Lombok (2022) has recorded 2,741 diarrhea sufferers in Lembar and Sekotong during 2022. In turn, the negative impact of tidal floods will lead to weak community resilience in the socio-economic livelihoods of affected communities.

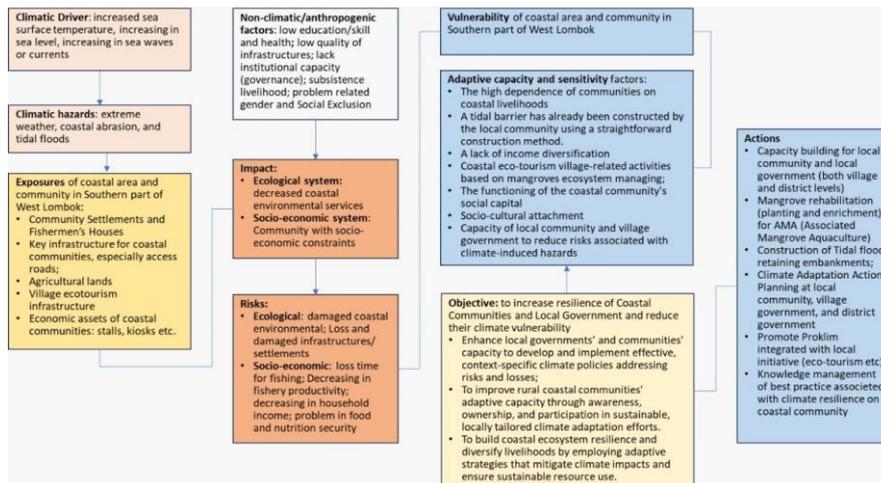


Figure 7. Climate Impact Chain in the coastal area of West Lombok

Project Context

17. Based on the description of the factual conditions above and aligned with the Presidential Regulation (PERPRES) No. 98 of 2021 concerning the Implementation of Carbon Economic Value for the Achievement of National Contribution Targets and Greenhouse Gas Emission Control in National Development, NTB Climate Change Adaptation Action Plan 2019-2023 (BAPPEDA NTB, 2019) and the National Climate Resilience Development Policy 2020-2045 (BAPPENAS, 2020), we argued that this project interventions are needed to respond these. The management of disasters and vulnerabilities in coastal areas has been mandated in the NTB Climate Change Adaptation Action Plan 2019-2023 on the explanations related to the marine sector and small islands (p.100). At least, there are three main issues to be addressed as the root of problem in the targeted-site. *First*, the occurrence of tidal flooding has always been repeated in the last 20 years. This means that efforts to reduce tidal flooding' impacts by various parties have not been effective; *Second*, the tidal flooding has impacted on the weakening of community's livelihoods due to the loss of job opportunities and the decline in productive activities as well as disruption of education and public health aspects; *Third*, repeatedly tidal waves, not only due to natural anomalies induced by climate change, but also the unavailability of adequate infrastructure for supporting it, both naturally and artificially.
18. This proposed project will contribute to the NTB Province's Climate Change Adaptation Action Plan (P-CCAP) for the 2019–2023 period, which aims to increase the adaptive capacity of coastal communities to the impacts of climate change such as sea level rise, coastal abrasion, and hydrometeorological disasters. The proposed activities outlined in this project proposal, such as coastal zone protection, strengthening local institutional capacity, and community-based early warning systems, are therefore aligned with the priority adaptation actions as stipulated in Governor Regulation No. 54 of 2019. Since 2023, the policy direction has continued with the preparation of the Low Carbon and Climate Resilience Development Plan (LCCRDP) for the period 2025–2045, as the latest strategic document that integrates the P-CCAP and the Provincial Greenhouse Gas Emission Reduction Action Plan (P-GGERAP). This project is very relevant to the LCCRDP, especially in coastal and small island management, disaster risk reduction, and strengthening community-based governance. This project also supports the achievement of LCCRDP indicators, such as reducing economic losses due to climate change and protecting coastal ecosystems sustainably, with a participatory, inclusive, and sensitive approach to gender, disability, and social inclusion (GEDSI) issues. In addition, the project will help identify support for LCCRDP's priority sectors and strategies over the medium and long term. It is also aligned with the National Action Plan for Climate Change Adaptation (RAN-API 2023), especially to achieve targets in the coastal and small islands sub-sector, the project plan will contribute to 2 main strategies, namely: a). Stability of coastal and small island communities' lives against the threat of climate change; and b). Improving the environmental quality of coastal areas and small islands.
19. Actually, the Government has been concerned to overcome the tidal flooding disaster through the initiation of villages developing such as Disaster Resilient Villages (DESTANA), Pro-Climate Villages (Proklim), and Tourism Villages. Through this project, facilitation will be carried out Pro-Climate Villages (Proklim) in Central Sekotong Village, West Sekotong and South Lembar. In addition to the project's contribution to the achievement of the national contribution target for climate change adaptation (Proklim), facilitation will also be carried out in 50 villages in West Lombok Regency to be registered as Proklim villages and assistance to become Proklim Villages with Primary status. This is in accordance with the mandate of Presidential Regulation No. 98 of 2021. Disaster management initiatives in four villages in Lembar and Sekotong districts through the determination of village status as shown in the following Table 4.

Table 4. Disaster management initiatives in four villages in Lembar and Sekotong districts through the determination of village status

| District | Name of Village | Disaster Resilient Village (Destana) | Climate Hamlet Program (Proklim) | Tourism Village |
|----------|------------------|--------------------------------------|--------------------------------------|-----------------------------|
| Sekotong | Cendi Manik | √ | √ | √ |
| | Central Sekotong | √ | - | √ |
| | West Sekotong | √ | - | √ |
| Lembar | South Lembar | √ | - | √ |
| | Source | BPBD ³ NTB Province, 2021 | DLHK ⁴ NTB Province, 2022 | West Lombok Regency Website |

³ Regional Disaster Management Authority = Badan Penanggulangan Bencana Daerah (BPBD)

⁴ Environment and Forestry Office = Dinas Lingkungan Hidup dan Kehutanan (DLHK)

20. Absolutely, various determinations of the status of the village can contribute to disaster reduction in the region. However, the fact is that the level of disaster vulnerability in the area has not changed significantly. Thus, it is essential to construct more carefully the efforts of physical and non-physical arrangements related to the efforts to overcome the disaster vulnerability. The urgency is that program interventions will need to be carried out that will ensure that the community is safer from the tidal disaster, the community has an institutionalized adaptation attitude, and the community is supported to have a way of getting around (choices) to create economic and social resilience when the tidal disaster comes unavoidable. In addition, supporting the normalization of the carrying capacity of ecosystems and the environment in coastal areas is vital in strengthening climate adaptation and resilience in the targeted villages.
21. One of the limiting factors in the West Lombok Region in disaster management is the small Regional Budget (APBD⁵). In 2020 the West Lombok APBD amounted to IDR1.9 trillion (West Lombok Regional Regulation No. 03/2020 on the Regency's APBD). Support for the Adaptation Fund (AF) project is highly expected to stimulate the tidal disaster management objectives described above. AF project support can finance the provision of adaptation infrastructure, strengthening community capacity, financing for increasing community income, and strengthening community and village institutions.
22. The management of this project is carried out with the target of focusing on the beneficiary communities that directly impact the disaster. Unlike previous government programs, the government does not focus on disaster management and can only help during disasters. Meanwhile, for regional funding, programs are often not optimal and unsustainable due to constraints on the available funds and changing leadership, resulting in changes in policies, programs, and target focus. So, mentoring is often incomplete. Institutions, policies, and planning at the village level also need to focus on Disaster Risk Reduction. On the other hand, the capacity of village governments and communities related to climate change adaptation is still low because local governments, through previous programs, have not touched the grassroots. Village development planning that focuses on climate change adaptation actions is also expected to be carried out so that funding from villages through the village budget (APBD) can be a source of funding for adaptation programs. Therefore, it is significant that this project be implemented to assist and increase the capacity of village governments and communities by encouraging climate change adaptive village development policies and planning.
23. To reduce the impact of this disaster, the project will use a bottom-up system and, within 2 years, will allow for changes because intensive assistance will be carried out with the same Field Facilitators and will engage with beneficiaries. Funding is also clearer and more focused. This project will make an integrated change from the grassroots to the level of policymakers by paying attention to fairness and equity (inclusive). Consortium members have had successful stories in empowering and helping vulnerable communities to become more resilient and sustainable within 2-3 years in various regions in NTB. This will be the experience in this project that covers the target area. The model of a focused coaching approach followed by the scale-up program has been realized through an intensive project approach like this. The hope is a broader model for community empowerment in 1 Regency and even the province. Project/Programme Objectives:

Project/Programme Objectives

List the main objectives of the project/programme

24. This project aims to:
 1. To enhance local governments and communities' capacity to develop and implement effective, context-specific climate policies addressing risks and losses.
 2. To improve rural coastal communities' adaptive capacity through awareness, ownership, and participation in sustainable, locally tailored climate adaptation efforts.
 3. To build coastal ecosystem resilience and diversify livelihoods by employing adaptive strategies that mitigate climate impacts and ensure sustainable resource use.

Below is the Theory of Change of the Project and alignment of the project objectives with the Adaptation Fund Result Framework at the outcome level as indicated red boxes:

⁵ Regional Budget = *Anggaran Pendapatan dan Belanja Daerah (APBD)*

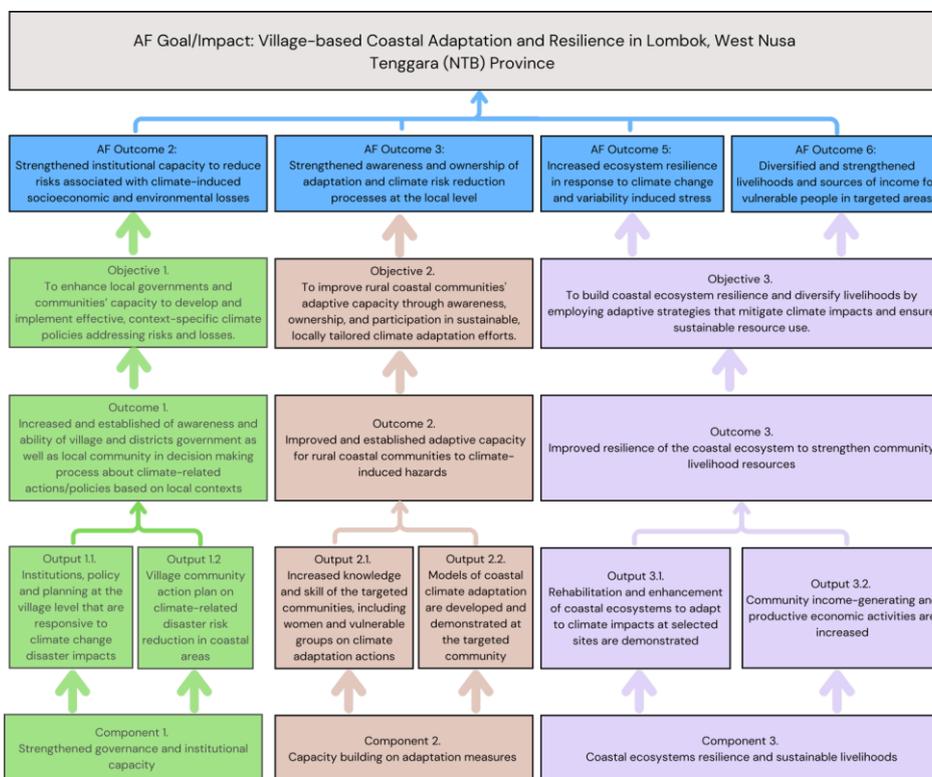


Figure 8. The Theory of Change (TOC)

Project/Programme Components and Financing:

Fill in the table presenting the relationships among project components, activities, expected concrete outputs, and the corresponding budgets. If necessary, please refer to the attached instructions for a detailed description of each term.

For the case of a programme, individual components are likely to refer to specific sub-sets of stakeholders, regions and/or sectors that can be addressed through a set of well-defined interventions / projects.

Table 5. Project/Programme Component and Financing

| Project/Programme Components and Objectives | Expected Concrete Outputs | Expected Outcomes | Amount (US\$) |
|---|---|---|---------------|
| Component 1. Strengthened governance and institutional capacity Objective 1: To enhance local governments and communities' capacity to develop and implement effective, context-specific climate policies addressing risks and losses. | Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | <ul style="list-style-type: none"> Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | 248.981 |
| | Output 1.2 Village community action plan on climate-related disaster risk reduction in coastal areas | | 47.770 |

| Project/Programme Components and Objectives | Expected Concrete Outputs | Expected Outcomes | Amount (US\$) |
|--|---|---|----------------|
| Component 2. Capacity building on adaptation measures Objective 2. To improve rural coastal communities' adaptive capacity through awareness, ownership, and participation in sustainable, locally tailored climate adaptation efforts. | Output 2.1 Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions | <ul style="list-style-type: none"> Improved and established adaptive capacity for rural coastal communities to climate-induced hazards | 134.988 |
| | Output 2.2 Models of coastal climate adaptation are developed and demonstrated at the targeted community | | 125.848 |
| Component 3. Coastal ecosystems resilience and sustainable livelihoods Objective 3. To build coastal ecosystem resilience and diversify livelihoods by employing adaptive strategies that mitigate climate impacts and ensure sustainable resource use. | Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated | <ul style="list-style-type: none"> Improved resilience of the coastal ecosystem to strengthen community livelihood resources | 258.721 |
| | Output 3.2. Community income-generating and productive economic activities are increased | | 42.000 |
| 1. Project/Programme Activities Cost | | | 858.308 |
| 2. Project/Programme Execution cost | | | 62,189 |
| 3. Project/Programme Cycle Management Fee charged by the Implementing Entity (if applicable) | | | 78,242 |
| Amount of Financing Requested | | | 998,739 |

Projected Calendar

Indicate the dates of the following milestones for the proposed project/programme

| Milestones | Expected Dates |
|---|----------------|
| Start of Project/Programme Implementation | November 2025 |
| Mid-term Review (if planned) | November 2026 |
| Project/Programme Closing | October 2027 |
| Terminal Evaluation | December 2027 |

PART II: PROJECT/PROGRAMME JUSTIFICATION

A. Describe the project/programme components, particularly focusing on the concrete adaptation activities of the project, and how these activities contribute to climate resilience. For the case of a programme, show how the combination of individual projects will contribute to the overall increase in resilience

The project has 3 components, namely:

Component 1. Strengthened governance and institutional capacity.

25. This component supports the Project objective: To enhance local governments and communities' capacity to develop and implement effective, context-specific climate policies addressing risks and losses. This will contribute to Project Outcome 1: Increased village governance, policy instruments, and capacity on climate resilience measures, that is aligned with Adaptation Fund Outcome No.2. Strengthened institutional capacity to reduce risks associated with climate-induced socioeconomic and environmental losses.

Component 2. Capacity building on adaptation measures.

26. This component will support the project objective: To improve rural coastal communities' adaptive capacity through awareness, ownership, and participation in sustainable, locally tailored climate adaptation efforts. The Project will contribute to Project outcome: increased rural coastal communities' knowledge and awareness of adaptive measures on climate-induced hazards, that is aligned with Adaptation Fund Outcome No.3. Strengthened awareness and ownership of adaptation and climate risk reduction processes at the local level.

Component 3. Coastal Ecosystems Resilience and Sustainable Livelihoods

27. This component will contribute to the Project objective: To build coastal ecosystem resilience and diversify livelihoods by employing adaptive strategies that mitigate climate impacts and ensure sustainable resource use. This will contribute to Project outcome 3: increased the carrying capacity of coastal ecosystems to serve as a natural defense and livelihood source towards climate impacts and Outcome 4: Increased sources of income of targeted beneficiaries especially the vulnerable communities in coastal areas. These Project outcomes are aligned with the following AF outcome: Outcome 5. Increased ecosystem resilience in response to climate change and variability induced stress and Outcome 6. Diversified and strengthened livelihoods and sources of income for vulnerable people in targeted areas. All components consist of objectives, outputs and activity descriptions as shown in the table 5 below.

Table 6. List of Components, Objectives, Outputs and Activities Description

| | |
|---|---|
| <p>Component 1. Strengthened governance and institutional capacity Objective 1: To enhance local governments and communities' capacity to develop and implement effective, context-specific climate policies addressing risks and losses. Outcome 1: Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts</p> | |
| <p>Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts Activities Description:</p> | <p>1.1.1 Recruitment of village volunteers for climate-induced disaster preparedness; 1.1.2 Participatory climate risk consultation (PCRC) to explore and detail the characteristics and diversity of climate risks at the household level based on socio-economic aspects and GEDSI 1.1.3 Establishment of a village climate disaster preparedness work team from village volunteer members and added with other community components. 1.1.4 Training packages for village government and village climate disaster preparedness work team; 1.1.5 Formulation of local policies on climate resilience (both at village and district levels) 1.1.6 Facilitation for formulating climate disaster-related guidelines/plans/standards (contingency plan, early warning system);</p> |

| |
|---|
| <p>1.1.7 Formulation of policy brief/policy paper to strengthen climate resilience actions or policies at sub-national level</p> <p>1.1.8 Technical assistance on policy making and governance process at subnational level to support climate adaptation measures at village level (including strengthening knowledge management systems)</p> <p>1.1.9 Refreshment and coordination of program on institutionalization of village governance and policy making</p> |
| <p>Output 1.2 Village community action plan on climate-related disaster risk reduction in coastal areas</p> <p>Activities Description</p> <p>1.2.1 Dissemination of PCRC's results to the wider community through presentation of work team representative in workshop for each village</p> <p>1.2.2 Community Action Planning (CAP) on climate resilience through community discussion series and field workshop. Formulation of CAP also consider input and comments in previous workshop regarding PCRC' results</p> <p>1.2.3 Facilitation on integration Community Action Plan (CAP) with the village government's annual plan and budget through discussion series with village government;</p> <p>1.2.4 Facilitation of annual village development planning forum to decide on village development priority programs in the current year including CAP on climate-induced disaster resilience</p> <p>1.2.5 Advocacy of CAP to sub-national government policies both at district and provincial levels through lobbying and discussion series by inviting sub-national government representatives both district and provincial levels.</p> <p>1.2.6 Series of meeting and technical coordination on village CAP development</p> |
| <p>Component 2. Capacity building on adaptation measures</p> <p>Objective 2. To improve rural coastal communities' adaptive capacity through awareness, ownership, and participation in sustainable, locally tailored climate adaptation efforts.</p> <p>Outcome 2. Improved and established adaptive capacity for rural coastal communities to climate-induced hazards</p> |
| <p>Output 2.1 Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions</p> <p>Activities Description</p> <p>2.1.1 Trainings for targeted community on climate adaptation and resilience.</p> <p>2.1.2 Conducting climate field school on adaptation actions on coastal areas conditions (mangrove, land-based farming in coastal, salt farming); in-class for 6 times in each targeted community, and preparing demonstration plots for climate adaptation (field practices).</p> <p>2.1.3 Conducting simulation/exercise to respond to climate induced disaster by testing the contingency plans and early warning system</p> <p>2.1.4 Developing and implementing a learning platform and process for communities related to climate adaptation actions through regular learning forums in each village and cross visits to other areas;</p> <p>2.1.5 Procurement of climate-induced disaster information and documentation systems:</p> <p>2.1.6 Documenting knowledge and best practices of community actions in climate change by producing Stories of Change (SoC) from targeted groups, videos, and book.</p> <p>2.1.7 Review and reflection of learning and program coordination on climate adaptation capacity building.</p> |
| <p>Output 2.2 Models of coastal climate adaptation are developed and demonstrated at the targeted community</p> <p>Activities Description</p> <p>2.2.1 Conducting analyses and model development on climate adaptation in coastal areas to identify, analyze, design of model by hiring the expert team with taking into account PCRA's results and CAP.</p> <p>2.2.2 Procurement of climate-induced adaptation facilities/equipment: construction of fishpond, fish seed, stationaries (silvofishery in mangrove);</p> <p>2.2.3 Demonstration of climate adaptation models of coastal climate adaptation at least 3 models i.e. silvofishery in the mangrove, climate-smart land-based farming in the coastal, and ecotourism services.</p> <p>2.2.4 Documentation of best practices and lessons learned from climate adaptation models in coastal areas by producing practical guidebooks and videos.</p> |

| | |
|---|--|
| | 2.2.5 Sharing best practices and learning, and program coordination on climate adaptation capacity building. |
| Component 3. Coastal ecosystems resilience and sustainable livelihoods Objective 3. To build coastal ecosystem resilience and diversify livelihoods by employing adaptive strategies that mitigate climate impacts and ensure sustainable resource use. Outcome 3: Improved resilience of the coastal ecosystem to strengthen community livelihood resources | |
| | Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated Activities Description 3.1.1 Participatory coastal area spatial plan integrated with climate-induced disaster resilience. 3.1.2 Development of Associated-Mangrove-Aquaculture (AMA) based on research and tourism 3.1.3 Mangrove planting in 20-hectare areas at selected sites; 3.1.4 Facilitation in providing infrastructure packages for climate-disaster risk reduction in mangrove areas; infrastructures: rob-resistant embankments and rob-resistant houses; |
| | Output 3.2. Community income-generating and productive economic activities are increased Activities Description 3.2.1 Value chain development of smallholders' fishery products. 3.2.2 Facilitation of training packages for sustainable smallholder fisheries and livelihood: good practices on fisheries cultivation; diversification of products/processing; marketing. 3.2.3 Facilitation small-scale business licensing and product certification 3.2.4 Procurement of equipment for productive economies and businesses i.e. production machines, packaging machines, etc.; 3.2.5 Technical assistance for developing market-demand commodities and products 3.2.6 Facilitation on access to finance (including venture capital) to support communities' businesses by developing network or collaboration with banks or private sectors. 3.2.7 Review best practices and lesson learned on alternative livelihood improvement |

28. Based on activity 1.1.2. Participatory climate risk consultation will be conducted to consult the findings of the climate risk analysis with the relevant communities and further explore the characteristics of climate disasters impacting households. This activity supports community action plans involving village governments and community groups so that implementing Community Resilience Improvement Activities in dealing with weather uncertainty for their businesses, livelihoods, and families will be carried out appropriately. This activity is significant because the risks that occur during the activity will always be identified and discussed regularly for project evaluation.
29. Government programs that have entered the target village are disaster resilient, climate, and Tourism Village. In carrying out the disaster resilient program, the district government has set 4 target villages as disaster resilient villages and established a Disaster Risk Reduction forum and village alert team as a forum to coordinate disaster risk reduction efforts at the village level. However, the West Lombok regency government has not maximized these efforts because of the many villages that must be accompanied and the limited budget. In addition, the determination of The Climate Village Programme Village is still restricted to the registration process, verification of activities, and determination as a Climate Village Programme village without intensive assistance to strengthen knowledge and slow down the replication of the program. On the other hand, the Tourism Village program has been established in 4 villages and infrastructure development such as photo spots, mangrove tracking, and construction of merchant stalls. However, the program implemented by the government still requires support; for example, after the disaster-resilient village was formed, it was not equipped with knowledge, institutional and infrastructure strengthening. On the other hand, the Climate Village program still needs to strengthen expertise and institutions because, after the determination process as a climate village, assistance is required to make the village into the primary, intermediate and main categories. In addition, the tourism village set by the government only supports infrastructure and does not prepare human resources with skills in tourism management. Therefore, this project will complement and further strengthen the government's program because it focuses on disaster risk management efforts through strengthening village-level disaster preparedness work teams, training, formulation of local climate resilience policies and technical assistance for Policy and governance development that supports climate change adaptation at the village level. This will be supported by a team of village volunteers who are local community members. In addition, to support and strengthen government initiatives, this project will assist village governments in facilitating community action planning on climate resilience and

advocating village government policies for mitigation with the priority of developing villages resistant to climate disasters. With output 1.1. and 1.2. above all, this project will significantly help the community strengthen and realize government programs and initiatives.

30. In preparing the proposal, the proposed activities have been through an in-depth study process through the PCRC and gender analysis sourced from interviews with FGDs and proposals from the community. Based on the study, activities have been identified as proposed in outputs 3.2 and 2.2. Therefore, the activities contained in output 2.2. and 3.2. As proposed the project is just that, and no other additional activities. In addition, this project will produce micro, small, and medium enterprises, especially for women, youth, and people with disabilities, to be involved in producing products with market reach and significant value addition. The results of our study show that this group of women, youth, and disability are widely involved in Micro, Small, and medium enterprises. Activities will include product training and business management, mentoring products and business management, and assistance tools and materials. This assistance includes supervision and legality of the product to penetrate a broader market. To improve the results and participation of target groups, the project will ensure that social capital (networks and trust) in the development of micro, small, and medium enterprises will be further strengthened to facilitate business expansion and increase the income of the beneficiary groups. One of the breakthroughs that will be made is to involve MSMEs who have been successful with their business and marketing networks and are concerned about empowering the community's economy in this project. Their experience will be used to bring these target communities into the network of these advanced SMEs because our resources are sufficient for this implementation.
31. Developing various processed products based on marine fish and agricultural products focuses on sustainably managing raw materials, using methods that minimize negative environmental impacts. Some examples of processed marine fish products include shredded fish, fish crackers, or fish nuggets without the use of preservatives (meet the standards of the Food and Drug Administration/BPOM). In addition to fish-based products, agricultural products can also be processed into vegetable chips, cassava, sweet potatoes, and corn without the addition of chemical preservatives. The necessary infrastructure includes providing raw material processing equipment/production machinery and environmentally friendly product packaging to support the development of processed products. This is done to produce hygienic, healthy food standards-compliant products that are marketable to consumers.
32. The sustainable livelihoods (SL) approach is a framework of this proposed project to ensure the achievement of climate resilience by considering the potential and diversity of local community livelihood sources in the coastal areas of West Lombok. Refers to the SL approach, it can be described that individuals, households, or communities usually rely on various livelihood sources that are owned and can be accessed and controlled to sustain their lives. These livelihood resources are constructed into five assets: human, natural/environmental, physical/ infrastructures socio cultural, and economic. Ownership, access, and control over livelihood resources are unequally distributed and often modified by social roles and social relation patterns (such as gender, economic class, age, ethnicity, religion, and social position). All livelihood resources have the potential to be lost and damaged if affected by a disaster or climate crisis. The ability of individuals, families, or communities to maintain their existence will be disrupted if one or more livelihood assets are lost or damaged, especially for vulnerable or marginalized groups. Coastal communities live in prone areas and are affected by climate variability or extreme weather. Most of them relied on household incomes from unadaptable livelihood sources due to their high vulnerability to the negative impacts of climate change. Therefore, one of the main components of this proposed project is to improve coastal community livelihood resources in West Lombok to be more adaptive and resilient under climate change stresses by assessing community risks, vulnerabilities, and capacities using a sustainable livelihood approach.
33. Improving the quality of coastal ecosystems is one of the key elements to taking account in the development of village-based climate resilience institutionalization mechanisms regarding to its existence as a land-scape (natural resources) and community's life-scape (socioeconomic-related aspects). This argument is based on the objective fact that damaged coastal ecosystems due to various pressures, both natural-factors and man-made, will further exacerbate to vulnerability situation of the environment and humans to tidal flooding threats when sea level rise occurs. The measures to improve ecosystem quality will begin with the formulation of coastal areas' spatial plans through consultation and discussion with the community which will be integrated with deliverable results of previous climate risk analysis (including vulnerability and capacity assessment) under tidal flooding hazard. This participatory coastal area spatial plan includes agreements and determination of protection and cultivation zones. Within this component, the project will also facilitate demonstration activities on coastal restoration and rehabilitation through mangrove planting as an effort to reduce vulnerability to tidal threats while

rehabilitating the mangrove ecosystems that function as potential sources for livelihood activities so the community becomes more adaptive and resilient to climate change impacts. In addition, mangrove restoration and rehabilitation are an innovative approach for community livelihood strategy that can be implemented under local agro-ecological. In the designed project activities, some models of coastal community livelihood diversity that will be intervened in parallel with mangrove restoration and rehabilitation are climate-smart coastal community agriculture; coastal ecotourism; processing fishery, and farming products for women's groups. In addition, a tidal flood or an abrasion barrier building will be constructed.

B. Describe how the project/programme provides economic, social and environmental benefits, with particular reference to the most vulnerable communities, and vulnerable groups within communities, including gender considerations. Describe how the project/programme will avoid or mitigate negative impacts, in compliance with the Environmental and Social Policy and Gender Policy of the Adaptation Fund

Economic, Social, and Environmental Benefits

1. Economic and Social Benefits

34. Economically, this project directly impacts the livelihoods of coastal communities through a 10-15 revenue increase in the next 5 years from income sources that are more diverse, adaptive, and resilient to climate change stressors based on optimizing local coastal potential. The range of fishers' income is USD 450-850 per year (small fishers) and USD 900-1,200 million per year (middle fishers). Meanwhile, the farmer's income is USD 600-1,014 per year. The following is detail of targeted increasing income for each affected jobs by this project:

Table 7. Targeted Increasing Income each Affected-Jobs by this Project (in next 5 years)

| Source of Incomes | Briefly Description | Average of Income per year (USD) | Intervention | Estimation of Income (USD) |
|--------------------------------|---|----------------------------------|---|----------------------------|
| Fishing | <ul style="list-style-type: none"> The average fish catch is 3-5 kg per day with a selling price of USD 6.2-10.3 and the average number of days at sea is 20 days/month. Catch crabs and shellfish found in the area mangroves almost every day for both men (crab catchers) and women (shellfish catchers). The average income is USD 2.1 – 3.4 per during 20 days / month | 2,648.28 | <ul style="list-style-type: none"> Mangrove rehabilitation Increasing capacity for fish processing Silvo-fishery | 2,980,0 |
| Farming | <ul style="list-style-type: none"> Dry land farmers with an average land ownership of 0.5 ha. Two planting seasons (1 planting season for rice and the other for secondary crops and vegetables. Rice yields are 1.5 - 2 tons/ha for own consumption. Likewise for secondary crops and vegetables. | 2,234.5 | <ul style="list-style-type: none"> climate-smart coastal community agriculture; Increasing capacity for farming products processing | 2,513.4 |
| Small Micro Enterprises (SMEs) | <ul style="list-style-type: none"> Selling in small kiosks/home stalls and around tourist locations (basic necessities, snacks, processed products, food and drinks) In the week end, sales volume reached 3-5 times rather than normal days. Normal daily income ranges from USD 5.2 – 6.9 100,000, and at peak times reaches USD 20.7/day. | 1,717.24 | <ul style="list-style-type: none"> coastal ecotourism processing farming products for women's groups | 1,931.9 |
| Fish Ponds | <ul style="list-style-type: none"> Milkfish and crab ponds are managed by local communities with an area of around 100 m2 | 1,241.4 | <ul style="list-style-type: none"> Wall retaining tidal flood | 1,396.6 |
| Services in Ecotourism areas | <ul style="list-style-type: none"> Ecotourism service provider | 579,31 | <ul style="list-style-type: none"> Coastal ecotourism | 651,72 |

35. The total targeted beneficiaries of the project are **1,729 persons (1,119 men and 610 women)**, distributed in **four (4) villages** in Sekotong and Lembar sub-districts. The sub-districts are included in the vulnerable coastal areas to adverse impacts of climate change as shown in the following table:

Table 8. Targeted Beneficiaries of the Project

| Sub-District | Village | Population | | | Targeted Beneficiaries (5 % of total) | Distribution of Targeted Beneficiaries | |
|--------------|------------------|---------------|---------------|---------------|---------------------------------------|--|------------|
| | | Men | Women | Total | | Man | Women |
| Sekotong | West Sekotong | 4,055 | 4,736 | 8,791 | 440 | 290 | 150 |
| | Central Sekotong | 4,664 | 4,699 | 9,363 | 468 | 308 | 160 |
| | Cendi Manik | 2,831 | 2,868 | 5,699 | 285 | 185 | 100 |
| Lembar | South Lembar | 5,436 | 5,287 | 10,723 | 536 | 336 | 200 |
| TOTAL | | 16,986 | 17,590 | 34,756 | 1.729 | 1,119 | 610 |

36. In determining the number of beneficiaries, this project provides the broadest possible access to health to all citizens of the community, both men, women, youth, and disabilities. However, realistically and not too ambitious, it is necessary to consider the sociocultural factors of the target community. The research results show that men are the holders of the public role of the family, and women dominate the domestic and the role of supporting additional family income. In this project, we will gradually increase women's involvement to avoid sociocultural pressure on vulnerable groups (women) if we push too ambitiously for equality in the number of men and women participating. The Indonesian government alone targets women's involvement in the 2020-2024 National Medium-Term Development Plan (RPJMN) in various aspects of development to be 8.74% by 2024. Therefore, the target of 30% involvement of women is realistic and optimistic in this regard.
37. Direct beneficiaries are not calculated based on the resident population (as in Table 7 column 3) but on residents' livelihoods affected by ROB flood. According to the results of PCRA, four livelihoods are affected: farmers, fishermen, breeders, and traders. The results of the Gender assessment study showed that the three livelihoods affected were dominated by men (annex 3, Table 9) and small business traders (MSMEs) were carried out by women. Therefore, the implementation of this project is very realistic if the proportion of men and women is 70%:30%. Activities in the form of training packages for aquaculture and agriculture are more emphasized on male beneficiaries. So far, the activities carried out by women are processing raw materials and marketing (as traders). Work as a farmer, fisherman or rancher is considered a job that is classified as heavy so that men and women dominate it and play more roles in domestic affairs, helping agricultural and fishing activities that do not require heavy labour and processing of farm products/fish catches to be marketed around the village as an overview of project beneficiaries based on livelihood is presented in Table 8.

Table 9. Direct beneficiaries of livelihood-based projects

| Beneficiaries | Village | | | | Total (People) |
|-------------------|----------------|-----------------|-------------|----------------|----------------|
| | Sekotong Barat | Sekotong Tengah | Candi Manik | Lembar Selatan | |
| Farmer Groups | 180 | 164 | 75 | 99 | 518 |
| Fishing Group | 140 | 125 | 90 | 250 | 605 |
| Group Of Breeders | 40 | 60 | 50 | 22 | 172 |
| Merchant Group | 80 | 119 | 70 | 165 | 434 |
| Total | 440 | 468 | 285 | 536 | 1.729 |

38. The social benefit of this project is improving local governance on climate-induced disaster risk management in coastal areas by ensuring the social participation of representatives of all community groups without exception, both men and women especially the vulnerable groups (poor people, persons with disabilities, etc.) to participate, engage, and voice out their aspirations, advice, suggestions, and expectations regarding climate adaptation and resilience actions align with climate justice principles by fulfilling their rights especially those who are affected by climate change negative impacts. It is acknowledged that the impact of climate-related crises has been distributed unfairly across communities as a result of differences in social status, gender, income, etc. Likewise in coastal communities of West Lombok, especially in project location villages.

2. Environmental Benefits

39. This project will improve the environment around the areas affected by tidal floods, both in natural and artificial environments, and enable the development of environmentally friendly products. The project will improve the natural environment by rehabilitating and planting mangroves in coastal areas covering 20 hectares (intensively) and 20 hectares (enriching) to build environmental resilience in resisting tidal waves and flood currents.
40. Another ecological improvement is the availability of support in constructing infrastructures or facilities of tidal flood retaining embankments along 2 Km (South Lembar), 350 meters (Central Sekotong), and

boat mooring spots (25 points) which will be constructed on the coastline adjacent to settlement areas in order to minimize abrasion/tidal flood damage. The other benefit of environmental restoration is to development of various processed products by prioritizing fewer chemicals or organic products. In addition, mangrove rehabilitation also provides opportunities for village governments to develop coastal ecotourism areas resilient to climate-induced disasters.



Figure 7. Existing condition of embankments in South Lembar village

3. Gender and Vulnerable Groups Benefits

41. In the context of gender and social inclusion (GESI), the expected benefit of this project is to increase community involvement, both men and women, especially vulnerable and marginalized groups (including a person with disabilities), in discussing and planning actions related to climate resilience and adaptation. In addition, the project will implement gender and social inclusion mainstreaming by providing 'space' for poor people, both men and women, as well as other vulnerable groups as right holders to claim their rights in access, participation, and as beneficiaries of this project with expected-impact, is support on the sustainability of resilience their livelihoods. This project requires the involvement of at least 30% of women's representatives in every activity. RCRA results (2023) showed that tidal floods have disrupted the livelihood activities both of men and women, which further implications to cut the cash flow of household income. For women, local disasters increase their burden related to domestic work due to the loss of sources of livelihood (the washing away of salt ponds and the destruction of mangroves as habitats for shellfish, shrimp, and crabs). Women must also work hard to find ways/strategies to meet their family's consumption needs when their main sources of livelihood are threatened by disaster.
42. Gender statistics of West Lombok Regency (2022) recorded the number of Women Headed Household (WHH) around 11.9 percent compared to Men Headed Household (MHH) of 88.11 percent. Some causes of women as head household are as follows: divorce because their husband has died, divorce because their husband lives, as the second or third wife of a polygamous husband, the husband under condition impossible to earn needs. RCRA revealed that WHH plays the central role as breadwinner for family members from various sources of income. They rear the family's livestock and control sales decisions and price determination. If a tidal flood occurs, WHH evacuates their livestock to a safe location without waiting for volunteers to help them. In the village of Cendi Manik, there are women heads of families who are exemplary salt entrepreneurs and sell their harvested salt through cooperatives. They received the assistance of salt production equipment because they were active as cooperative members. In the village of South Lembar, salt ponds can no longer be produced due to continuous tidal attacks. The strategy of WHH is to buy coarse salt from other places and process it into acceptable salt for sale. Besides that, they also sell fish at the local market or go around to houses in the village.
43. Gender roles are relatively less recognized as determining factors in taking actions and decision-making related to climate change adaptation at the household level. Men have played a vital role as the primary breadwinner, and they are responsible for ensuring family income stability. Meanwhile, women are income managers and have a supporting role as the second line of income seekers by selling in local stalls and markets. In disaster situations or crisis events, women play an essential role as the mainstay of fulfilling the family's economic needs. They have wider access to non-bank credit institutions rather than men. Women have control over the use of family assets and savings, such as selling small livestock, pawning goods, borrowing money or rice from neighbors or relatives, and looking for additional work

(such as seeking and collecting shellfish). In addition, they also have the crucial task of ensuring adequate food and nutritional security for family members daily. Patterns of family consumption do not change even though they are experiencing crisis situations due to disasters or when the head of the family (male) cannot generate income.

Table 10. Matrix of segregation gender roles based on various activities in each type of work at the site project

| Activities | Level of Dominance Gender-based Role | | Description |
|--|--------------------------------------|---------------|--|
| | ♂ | ♀ | |
| Fisheries | | | |
| Fishing in the sea | Very High (5) | Very Low (1) | Fishing in the sea is generally worked by men and there are also several men with disabilities as fishermen |
| Collecting shellfish, shrimp, crabs | Very Low (1) | Very High (5) | Women generally collect shellfish, shrimp or other pond products when the sea water is low. These products are sold when their catch is considered large enough (minimum 1 kg). |
| Selling fish or others | Very Low (1) | Very High (5) | The identified marketing channels for seafood are selling to local markets, through collectors/retailers, and directly to consumers. |
| Crop cultivation and raising livestock | | | |
| Raising cattle and goat | High (4) | Medium (3) | <ul style="list-style-type: none"> ▪ Livestock is considered as a family savings ▪ There are slight variations in the roles of men and women in raising livestock; ▪ Generally, men are dominant in raising and selling livestock. Meanwhile, women tend to help when their husbands are at sea or not at home. ▪ In the case of Women-Headed Households, they play a major role in caring for the family's livestock |
| Raising poultry (chicken, duck etc) | Low (2) | High (4) | |
| Sale of large livestock (cattle/goat) or poultry (chicken, duck etc) | High (4) | High (4) | Women-headed households also make decisions for sale their cattle. |
| Determining livestock selling prices | High (4) | High (4) | <ul style="list-style-type: none"> ▪ In livestock sales, the selling price is determined based on mutual agreement between the husband and his wife ▪ Livestock are usually sold when the family needs cash, especially when a crisis occurs (including a disaster) because there is no family income from their main or side jobs. ▪ Large livestock (such as cattle or goats) are sold when they need money for large expenses (child's marriage or the cost of the child's education to a higher level). Meanwhile, small livestock/poultry will be sold when the family does not have income for daily consumption needs. |
| Crop cultivation | High (4) | Medium (3) | In crop farming, men and women play a role in cultivation from land preparation to harvesting and selling yields. For sales, men usually meet and negotiate with buyers (collectors). Meanwhile, women play a role in managing income from selling harvests to meet family needs |
| Small and Medium Enterprises (SMEs) and Ecotourism Activities | | | |
| Coarse salt farming | High (4) | Low (2) | |
| Artisanal mining | Very High (5) | None | Be workers (laborers) in artisanal mining are generally men in the sites' location. Meanwhile, there are no women participated due to the mine spots are remote and difficult to access People consider this job to be a source of income for |

| Activities | Level of Dominance Gender-based Role | | Description |
|--|--------------------------------------|---------------|---|
| | ♂ | ♀ | |
| | | | fulfilling daily needs when the main job's income is inadequate |
| Refined salt farming | Very Low (1) | Very High (5) | |
| Small traders, mobile sellers, or retail sellers in the local market | Very Low (1) | Very High (5) | |
| Online sales | Medium (3) | Medium (3) | Online traders are generally young men and women |
| Culinary | Low (2) | High (4) | |
| Laundry | Very Low (1) | Medium (3) | |
| Hand crafts | Very Low (1) | Medium (3) | |
| Small traders in tourism areas | Medium (3) | Medium (3) | Disabled people and youth also get access to these jobs |

44. Regarding current climate change adaptation-related actions, vulnerable communities and other marginalized groups (men and women) in almost all study areas still need to be fully aware that they must adapt to uncertain climate variability and change impact. These rights holders complain that the government's measures to solve their problems have not been optimal, from the preparedness stage, emergency response when a disaster occurs, and post-disaster recovery. Affected people by tidal floods often do not receive services to fulfill their daily consumption needs because their economic activities are stopped due to tidal surges. This situation repeats in every year. There is an exciting story amidst this situation. The lack of duty-bearers attention encouraged local leaders in one of the hamlets affected by the tidal flood to collect community funds independently to construct a tidal surge-resisting to prevent flooding into settlement areas. Regarding gender and social inclusion, the issue is that women, people with disabilities, and other vulnerable groups are increasingly vulnerable to the negative impacts of climate change due to their low level of knowledge and skills to adapt when government efforts are not directed at improving their adaptive capacity.

4. Mainstreaming gender in project

45. Considering the importance of women's roles in various aspects, especially in development issues, this project will use a gender perspective from planning to program implementation. The aim is to mainstream gender, especially in the management of coastal areas. By applying the principle of gender inclusivity, this project sees the role of women as crucial and potential parties to maintain the sustainability of coastal areas through pilot and productive businesses.
46. Women are the most vulnerable social group and are affected by *rob*. When the disaster occurred, women's activities (productive sector including salt making, activities in the fields, making processed food from marine products, mangrove nurseries, buying and selling fish catches, and small traders at tourist village locations) were affected and even stopped being productive. Women tend to do domestic work; while men are more involved in securing the environment and their homes as *the rob* occurs.
47. In addition, there is a high gap between women's and men's roles in managing coastal areas prone to tidal floods, according to previous research. The increased gap occurs in two aspects: institutional governance and governance of the coastal regions and the environment. However, women have a prominent role in business governance. Accordingly, this project will try to provide enabling environment and opportunities that women can be involved in both aspects. In the institutional aspect, women must be involved proportionally in meetings, discussions, and capacity-building activities. In regional governance, on the other hand, women are given opportunities in various aspects of the project.
48. Based on the results of consultations conducted on August 12, 2023 (report attached to annexe 6) and the results of the study a gender action plan to strengthen responsive actions is carried out by increasing the capacity and representation of women in decisions. The actions taken are 1) project implementers know the role of men, women, and marginal groups at the household scale and their role in community life to ensure that beneficiaries can present gender representation fairly and inclusively 2) project implementers understand access to resources by reviewing differences in access to livelihoods, education, health, and access to other resources so that equal access and economic empowerment,

namely ensuring women and men have equal access to project benefits, and supporting women's roles in economic activities. In order to monitor the gender-responsive action using indicators: 1) the participation of 30% of women in the involvement includes knowledge improvement training, regular group meetings, economic development training, and other project activities 2). gender-segregated data collection that ensures project data includes information based on gender, 3) conduct independent monitoring involving women's organizations to monitor the implementation of gender action, and periodic reviews with periodic evaluations to assess the success of gender Action Plans.

C. Describe or provide an analysis of the cost-effectiveness of the proposed project/ programme

49. The tidal flood caused fishermen can't go to sea for fishing because they prioritized keep the safety of their families. There is a loss of time at sea of 3-5 days for each fisherman in a month or as much as 60 days/year. If their average net income per trip to sea is USD 2.0-3.3, they lose an income of USD 120.0-200.0 year/person. Rob also has an impact on reducing the work motivation of farmers and other service providers (builders, gold diggers, etc.). If the average wage of farmers or construction workers or gold-diggers is USD 4,7/day, then they lose income of up to USD 280.0 per year/person. Losses of rice fields due to flooding by sea water up to 50% of total production. If the average land production capacity is 2 tons/ha at a price of USD 140.0/ha, then the potential loss is USD 140.0/ha per year (lowland rice) and USD 140.0/ha per year (upland rice). Losses from milkfish ponds and salt ponds affected approximately 70 ha of ponds with plot sizes ranging from 10x10 m² to 20x20 m² and investment between USD 666.7-1,333.3/pond. If a flood occurs, production failure can reach 50-100% due to fish being washed away of the pond. The value of economic losses due to flooding for pond farmers reaches USD 333.3-666.7/year.
50. From the cost-effectiveness analysis, AF support is effective and feasible to reduce the negative impacts of tidal flooding on community livelihoods from environmental, social, and economic aspects. With a project value of USD 998,739 and an initial cost of USD 25,000 (total USD 1,023,739 or USD 1.02 million), the benefit value for the next 10 years reaches USD 1.67 million or a B/C ratio of 1.62 (B/C ratio value > 1 or considered feasible). If the total value of losses and damage from tidal flooding (physical, socio-economic, environmental) is calculated at USD 14.6 million, the benefit value of this project activity will contribute 11% to reducing potential losses in the next 10 years. The negative impacts of tidal flooding on community livelihoods can be reduced more quickly if financial support is available from other parties (multilevel government, NGOs, and community self-help).

Tabel 11. The 1st Intervention: Associated Mangrove Aquaculture (AMA)

| Component | Silvofishery Compound Model | Proposed Project |
|-----------------|--|---|
| Intervention | 20 hectares with the compound model | 20 hectares (intensively planting) and AMA Development |
| Cost | USD 133.333 | USD 90.000 |
| Approach Metode | Construction: Design for compound model silvofishery (edge or center) requires the construction of embankments with a minimum width of 100 cm. Water inlet and outlet channels are required, where the current condition must be reconstructed with major improvements. | Construction: Design for AMA with the construction of a 50 cm wide embankment and water channel, the current condition only requires minor repairs. |
| | Costs: Production inputs for aquaculture are higher due to the use of commercial feed, probiotic chemicals, procurement of pumps and piping. Routine costs due to water replacement using mechanical pumps | Costs: Input for cultivation is lower because in addition to commercial feed, it is also supported by natural feed from the mangrove ecosystem. Operational costs for mechanical pumps are lower because they utilize the tidal circulation of sea water |
| | Land Maintenance: Requires intensive maintenance (costs for regular mangrove pruning and root reduction) | Land Maintenance: Routine maintenance is not required because the pond and mangrove zones are separate. Cultivation does not sacrifice ecological sustainability, because mangroves become a coastal belt (in front of the cultivation zone) |
| | Livelihoods: Production with intensive system 5.1 tons/ha/year (per cycle production 1.7 tons/ha, stocking density 5,000-7,000 heads/ha). Business income reaches USD 4,080/ha/year. | Livelihoods: AMA produces 6 tons/ha (per cycle production 2 tons/ha, stocking density 5,000-7,000 fish/ha). The profit from cultivation reaches USD 4,800/ha/year. |
| | Sustainability: Procurement of mangrove seedlings (5,000 seedlings/ha) with the type | Sustainability: AMA uses natural propagules, minimal seed costs (using |

Commented [GU1]: butuh penjelasan kenapa biaya yang diusulkan bisa lebih murah

Commented [SM2R1]: cover area apa yang akan di intervensi ?


| Component | Silvofishery Compound Model | Proposed Project |
|-----------------------------|---|---|
| | desired by the land owner. Sustainability of silvofishery tends to be vulnerable. Less support for environmental conservation. | community-cultivated seeds). Supports the sustainability of silvofishery. Environmental restoration and long-term income. Natural filtration (absorbs organic waste (N, P) from cultivation. Reduces land subsidence and maintains the coastline. |
| Impact on coastal ecosystem | <ul style="list-style-type: none"> Mangrove cover in the pond area is increasing due to mangrove planting in the pond. Coastal biodiversity is increasing. | <ul style="list-style-type: none"> The 40-hectare mangrove forest area was rehabilitated by planting and enrichment |
| Economic Impact | <ul style="list-style-type: none"> The complex system will impact declining pond productivity because mangrove planting in the middle and edge of the pond area will reduce cultivated land. Of course, this will impact declining farm yields and decrease farmer income. | <ul style="list-style-type: none"> The value of economic benefit is around USD 67,126.4 per year and the Break Event Point (BEP) will be achieved in the 2nd year. In the 3rd year, beneficiaries will receive economic benefits. |
| Others | <ul style="list-style-type: none"> Farmers disagree with the silvo-fishery model kompanion because of farmers' difficulties in the ponds' maintenance. Rhizophora, Avicennia, and Sonneratia roots grow very quickly, causing farmers' ponds to be covered with thorn roots and breathing roots. The impact on aquaculture is the difficulty of catching milkfish, shrimp, or other fish farming. | <ul style="list-style-type: none"> Increasing community resilience to the impacts of climate change through providing alternative sources of livelihoods and improving mangrove cover |

Tabel 12. The 2nd Intervention: Embankments Improvement

| Component | Seawall Revetment | Proposed Project |
|-----------------------------|---|---|
| Coverage areas | Improvement of the tidal embankment (2 km), using concrete and stonework techniques, carried out by commercial contractor with labor and materials from outside the village. | Increasing the tidal embankment (2 km) in Lembar Selatan Village, building a tidal embankment (350 meters) in Sekotong Tengah Village, 25 boat mooring points. |
| Cost | Estimated cost up to USD 800,000 | USD 155,211 |
| Approach Method | Preparation: The contractor needs to conduct a technical survey regarding environmental conditions to create a construction design. | Preparation: The community understands the environmental conditions around them better, so they can ensure construction that meets their needs. |
| | Material: Concrete panel material (precast) + concrete reinforcement (concrete material is molded and formed in the factory and produced in a controlled manner). Utilization of additional materials in the form of geotextiles. | Material: Materials are sourced locally, and using the right concrete mix to ensure quality. Boat mooring with cast concrete (Cast in situ) or poured concrete on site. |
| | Construction Techniques: Installation with heavy equipment. | Construction Techniques: River stone foundation and reinforcing iron. |
| | Management: Construction management using contractors (third parties). | Management: Construction is carried out by the community supervised by technicians. |
| Impact on coastal ecosystem | Piling up rocks for coastal embankments will disrupt the balance of the ecosystem. This can disrupt the habitat of mangroves and other biota, and air pollution due to the transportation of materials. | No negative impact to the coastal area. The coastal ecosystem is maintained as a comfortable habitat for marine flora and fauna. In addition, the function of the beach can also be developed as an ecotourism spot or entertainment site for the community |
| Economic Impact | With an investment of USD 800,000, there is no calculation of economic impact. However, it is estimated that the economic impact is similar to the proposed project | With an investment of USD 146,577.4, the value of economic benefits will be received about USD 1.34 million in the next 10 years (based on present value with a discounted factor of 10 %) |
| Others | Transporting large quantities of stone will require heavy equipment. In addition, due to the use of a large amount of stone, it will result in damage to the ecosystem in the stone exploitation area. In addition, the improvement of embankments with perched will also make it difficult for fishermen to access their boats | Overcome crop failure and livestock death; address public health problems; overcome settlement damages; prevent loss of jobs for fishermen, small enterprises of ecotourism, and others services. |

Layout Compound


Layout 1. Compound Model

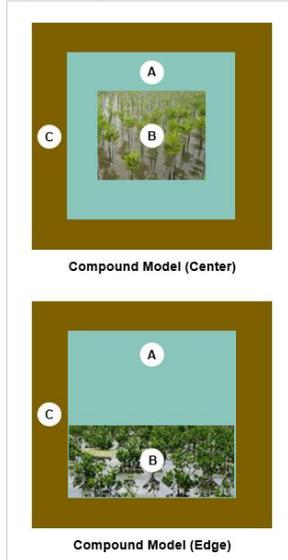


Side View Design
 A = Cultivation Pond
 B = Mangrove Planting Area
 C = Embankment
 (Source: BSMA Marvel Project)

Layout AMA

Layout 2. Single Pond

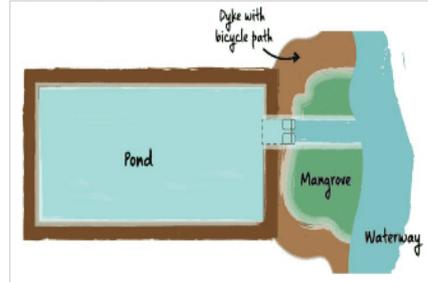

Layout 3. Complex AMA System for Better Water Management

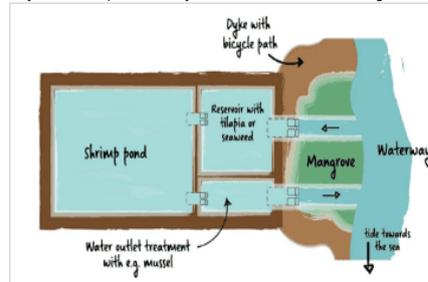

Side View Design
 HAT = Highest Astronomical Tide;
 HHWS = Highest High-Water Spring;
 MHWS = Mean High-Water Spring;
 MSL = Mean Sea Level;
 MLWS = Mean Low Water Spring;
 LLWS = Lowest Low Water Spring;
 LAT = Lowest Astronomical Tide
 (Source: Technical Guideline #4 Associated Mangrove Aquaculture)

51. The proposed project is considered to provide benefits toward the environmental, social, and economic resilience for the community livelihoods of 1,729 persons in the 4 (four) villages as targeted sites. From the project value of USD 998,739, the beneficiaries will receive financing of USD 577,64 per person or USD 249,685 per village. Then, the value of obtained benefits in the next 10 years is USD 963.94 per individual or USD 416,665.21 per village. On the other hand, this project also provides multiplier effects, including preserving coastal ecosystems, increasing public knowledge, maintaining regional food security, increasing employment opportunities, and developing tourist areas.
52. Potential sources of funding support to finance project activities and project sustainability will be supported from village funds of USD 21.429, community self-help USD 42.857, budget from the Regional Budget through several technical OPDs including the Public Works Service, the Tourism Office, the Regional Disaster Management Agency amounting IDR 2 billion (USD 142.857). Other potential support from the private sector includes hotels, homestays and Indonesian shipping companies (PELINDO) in the amount of IDR 1 billion (USD 71.429).
53. The project intervention is cost effective, as it includes continuous education, the development of community action plan, and policy related to climate change, adaptation, and livelihoods (topics that are often not well understood by local communities). Providing this information and empowering communities is essential for building long term knowledge and supporting effective adaptation. These efforts will also help reduce the impact of climate related events, such as tidal flooding, which can have serious economic consequences. Strengthening awareness and preparedness will enhance the community's capacity to respond to the impacts of climate change.

54. The project will also develop and enhance the silvo-fishery model and embankments, which are essential for securing local livelihoods and strengthening the resilience of the mangrove ecosystem through rehabilitation efforts. A healthy mangrove ecosystem will help reduce erosion and mitigate the negative impacts of tidal flooding. Additionally, the implementation of this project will involve local communities and relevant stakeholders to foster a sense of ownership over the improved embankments, which play a vital role in protecting residential areas within the community.
55. To ensure the project sustainability, the project will continue to improve the of capacity local community groups to maintain the project assets, including the silvo-fishery model and embankment. Regular capacity-building activities will be planned and conducted, and a formal process for asset transfer will be undertaken. The future community group will receive instructions on maintaining and repairing the embankments, and detailed guidelines (operational procedures) will be developed to maintain the sustainability of all project assets.

D. Describe how the project/programme is consistent with national or sub-national sustainable development strategies, including, where appropriate, national adaptation plan (NAP), national or sub-national development plans, poverty reduction strategies, national communications, or national adaptation programs of action, or other relevant instruments, where they exist

56. Nationally Determined Contributions (NDC) of Indonesia: This proposed project will contribute to Indonesia's commitment on climate adaptation by enhancing climate resilience of coastal areas and small islands West Nusa Tenggara, particularly in Lombok Island. In the national context, this project will contribute to the GHG emission reduction target of 26% and up to 41% with international support. This project objective supports the Nawacita Mission towards a low-carbon and climate-resilient development direction, with climate change adaptation and mitigation as an integrated and cross-sectoral priority in the national mid-term development plan. The proposed project will do so by applying these strategies: (1) developing village-based local climate resilience institutionalization mechanisms in the coastal area of West Lombok, 2) Improving community livelihoods that are resilient and adaptive to climate change, 3) Increasing the carrying capacity of ecosystems.
57. Indonesia's National Climate Adaptation Plan (RAN API). The project will support Indonesia's National Adaptation Plan (RAN-API) prepared by BAPPENAS in 2021, especially in Marine and Coastal Priority Sector in terms of: i) Infrastructure: by combining Community-based Adaptation (CbA) approaches; and Capacity building: by providing alternative livelihood for small-scale fishermen during extreme weather. It will also refer to The Ministry of Environment and Forestry Regulation No. P.33, 2016 about Guidelines on Climate Adaptation Action. This project will provide inputs for the Climate Adaptation Plan.
58. Indonesia's Adaptation Communication. The Project will contribute in strengthening and demonstrating the eight pillars of NDC Roadmap Adaptation strategies particularly on strengthening policy instruments for climate change adaptation and disaster risks reduction in coastal areas, integrating climate adaptation into development planning and financial mechanisms at village and subnational level, strengthening local capacity by best practices in coastal climate adaptation and application of adaptive technology for climate impacts in coastal areas.
59. In the sub-national context, this project will contribute to strengthen the following sustainable development policy and strategy:
- Governor Regulation No. 54/2019 regarding Climate Change Adaptation (API⁶) Regional Action Plans (RAD⁷),
 - Governor Regulation No. 51/2012 regarding regional action plans to reduce greenhouse gasses (GRK⁸),
 - Regional Regulation No. 12/2017 regarding zoning plans for coastal areas and small islands in NTB, concerning poverty reduction strategies, the implementation of this project supports efforts to improve community livelihoods that are resilient and adaptive to climate change in coastal areas so that this is very much following the NTB Gubernatorial Regulation No. 29/21 concerning poverty alleviation.

⁶ Climate Change Adaptation = Adaptasi Perubahan Iklim (API)

⁷ Regional Action Plans = Rencana Aksi Daerah (RAD)

⁸ Greenhouse gasses = Gas Rumah Kaca (GRK)

E. Describe how the project/programme meets relevant national technical standards, where applicable, such as standards for environmental assessment, building codes, etc., and complies with the Environmental and Social Policy of the Adaptation Fund

60. Relevant national policies/regulations to this project, as well as the compliance to AF Environmental and Social Policy are described in below:

Commented [GU3]: apakah ada aturan subnational dilokasi yang align juga dengan intervensi

1. Conservation of Biological Diversity

- Law No. 1, 2014 on changes of Law No. 27, 2007 on Coastal and Small Island Management. The law is a reference for national and local governments in managing coastal areas and small islands. The project focuses to improve climate resilience of coastal areas and small islands
- Government Regulation No. 26 of 2020 on Forest Rehabilitation and Reclamation. The regulation is a reference on general pattern, criteria and standard for forest rehabilitation and reclamation. Project activities will include rehabilitation of mangroves in coastal areas and will follow this regulation
- Minister of Marine Affairs and Fisheries Regulation No. 24/PERMEN-KP/2016 on Procedures for acquiring permits to manage Coastal Areas and Small Islands. The regulation is a reference for national, local governments and the private sector in acquiring location permits and permits to manage coastal areas and small islands. The project activities in conducting ecosystem restorations and developing livelihood activities will follow this regulation.
- Regulation of the Minister of Maritime Affairs and Fisheries No.3 of 2019 regarding community participation in implementing the protection and empowerment of fishermen, fish cultivators and salt farmers

2. Protection Habitat

- Law No 32/2009 on Environmental Management and Protection. Project activities are related to environmental protection and management, so this regulation is a guideline in carrying out environmental management and monitoring activities
- Law No. 11, 2020 on Job Creation. Article 35 states that businesses and/or activities that are not required to be equipped with UKL-UPL as referred to in Article 34 paragraph (4) are required to make a statement of ability to manage and monitor the environment (SPPL).
- Government regulation No. 22/2021 on Implementation of environmental protection and management. This regulation will support project activities in environmental protection, especially embankment improvement and mangrove rehabilitation activities.
- Minister of Environment and Forestry Regulation No. 4/2021 on a list of businesses that require Environmental Permits (AMDAL, UKL-UPL and SPPL). Most project activities are knowledge management and capacity building activities which do not require AMDAL/UKL-UPL. Project activity particularly improvement of small hybrid infrastructure for ecosystem restoration will have the environmental permit (SPPL).
- Regulation of the Minister of Public Works and Republic of Indonesia public housing number 07/PRT/M/2015 concerning Beach security. This regulation is in strict accordance with the project activity in the improvement of embankments. It serves as a guideline in the design of structures, technical specifications and plan drawings, and calculation of the volume and cost of building embankments.

3. Climate Change

- Law No.24 of 2007 concerning Disaster Management. The project will strengthen disaster-resilient villages through policy, institutional and village planning support
- Presidential Regulation No. 98, 2021 on implementation of carbon economic value; section 3 on Implementation of Climate Change Adaptation. The regulation is a reference for the implementation of carbon economic value to reach the nationally determined contribution (NDC) by climate mitigation and adaptation. The project will follow the regulation particularly on implementation of climate adaptation.
- Ministry of Home Affairs Regulation No 114 of 2014 on Guidance for Village Development. This regulation strongly supports project activities related to the development of disaster-resilient villages.
- Ministry of Environment and Forestry Regulation No. 33/2016 on Guidance for Development of Climate Change Adaptation Action: The regulation is a reference for national and local governments to develop their climate change adaptation action plan and subsequently mainstreaming the plan into corresponding development plan. The regulation stated area/sector identification that will be the subject should be followed by climate vulnerability and risk

assessment before developing climate change adaptation actions and its implementation priorities. The actions should be mainstreamed to the corresponding development plan, program and policy. The project will support the district governments of Rote Ndao and Sabu Raijua to develop the climate change adaptation action plans.

- Ministry of Environment and Forestry Regulation No. P.84/MenLHK-Setjen/Kum.1/11/2016 about PROKLIM (*Program Kampung Iklim*); Directorate General of Climate Change Regulation No. P.1/PPPI/SET/KUM.1/2/2017 about Guidelines to implement PROKLIM. The regulations are a reference for the local governments to implement the climate village program (PROKLIM). The project will support the GOI in promoting the PROKLIM and will refer to these regulations.
- BNPB Head Regulation No. 1 of 2012 concerning general guidelines for disaster resilient villages.

4. Gender and Women Empowerment

- Government regulation No.7 of 2021 concerning facilitation, protection and empowerment of cooperatives, and micro, small and medium enterprises. This regulation is very relevant to community empowerment activities contained in output 3.2. So that it becomes a guideline for the project in improving the livelihood of beneficiaries & developing small businesses of target groups.
- Presidential Instruction No. 9/2000. Gender Mainstreaming in National Development emphasizes women's participation in development processes. This regulation serves as a project guideline in supporting women's participation in project activities, is very consistent with gender action plan.
- Technical guidelines Government incentive assistance to increase business/production capacity of tourism business actors and productive economy No.HK.01./2/Juknis/DII/2020 Ministry of Tourism and Creative Economy.

Identification of Project Compliance in Meeting Regulatory Standards

Table 13. Strategies for Complying with Regulations Most Relevant to Project Activities

| Output | Activities | Regulation | Project Strategy and Efforts in Meeting Standards and Regulations Based on Regulations |
|--------|---|--|--|
| 3.1. | 3.1.3. Planting mangrove enrichment in an area of 20 hectares in selected locations | <p>Law No.1, 2014 on amendments to Law No.27, 2007 on Coastal and Small Islands Management.</p> <p>Government Regulation No.26 of 2020 concerning Forest Rehabilitation and Reclamation</p> <p>Regulation of the Minister of Maritime Affairs and Fisheries No.3 of 2019</p> | <ul style="list-style-type: none"> • Permit for the use of coastal areas to the NTB Provincial Marine Service by attaching an application letter, technical plan for planting and recommendations from the village/sub-district government • The project ensures the suitability of the location in accordance with the RTRW of West Lombok Province and Regency • The project ensures the location is included in the area for mangrove rehabilitation • Field surveys to ensure soil conditions, salinity, and tides are suitable for mangroves • The use of local mangrove seedlings that are suitable for the ecosystem at the planting site • Seedlings must meet forest rehabilitation and reclamation standards according to the standards of the Ministry of Environment and Forestry (minimum 50 cm in height, healthy, certified from an official nursery). • Pay attention to the silvofishery planting method or planting 1x1 meter apart • Conducting coordinate data collection and the use of GPS for each plant for monitoring • Evaluation every 3 months to determine the life rate of the seedlings and pest threats • The survival rate is at least 60% according to the Ministry of Environment and Forestry Regulation no.7 of 2021 • If the seedlings die >40%, the project has a replanting obligation • The project ensures that the location of the planting of hasus is in accordance with the conditions of the mangrove ecosystem. • Selection of species planted through a biodiversity study process • Safeguards must pay attention to good techniques to ensure a high success rate • The project must conduct monitoring and evaluation • Involving the local community in the process of planting and maintaining mangroves • Planting activities are associated with the economic empowerment of local communities |

| Output | Activities | Regulation | Project Strategy and Efforts in Meeting Standards and Regulations Based on Regulations |
|--------|--|--|---|
| | | | <ul style="list-style-type: none"> All phases must be clearly documented, including the initial selection of the location, the planting process and the results of monitoring Submission of periodic reports to the Ministry of Environment and Forestry and the Ministry of Environment and Forestry and/or related agencies |
| | | Law No.24 of 2007 concerning Disaster Management | <ul style="list-style-type: none"> Project identifies disaster risks before planting Community participation by involving local communities The project integrates mangrove planting activities with regional disaster management plans The project prepares an action plan to overcome the disaster of coastal ecosystem damage with mangroves acting as ecosystems that can reduce disasters The project provides counseling and training to local communities on the importance of mangroves in disaster management and how to take care of them. |
| | | Presidential Regulation No.98 of 2021 concerning the Economic Value of Carbon | <ul style="list-style-type: none"> The project registers on the national registration system Climate Change https://srm.menlhk.go.id Complete the requirements of the project documents (planting plan, carbon sequestration target, mangrove rehabilitation permit from the Ministry of Forestry/Ministry of Environment/KKP) The project conducts periodic monitoring and reporting (MRV). Verification of the validity of the data by an independent verifier |
| | | Regulation of the Minister of Environment and Forestry No.33/2016 concerning Guidelines for the Development of Climate Change Adaptation Actions | <ul style="list-style-type: none"> The project conducts vulnerability analysis and community engagement assessments The project develops adaptation action plans (short- and long-term goals, mitigation measures and mangrove-planting specific activities) The project incorporates ecosystem aspects (action plan covers ecosystems that are maintained and restored to increase resilience to climate change) The project conducts capacity building through community training and public awareness. |
| | | Regulation of the Ministry of Environment and Forestry No. P.84/MenLHK-Setjen/Kum.1/11/2016 | <ul style="list-style-type: none"> The project prepares an activity plan which includes a recovery plan and initial analysis (soil conditions, salinity, extent of damage and mangrove species) The project conducts an analysis of location selection, species, planting methods, approvals and permits as well as maintenance and monitoring to ensure the success of mangrove planting and the sustainability of the mangrove ecosystem. |
| | 3.1.4. Facilitation in providing infrastructure packages for climate disaster risk reduction in mangrove areas; Infrastructure: seizure-resistant talut - (rehabilitation) | Government Regulation No.22/2021 concerning the Implementation of Environmental Protection and Management | <ul style="list-style-type: none"> Involvement of community participation in the implementation process. Conducting routine monitoring of environmental impacts during improvement Periodic project implementation reports to the relevant agencies |

F. Describe if there is duplication of project/programme with other funding sources, if any

61. Coastal community development initiatives in Lembar and Sekotong Sub districts have been implemented since 2012. Support for policy advocacy for the management of coastal areas and small islands through the preparation of draft regional regulations has been supported in the 2012 IMACS Project supported by IFAD in 2013-2017. Several strategic programs from the central government have also been implemented, including disaster-resilient villages and climate village programs. However, the project implemented did not entirely cover the 6 villages as proposed in this proposal.

62. Based on that, the proposed proposal can be declared as not overlapping with the previous projects because the proposed project focuses more on 1) on adaptation and resilience of village-based coastal areas, 2) increasing community participation to reduce the impact of tidal disasters, 3) creating other sources of livelihood for the community and 4) increasing the carrying capacity of the ecosystem to reduce the impact of the tidal disaster.
63. There are several interesting lessons from the initiatives that have been carried out by previous projects, namely 1) the Regional Regulation on the management of coastal areas and small islands (PWP3K) in West Lombok Regency provides guidelines as a direction for the management of coastal areas, 2) Starting to grow awareness and knowledge of the community regarding the importance of coastal ecosystems, 3) the emergence of community leaders who have a concern for the preservation of coastal ecosystems.

Table 14. Project Initiatives that have been implemented in Lembar and Sekotong sub-districts

| No | Project | Goal | Year | Funding Sources | Potential Synergies & Collaboration |
|----|--|---|-----------|---|---|
| 1 | Indonesian Marine and climate Support Project (IMACS) | Facilitation of Draft Regional Regulations (Raperda) regarding the management of coastal areas and small islands (PWP3K) in West Lombok Regency | 2012 | IMACS dan Gadjah Mada University | The project will leverage the information of climate change information in coastal areas and updated through Project intervention. The Project will also advocate for policy uptake on coastal areas management using the draft regulation and studies facilitated by IMACS |
| 2 | Coastal community empowerment project coastal Community Development Project (CCDP) | Empowerment of coastal communities through improving the economy of the community in South Lembar Village | 2013-2017 | CCDP - IFAD, Bappenas dan Marine and Fisheries Ministry | The Project will cascade and upscale the intervention to other villages from the activities carried out in CCDP sites |
| 3 | Ecotourism Development in Eat Mayang Area, Lembar District | Protection mangrove ecosystem and guiding mangrove cultivation independently | 2013 | Marine and Fisheries Ministry | This project will cascade and upscale ecotourism activities to other villages from activities carried out in ministry's project sites. |
| 4 | Disaster-resilient tourism village development | Provision of infrastructure and community empowerment in the village of South Lembar, Central Sekotong, Cendi Manik, West Sekotong | 2013 | BPBD NTB dan Palang Merah Indonesia (PMI) | The project will update the baseline information and cascade intervention to develop disaster resilient tourism villages in other villages (other than covered in BPBD programme) |
| 5 | Climate Village program | Increase public understanding of climate change and its impacts so that all parties are encouraged to take concrete actions that can strengthen resilience to climate change and contribute significantly to GHG reduction in South Lembar Village, Central Sekotong, Cendi Manik | 2021 | KLHK | The Project will leverage the awareness and knowledge produced from Proklam to be used on the key Project intervention that aim to strengthen and enhance awareness (Output 2.1) |

G. If applicable, describe the learning and knowledge management component to capture and disseminate lessons learned.

64. The successful implementation of this project will provide a series of lessons learned and project knowledge management. The project knowledge management plan is described in the following table.

Table 15. Knowledge Management Plan

| Project Output | Targeted Audience | Knowledge Products | Means of Dissemination | Means of Access |
|----------------|--|--|--|--|
| 1.1 | Government, community groups, Vulnerable groups (women and youth), Private sector, CSOs | Document of Participatory climate risk analysis (PCRA) | Workshop, video | Consortium & government website and social media, national and local media |
| | | Module of Training packages for village government and village climate disaster preparedness work team | Training, Video | Consortium and government website and social media, national and local media |
| | Government, community groups, Vulnerable groups (women and youth), Private sector | Document local polices | Workshop and Expert team meeting, Video | Consortium and government website and social media, national and local media |
| | Government of West Nusa Tenggara dan District of West Lombok, Community groups, vulnerable groups (women groups & youth) | Document of guidelines/plans/standards (contingency plan, early warning system) | Workshop and Expert team meeting, | Consortium and government website and social media, national and local media |
| | Village government, Community groups, Vulnerable groups | Policy brief/policy paper | Workshop and Expert team meeting | Consortium & government website and social media, national and local media |
| 2.2. | Government of West Nusa Tenggara dan District of West Lombok, Community groups, vulnerable groups (women groups and youth) | Video, Printing Document best practices and lesson learned from demonstration of climate adaptation models | Delivery to stakeholders | www.transform.or.id www.konsepsi.org www.kemitraan.or.id www.data.ntbprov.go.id www.satudata.lombokbarat.go.id |
| 3.1. | Local government, village government, fishermen groups, vulnerable groups (women and youth) | Document and Video Coastal area plan integration | Workshop and training, delivery networking, Media mainstreaming and media social | Consortium and government website and social media, national and local media |
| 3.2. | Private sectors, Government, Community groups, Fishermen groups, BUMDes, SMEs | Value chain analyses report, | Workshops, Journalist Trip | Consortium and government website and social media, national and local media |
| 3.3. | Private sectors, Government, Community, Fishermen groups, BUMDes, SMEs | Business case models, BMP publication, local champion stories or videos | Workshop, Journalist Trip, Exhibition, B2B Meetings | Consortium and government website and social media, national and local media |

65. To ensure synergy and sustainability of the knowledge transfer and management, the Project will also align the Project knowledge materials and dissemination with knowledge management centers owned by the West Nusa Tenggara Provincial government, namely; One NTB Data and West Lombok District Government, namely; SIWARTA, and NTB Siaga from BPBD NTB Province.

66. To maintain the sustainability of adaptation activities in the 4 target villages, several efforts can be made:

- a. Prepare support from village government funding by budgeting annually from the village budget (APBD). This budget support will be possible after policy advocacy is carried out by the project so that the village government realizes the importance of budget allocation from the village government. In addition, the project will ensure the improvement of knowledge and skills of beneficiary groups so that they can support adaptation activities with full awareness of the importance of climate change adaptation actions.
- b. Encourage support from outside parties, including universities, including the University of Mataram and other universities, NGOs, local governments, and other relevant institutions to strengthen climate change adaptation programs. The infrastructure monitoring and maintenance Program built from this project will continue with the support of these parties. Therefore, in the project's implementation phase, the consortium will involve external parties as part of the collaboration steps of the parties to realize the program's sustainability in the four target villages.

Table 16. The Role of Stakeholders in This Project is Described as Follows

| No | Organization | Roles | Required support | Methods | Tools |
|----|---|---|---|------------------------------------|---|
| 1 | Village Government | <ul style="list-style-type: none"> ▪ Integrating adaptation and mitigation projects/programs into village development policies. ▪ Issue / implement local policies and regulations to encourage the optimization of the results of projects/programs adaptation and mitigation of coastal areas and mangroves ▪ Perform low information and appreciation of the implementation of local customs and regulations to the community ▪ Provide funding through APBDES to support adaptation and mitigation projects for coastal and mangrove areas | <ul style="list-style-type: none"> ▪ Preparation of Village regulations, awig-awig project management/ program adaptation and mitigation of coastal areas and mangroves. ▪ Allocating APBDES funds for Project Management/adaptation and mitigation programs for coastal and mangrove areas | FGD, regular meeting, consultation | Letter, presentation materials, policy brief, photo documentation |
| 2 | West Lombok Regional Development Planning Agency | <ul style="list-style-type: none"> ▪ Coordinate community projects/programs with related regional device organizations (OPD). ▪ Ensure strategic planning and policy integration of coastal and mangrove areas into regional Medium-Term Development and regional strategic plans. ▪ Making coastal areas and mangroves a priority in developing environmentally friendly areas. ▪ Identify and allocate a budget from APBD to support adaptation and mitigation programs for coastal and mangrove areas | <ul style="list-style-type: none"> ▪ Ensuring financial support from the central government and the private sector through CSR funds ▪ Collaboration and integration project/program adaptation and mitigation of coastal areas and mangroves from multiple parties (Penta helix) | FGD, regular meeting, consultation | Letter, presentation materials, policy brief, photo documentation |
| 3 | West Lombok Regency Tourism Office | <ul style="list-style-type: none"> ▪ Developing ecotourism based on coastal and mangrove areas as a tourist destination that maintains sustainability, cleanliness, and environmental friendliness. ▪ Assist local communities in developing educational tour packages and conserving coastal and mangrove areas. ▪ Conducting education to the community of coastal and mangrove area entrepreneurs and also visitors in maintaining environmental sustainability, tourism waste management ▪ Branding coastal and mangrove tourism as environmentally friendly tourism by highlighting the beauty of nature and its conservation. ▪ Encourage environmentally friendly tourism policies or regulations | <ul style="list-style-type: none"> ▪ Provide building facilities for coastal and mangrove Tourist Information Centers. ▪ Improving community capacity in the management of coastal and mangrove tourism areas ▪ Provide grants or financial support to coastal and mangrove area management communities grants or financial support. ▪ Help promote coastal and mangrove areas ▪ Supporting the operationalization of Pokdarwis in the village to play an optimal role | FGD, regular meeting, consultation | Letter, presentation materials, policy brief |
| 4 | Village Government Empowerment Service, West Lombok Regency | <ul style="list-style-type: none"> ▪ Strengthening the capacity of the village government (prangkat) in planning, implementing, monitoring and evaluating community-based adaptation and mitigation programs ▪ Assist the village government in formulating local policies on the protection of coastal and mangrove management ▪ Encourage the planning of adaptation and mitigation programs for coastal and mangrove areas into the village | <ul style="list-style-type: none"> ▪ Ensure budget allocation support for adaptation and mitigation programs for coastal and mangrove Ecosystem areas. ▪ Coordination with the relevant OPD at the district and provincial levels related to the preservation of coastal and mangrove ecosystems ▪ Support for capacity-building activities for village and community apparatus staff in | FGD, regular meeting, consultation | Letter, presentation materials, policy brief |

| No | Organization | Roles | Required support | Methods | Tools |
|----|---|---|--|------------------------------------|---|
| | | <p>development plan (RPJMdes) and the village Government Work Plan (RKPDes).</p> <ul style="list-style-type: none"> Support the establishment/strengthening of coastal and mangrove monitoring groups Facilitate cooperation between villages to help improve the management of coastal and mangrove ecosystems that are environmentally friendly and adaptive. Ensuring budgetary support for the management of coastal and mangrove areas for communities | managing coastal and mangrove ecosystems | | |
| 5 | Forestry and Environmental Service of West Nusa Tenggara Province | <ul style="list-style-type: none"> Mapping mangrove areas to determine areas of protection, restoration, rehabilitation, and preservation. Integrating mangrove conservation efforts into strategic plans and regional action plans related to climate change Improving the technical capacity of local communities in the conservation and restoration of mangrove Ecosystem Management. Monitoring and evaluation of mangrove areas. Conducting low enforcement against communities that carry out mangrove degradation activities | <ul style="list-style-type: none"> Support for mangrove seedlings and community nurseries Coordination with relevant OPD at both district and village levels Provide rewards to communities that can preserve, rehabilitate, and become mangrove areas through environmental service payment schemes Incorporating coastal and mangrove areas into climate-friendly villages. Support the activities of community groups that run the climate Village program optimally | FGD, regular meeting, consultation | Letter, presentation materials, policy brief, photo documentation |
| 6 | Department of Fisheries and Marine Affairs of West Nusa Tenggara Province | <ul style="list-style-type: none"> Mapping coastal areas and mangroves to determine areas of protection, restoration, rehabilitation, and preservation. Integrating efforts to preserve coastal areas detailed plan Spatial Plan Improving the technical capacity of local communities in conservation, restoration, and management of coastal areas and capture fisheries Monitoring and evaluation of coastal areas and capture fisheries | <ul style="list-style-type: none"> Provide rewards to communities/groups that can preserve, rehabilitate, and maintain coastal areas and capture fisheries Support the activities of community groups that run the Pokmaswas program optimally. Support optimal funding of community monitoring groups | FGD, regular meeting, consultation | Letter, presentation materials, policy brief, photo documentation |
| 7 | Non-Government Organization (NGO) | <ul style="list-style-type: none"> Facilitate rehabilitation/ restoration programs, environmental education, and Community Empowerment for managing coastal areas and mangroves. Bridging the results of community-processed products with modern and traditional markets Increasing community awareness of coastal and mangrove ecosystems Assisting the community in drafting, implementing, and monitoring local regulations on the management of coastal and mangrove areas. | <ul style="list-style-type: none"> Help bridge third-party funding support for sustainable ecosystem management Policy advocacy to the parties | Observation, FGD, regular meeting | Letter, presentation materials |

| No | Organization | Roles | Required support | Methods | Tools |
|----|---|---|--|------------------------------------|---|
| 8 | University/ College | <ul style="list-style-type: none"> ▪ Researching coastal and mangrove Ecosystem Management. ▪ Provide recommendations based on research results to support policies and best practices in the management of coastal areas and mangroves ▪ Educating the community on sustainable management of coastal and mangrove ecosystems | <ul style="list-style-type: none"> ▪ Assist the local community through community service programs on an ongoing basis ▪ Provide guidance and assistance to strengthen administration and institutional management of coastal and mangrove areas. ▪ Access to field data for research in coastal and mangrove areas | Observation, FGD | Letters, presentation materials, photo documentation |
| 9 | Private Enterprise | <ul style="list-style-type: none"> ▪ Provide financial assistance through Corporate Social Responsibility (CSR) programs. ▪ Encourage sustainable investment that does not focus on coastal and mangrove ecosystems | <ul style="list-style-type: none"> ▪ Collaboration with NGOs or local communities in the implementation of CSR projects/programs. | FGD | Letter, presentation materials, policy brief |
| 10 | Mass Media | <ul style="list-style-type: none"> ▪ Disseminate information about the importance of coastal and mangrove areas and adaptation and mitigation efforts ▪ Raising public awareness through news and media coverage | <ul style="list-style-type: none"> ▪ Access data and information on research results and project/program reports to increase the credibility of news and news coverage. ▪ Cooperation with local communities and NGOs to collect data and field stories on Project/program performance | Observation, FGD | Letter, presentation materials, policy brief, photo documentation |
| 11 | Department of Industry and Trade of West Lombok Regency | <ul style="list-style-type: none"> ▪ Development of processed products based on coastal and mangrove ecosystems that are environmentally friendly. ▪ Empowerment of small and medium industries in coastal and mangrove areas through training activities, the establishment of joint business groups ▪ Strengthening supply chains and marketing by linking community products to modern markets and promoting them ▪ Improving the quality of processed products that are certified and have legality | <ul style="list-style-type: none"> ▪ Capacity building for the community in producing and marketing processed products from silvo-fishery and mangrove. ▪ Become a bridge for the product-community to enter the modern market ▪ Policies that require the modern market to conduct partnerships in the marketing of processed products silvo-fishery and mangrove ▪ Promote silvo-fishery and mangrove processed products | FGD, regular meeting, consultation | Letter, presentation materials, policy brief |

H. Describe the consultative process, including the list of stakeholders consulted, undertaken during project preparation, with particular reference to vulnerable groups, including gender considerations, in compliance with the Environmental and Social Policy and Gender Policy of the Adaptation Fund.

67. This project has consulted with relevant stakeholders in relevant with the policy/decisions related to issues (tidal flood and climate change adaptation) starting from the community level up to the regency and province level as summarized of consultation activities below:

Table 17. Results of Stakeholder Consultation on Tidal Flood Issues and Climate Change Adaptation, at Community, District, and Provincial Levels in NTB

| No | Methods | Implementation | Participants | Goals and results |
|----|--|--|--|--|
| 1 | Focus Group Discussion | July 10, 2023 in Gerung-District of Lombok Barat | This FGD was attended by 35 participants who represent: The Provincial Disaster Management Agency; the Provincial Forestry and Environmental Office; the District Disaster Management Agency; the District Fisheries Office; the District Agriculture Office; the District Development Planning Agency; the district of Village community and government empowerment office; head of 2 sub-district; head of 6 villages. | This FGD intended to gather data/Information related to the impact of Climate Change by sector and location as well as to inform the design of proposed project concept notes (as was submitted to AF) |
| 2 | Series consultation with targeted community | <ul style="list-style-type: none"> ▪ July 23, 2023 in Village of Cendi Manik ▪ July 24 in Village of Central Sekotong ▪ July 24, 2023 in Village of South Lembar ▪ July 24, 2023 in Village of West Sekotong | The number of participants in the six villages was 140 people (30% of them were women) as representatives of Village Government, Heads of sub-villages, Women's Groups, Persons with Disabilities, Vulnerable Groups, and local leaders. | This activity intended to explore the views, experiences, and stories of key informants regarding with tidal flood disaster and its impact on their livelihoods as well as to gather their suggestions/inputs about the kind of program or intervention model that they need. |
| 3 | Workshop Consultation of Project Proposal Design | August 10, 2023, at FAVE Hotel Mataram | This activity was attended by 37 participants from the provincial government (development planning agency, disaster management agency, environmental and forestry office, women empowerment office); the district government (agriculture office, fisheries office, head of sub-districts, development planning agency, disaster management agency); four (4) selected government village | The objective of this consultation workshop is to present the results of the Rapid Climate Risk Assessment in six (6) site villages and the project design that will be submitted to the Adaptation Fund. In addition, to gather suggestions and input from stakeholders regarding the proposed project design. |
| 4 | Presentation and consultation with the Directorate General of PPI, Ministry of Environment and Forestry (MoEF) | June 12, 2024, Via Zoom Meeting. (Figure 8 (F)) | This activity uses focus group discussion (FGD) technique. Participants who attended the meeting included staff of the Directorate General of Climate Change Control, Ministry of Environment and Forestry, staff of the Ministry of Home Affairs, staff of the Ministry of Marine Affairs and Fisheries, staff of the Directorate of Environment Ministry of MoEF | The purpose of the meeting was to present the scope of the project proposal to the PPI Directorate to obtain important input regarding the policy of the Directorate of climate change adaptation related to the project proposal. The suggestions given by participants include: 1. Input the reference source of Sidik data (national area vulnerability data) for the project target location village. |

| No | Methods | Implementation | Participants | Goals and results |
|----|---------|----------------|---|--|
| | | | as well as members of the consortium LC3 including Partnership, Transform and conception. | <ol style="list-style-type: none"> 2. In the introduction needs to be revised by showing the project's climate reasoning 3. Improvement of embankments need to consider 4. The Proposal needs to increase the number of proklim villages in the target districts so that it can support the national policy of 20,000 climate villages. 5. The target location of the project is not included in the conservation area of the Ministry of Environment and forestry 6. Embankment infrastructure development needs to consider whether environmental licensing is included in the EIA, UKL-UPL or other licensing. |



Figure 8. Workshop consultation process in villages (B,C) and district level (A,D,E), (F) National Meeting with KLHK

I. Provide justification for funding requested, focusing on the full cost of adaptation reasoning

68. Climate change adaptation aims to increase resilience by reducing vulnerability and increasing the capacity of communities and areas where they live, exposed to disasters. Thus, if hazards and vulnerabilities are reduced, and the power of the community and region is increased, the community's resilience in facing tidal disasters caused by climate change will be better/increased. Thus, it will minimize the communities' risk of loss of life, economy, society, and environment experienced by tidal flood disasters.
69. The development of climate resilience programs in West Lombok regency has been implemented in five villages, including Mareje, Cendi Manik, Banyu Urip, East Sekotong, and South Kuripan. The 5 villages have received a charter for their participation in developing the climate village program with an intermediate category by the Ministry of Environment and Forestry in 2021. However, the West Lombok Government's policy to integrate climate change management is still weak, as reflected in their 2019-2024 RPJMD. Goals for achieving the fifth mission: Increasing environmental quality and reducing regional disaster risk with the environmental quality index and regional disaster risk index as a measure of success with targets of 58.57 for IKLH and 123.58 for IRBD at the end of the RPJMD period. There are only two programs related to low carbon development and increasing climate resilience: The waste management performance development program and the pollution control improvement program.
70. This project is proposed to reduce the risk of vulnerability and increase the resilience of communities and the environment exposed to tidal disasters. This hope/goal will be achieved if the capacity of the community is increased. This is in the form of knowledge and skills of vulnerable groups, the ability to manage livelihood resources, and support from the institutional and policy needed for this purpose. In handling the tidal disaster in Lembar district and Sekotong district, the West Lombok government has included the handling of the tidal disaster in the 2019-2024 RPJMD. However, this effort has not been carried out because 1) the allocation of funds that should have been used for handling tidal flood disasters was diverted to overcome the COVID-19 pandemic, 2) the allocation of funds is relatively small, so it is not able to handle tidal disasters, 3) village funds are only able to handle small-scale development, 4) tidal flood's impact is felt almost every year, so urgent action is needed. For this reason, Adaptation Fund is needed to stimulate efforts for tidal flood disasters response.
71. If the community and the area in this project location do not have support from the Adaptation Fund, then the community in six villages (Lembar district and Sekotong district) will always be continuously exposed to tidal flood disasters because of climate change. In addition, environmental damage will get worse if this condition continues. Therefore, the existence of policy advocacy activities for stakeholders, especially the village, district, and provincial government, will ensure the sustainability of this program. This is especially in sustainable management of coastal areas and communities, in managing community livelihoods and the coastal regions for climate change adaptation.

Table 18. Scenarios and justifications for why this project intervention is vital to be proposed

| Component | Without the Adaptation Fund | With the Adaptation Fund |
|---|---|--|
| Output 1.1 Institutions, policy and planning Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | The institutional resilience at the village level in dealing with the tidal disaster is still limited due to its low capacity and limited support for facilities and infrastructure. | Losses due to climate change disasters from the aspect of resilience will increase. Meanwhile, the element of vulnerability will decrease because the capacity has increased. |
| Output 1.2. Village community action plan on climate-related disaster risk reduction | Community participation in contributing to mitigating and adapting to overcome disasters is small due to low awareness. | The number of people contributing to climate change adaptation activities will increase because they have received the support of knowledge & skills in dealing with climate change. |
| Output 2.1. Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions | The community's preparedness in dealing with disasters is lacking because the facilities and infrastructure to anticipate this happening do not yet exist. | The community will always be ready to face the tidal disaster because they have acquired the knowledge, skills, and infrastructure to deal with the tidal floods in the village. |
| Output 3.1. Established business management capacity and opportunity for viable community livelihood and smallholder businesses | Opportunities to obtain sources of livelihood are limited due to lack of knowledge and skills in creating job opportunities. Therefore, the number of people who will become jobless will increase. | Opportunities to develop and create sources of livelihood will be opened so that the community's income level when a disaster occurs will be stable. |

| Component | Without the Adaptation Fund | With the Adaptation Fund |
|--|---|--|
| Output 3.2. Community income-generating and productive economic activities are increased | Community income during the tidal flood disaster decreased due to the cessation of work activities. Unfortunately, the number of people who will experience this decline in income will continue to increase. | Opportunities to develop and create sources of livelihood will be opened so that the community's income level when a disaster occurs will be stable. |

J. Describe how the sustainability of the project/programme outcomes has been taken into account when designing the project/programme.

72. The sustainability of project/program outcomes has been considered when designing the project. The project's sustainability is developed from the perspective of policies, institutions, and financing at the village and regency levels.
73. At the village level, a multi-stakeholder forum will be formed to discuss and develop community action plans to reduce vulnerability to climate change. In addition, a village alert team will also be constructed or utilized, one of whose duties is emergency response to disasters. The establishment of these institutions is based on village regulations and legalized by the village head. Meanwhile, to ensure sustainable financing, the agreed community action plan to reduce vulnerability to climate change will be integrated into the village medium-term development plan (RPJMDesa) and/or village working plan (RPKPDesa) documents.
74. At the regency level, the regional action plan document for climate change adaptation (RAD-API) of West Lombok regency will be prepared, and legalized through a Regent Regulation. Furthermore, the village climate change adaptation plan that has been integrated into the village planning document is sought to be accommodated in West Lombok's RAD-API document. In addition, the West Lombok Climate Change Working Group (Pokja Perubahan Iklim) will also be formed, tasked to ensure the implementation of climate change adaptation programs and conduct evaluation monitoring.
75. NTB's risk index score decreased from 172.00 (HIGH) in 2013 to 128.05 (MEDIUM) in 2020 and 122.33 (MEDIUM) in 2021. In the last six years the regency/city's disaster risk index scores generally decrease. The IRBI 2021 data states that there are three regencies that are still "HIGH" risk, namely: Sumbawa, Central Lombok, and West Lombok. The risk index value that does not change is due to the constant capacity value as described above.
76. Along with the above, the progress of disaster-resilient village development is quite significant, including the villages in West Lombok regency. Disaster-resilient villages are mostly from districts in West Lombok. Most of them are financed from the APBD, while others are supported by Non-Governmental Organizations (NGOs).
77. In general, the distribution of disaster-resilient villages/sub-districts in West Nusa Tenggara is spread over Mataram city, covering three districts consisting of eight sub-districts, West Lombok regency includes eleven districts comprised of 50 villages/sub-districts, Central Lombok regency contains ten districts consisting of 34 villages/sub-districts, East Lombok regency includes 12 districts comprised of 31 villages/sub-districts, North Lombok regency covering five districts consisting of 22 villages/sub-districts, West Sumbawa regency covering three districts composed of five villages/sub-districts, Sumbawa regency includes four districts consisting of eight villages, Dompu regency includes seven districts comprised of 18 villages/sub-districts, Bima regency has eleven districts consists of 36 villages/sub-districts, Bima city includes five Sub districts and 12 villages/sub-districts.
78. Mechanisms to ensure the benefits of adaptation can be maintained and replicated after the project is completed by:
1. Encourage local governments (provinces and districts) to allocate more significant funding from local budget funds to address the effects of climate change and the allocation of budgets from village governments for infrastructure maintenance and mangrove protection programs.
 2. Encourage funding from Corporate Social Responsibility (CSR) for mentoring and empowering groups so that the sustainability of programs funded by the Adaptation Fund occurs.
 3. Collaboration of the private sector, NGOs, and universities to ensure the project's sustainability by creating a Memorandum of Understanding (MOU) to focus the activities carried out on four target villages. The collaboration can support and facilitate the community's processed products related to silvofishery and improve the welfare and livelihoods of the group. In addition, it also facilitates target

group processed products with modern and traditional markets, bringing closer access to financing for people who need financial support to develop processed products.

4. Increase group awareness, knowledge, skills, independent village institutions, and environmental consciousness from the group level to the village government to ensure the development of embankment infrastructure and mangrove rehabilitation can be well maintained and expanded with group awareness. In addition, encouraging the sylvo-fishery model can be replicated in other locations to improve community welfare and Coastal Environmental Protection efforts in 4 target villages.
5. As part of the exit strategy, the handover of operational and maintenance from project implementers to local governments, village governments and NGOs that have focused activities that handle products facilitated through AF funds is carried out.
6. In the implementation of project implementation activities, stakeholders related to local government, universities, private sector (CSR), NGOs, and community groups are involved in regular meetings, FGDs, or consultations so that when the project is completed, it will facilitate the sustainability and replication of the project.

K. Provide an overview of the environmental and social impacts and risks identified as being relevant to the project/programme.

79. The results of the component categorization show that component 1 is included in the low risk category (Category C) - Strengthening governance and institutional capacity does not have any significant impact or pose severe negative risks to the environment and society. Component 2 is included in the low-risk category (Category C) - Capacity building in adaptation measures does not have any major impacts on the environment and society. Component 3 is included in the low-risk category (Category C) for coastal ecosystem resilience and sustainable livelihoods. This component includes several activities, including infrastructure development, which may have minor environmental and social impacts. However, the project has been carefully planned, with well-defined interventions and activities, and therefore does not require Unidentified Sub-Projects (USPs). Additionally, the project has identified the relevant policies and regulations to be followed (Table 13), and the proposed interventions and activities have been carefully reviewed and assessed to ensure their feasibility during implementation.
80. The consortium has consulted with relevant stakeholders to identify the necessary requirements for project implementation. Based on these consultations, all project activities, outputs, and outcomes will be prepared, carried out, and achieved by the consortium. As all planned activities fall within the consortium's expertise and experience, no Unidentified Sub-Projects (USPs) will be required during implementation. The selection of interventions to be carried out is in accordance with the assessment and identification of possible risks so that the activities carried out focused on the activities and would not have an impact outside the programme location. These activities will also be carried out by LC3 together with the Consortium.
81. The project will not involve the construction of entirely new embankments, but will focus on improving rehabilitation of embankments existing, damaged embankments that require enhancement. In this context, the project has consulted with relevant stakeholders and confirmed that a UKL-UPL is not required. Accordingly, the term "construction" in the project proposal has been revised to "improvement" to describe the actual activities of the project.
82. From the results of risk identification based on the output project, there are several risks that fall into the moderate category and need to get serious attention in this project, including risks to beneficiaries who do not have access to capital, loss of community livelihoods and injustice in obtaining social assistance when the rob disaster, the risk of very slow growth of mangrove planting, and the risk of soil pollution due to the use of plastics. In minimizing these risks, the project has identified mitigation actions including project activities that need to connect beneficiaries with the bank as well as facilitation of licensing and product marketing so that it is hoped that beneficiaries can run their businesses to increase income, conduct an inventory of directly affected communities as a basis for targeting the provision of assistance from government and other parties, using certified mangrove seeds and assisting the community in carrying out maintenance and monitoring evaluations, limiting the use of plastic in project activities.
83. The risks that have a low level identified include the risk of non-compliance in infrastructure development with standard civil technical requirements which must refer to Law No. 18 of 1999, the risk that local people do not get access to work, the risk of domination of certain mangrove species over other species, the existence of the risk of releasing greenhouse gases originating from vehicles transporting project

materials, there is a risk that vulnerable groups in society (disabilities, women, the elderly) are not given the opportunity by their families and relatives to be involved in project activities. Mitigation efforts that need to be carried out have been identified to minimize the risk of this happening. The results of risk identification, levels and mitigation actions based on ESP Adaptation Fund are more clearly presented in the following table.

Table 19. Environmental and Social Principles, Compliance Assessment, Potential Impacts and Risks

| Checklist of Environmental and Social Principles | No Further Assessment Required for Compliance | Potential Impacts and Risks – Further Assessment and Management Required for Compliance |
|---|---|---|
| <i>Compliance with the Law</i> | √ | |
| <i>Access and Equity</i> | √ | |
| <i>Marginalized and Vulnerable Groups</i> | √ | |
| <i>Human Rights</i> | √ | |
| <i>Gender Equality & Women's Empowerment</i> | | √ |
| <i>Core Labour Rights</i> | √ | |
| <i>Indigenous Peoples</i> | √ | |
| <i>Involuntary Resettlement</i> | √ | |
| <i>Protection of Natural Habitats</i> | √ | |
| <i>Conservation of Biological Diversity</i> | √ | |
| <i>Climate Change</i> | √ | |
| <i>Pollution Prevention & Resource Efficiency</i> | | N |
| <i>Public Health</i> | √ | |
| <i>Physical and Cultural Heritage</i> | √ | |
| <i>Lands and Soil Conservation</i> | √ | |

Commented [SM4]: apakah tidak ada terumbu karang atau lamun yang terdampak??

Commented [wjs5R4]: Tidak ada terumbu karang atau lamun yang terdampak, lokasi berjarak puluhan Km dari areal konservasi

Commented [YU6]: butuh klarifikasi dan penjelasan soal dampak pada public health ini

Commented [SM7R6]: lebih baik d centang pada bagian no risk, jika ada Risk efek yang ditimbulkan menjadi permanen

a. Compliance with the Law

In the implementation of the project's activities, including the rehabilitation and enhancement of embankments, all interventions will be conducted in accordance with applicable policies and regulations. In particular, the project will align with the Ministry of Environment and Forestry Regulation No. P33 of 2016 concerning Guidelines on Climate Change Adaptation. Compliance with this regulation is expected to ensure that the project does not result in any significant adverse impacts or risks.

b. Access and Equity

The project will not give priority to any particular group or community during its implementation. It is developed solely to address the impacts of climate change, which could worsen over time if not properly managed. In addition, the project will ensure that all relevant stakeholders have equal access to information, which will be made available through inclusive and transparent channels such as project social media and reports. Any concerns related to equal access to project information and benefits will be addressed in a timely and appropriate manner.

c. Marginalized and Vulnerable Group

This project will not involve marginalized and vulnerable groups in any way. Therefore, no further assessment is required, as the project is not expected to have any direct or indirect impact on these groups.

d. Human Rights

This proposal has been developed through consultations with relevant stakeholders, experts, and local communities, respecting human rights in all proposed activities. Therefore, the proposed intervention is not expected to cause any human rights violations, as it aims to address environmental and climate change issues. Furthermore, all participation in the project is voluntary and without coercion.

e. Gender Equality and Women's Empowerment

Women's participation in project initiatives is sometimes limited due to prevailing conservative norms that view their roles as confined to household duties. This project encourages the active involvement of women while ensuring that their existing responsibilities are not further burdened. Women's participation is especially important in achieving Objective 2 (enhancing the adaptive capacity of rural coastal communities to climate-induced hazards) and Objective 3. (strengthening community livelihood resources). By empowering women and ensuring their voices are represented and considered, the project aims to achieve its goals in a more inclusive and equitable manner.

f. Core Labor Rights

All project personnel involved in this initiative will have an employment contract or agreement outlining the rights and responsibilities of both parties (project workers and employer). Regular meetings, trainings, and workshops will be conducted to ensure ongoing coordination and to address any concerns including technical implementation and labor rights. The project will ensure that all workers are aware of their rights and understand their responsibilities as personnel of the project team.

g. Indigenous People

The project will not involve indigenous peoples, as the project sites are located in areas where no indigenous communities are present. Therefore, this project is not expected to have a negative impact or pose a risk to indigenous peoples.

h. Involuntary Settlement

The proposed activities of this project will not require the relocation of residents from the project site areas. Specifically, the embankment improvement and mangrove rehabilitation will not affect the existing residences of local communities.

i. Protection of Natural Habitat

There are no potential risks or negative impacts expected on the natural habitat surrounding the project area. The project location is a settlement, which is tens of kilometers from Bangko-Bangko National Park. The project intervention only increases the existing tidal embankment and does not build new facilities, so the potential to damage the natural habitat is almost non-existent. This project actually aims to increase habitat resilience through rehabilitation of the existing mangrove ecosystem. Therefore, further assessment related to the protection of natural habitat is not required.

j. Conservation of Biological Diversity

Negative impacts and risks to biological diversity are not expected in this project, as the activities mainly involve working with local communities, improving existing embankments, and rehabilitating mangroves. These interventions will not directly or indirectly affect biological diversity, as they do not involve activities that interfere with it. Instead, the mangrove rehabilitation, carried out on degraded land, is expected to enhance the resilience of the mangrove ecosystem in a long term.

k. Climate Change

This project is expected to enhance the capacity of local communities to adapt to climate change. It will not produce significant carbon emissions; instead, it will contribute to reducing the impacts of climate change. Furthermore, the project aims to strengthen the local community's resilience to climate change by developing responsive policies, institutions, and planning to address its impacts (Output 1.1 and Output 1.2)

l. Pollution Preventions and Resources Efficiency

The improvement of the 2,350-meter embankment may result in dust and noise pollution due to the transportation of materials. Additionally, these activities will generate waste. The project will inform affected communities about the planned embankment improvement and provide dust masks to minimize health impacts. Community consent will also be sought prior to the start of the embankment improvement. All generated waste will be collected and disposed of at designated landfill sites.

m. Public Health

The dust generated from the embankment improvement poses a moderate risk to local communities. To address this, the project will obtain consent from potentially affected communities, provide dust masks, and advise residents to stay indoors or limit activities near roads used for material transportation. Additionally, the project will carry out regular watering of these roads to reduce dust levels and minimize impacts.

n. Physical and Cultural Heritage

There are no physical heritage or cultural heritage sites within the project area. Therefore, there are no associated risks, and no further assessment or management is required related to physical and cultural heritage for this project.

o. Land and Soil Conservation

The project will involve improving embankments and rehabilitating mangroves. These activities will not impact land or soil conservation, as the interventions will be carried out on existing embankments and

degraded land that requires rehabilitation. Furthermore, the rehabilitated mangroves are expected to reduce erosion in areas where the mangrove ecosystem has been degraded. Successful rehabilitation will also contribute positively to soil conservation.

84. With risk identification per E&S Principles, the proposed project is categorized as C according to the categories specified in the ESP. Category C corresponds to projects with small potential impact risks, less widespread, reversible, and mitigated. The details of the analysis are as follows:

Table 20. Categorization Definition

| Questions | Component Answer YES/NO | | |
|---|-------------------------|----------|----------|
| | 1 | 2 | 3 |
| Does the Project Outputs/Activities have significant adverse environmental or social impacts that are diverse? | No | No | No |
| Does the Project Outputs/Activities have significant adverse environmental or social impacts that are widespread? | No | No | No |
| Does the Project Outputs/Activities have significant adverse environmental or social impacts that are irreversible? | No | No | No |
| Does the Project Outputs/Activities have few adverse environmental or social impacts? | No | No | No |
| Does the Project Outputs/Activities have in small scale / low widespread adverse environmental or social impacts? | No | No | No |
| Does the Project Outputs/Activities have reversible or easily mitigated adverse environmental or social impacts? | No | No | No |
| Does the Project Outputs/Activities have no adverse environmental or social impacts? | Yes | Yes | Yes |
| Categorization | C | C | C |

PART III: IMPLEMENTATION ARRANGEMENTS

A. Describe the Arrangements for Project/Programme Implementation

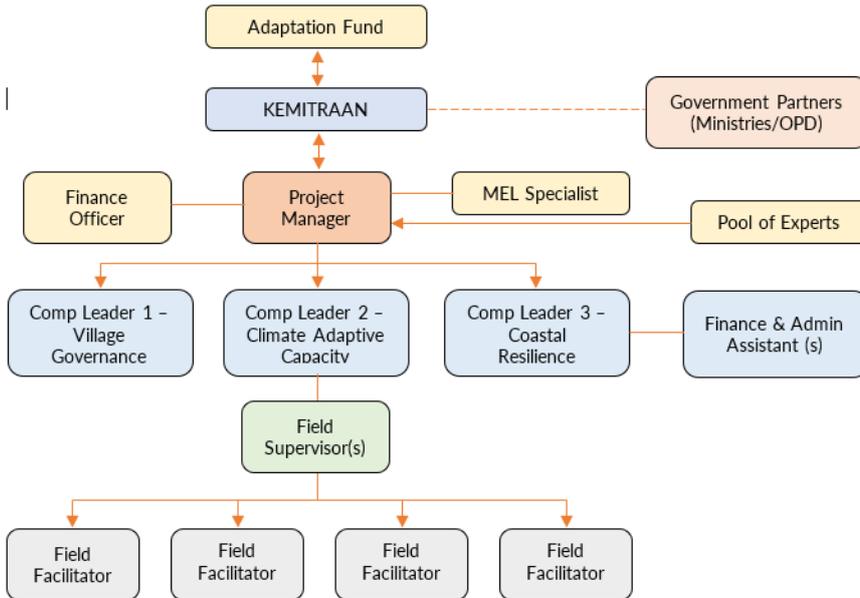


Figure 9. Project Governance Structure

85. The Executing Entity (EE) for this project is LC3 which form Consortium partnership with two local civil society organizations (CSOs) in West Nusa Tenggara, TRANSFORM and KONSEPSI. The Consortium formed a Project Management Unit (PMU) which will be responsible to implement the project and ensures the outcomes to be achieved are in accordance with the project framework and planning. Division of responsibilities among the consortium members has been agreed as stated in the Letter of Agreement signed by consortium members. The LoA has been attached in this proposal document.
86. The Project Management Unit is led by a Project Manager that will be responsible and report directly to KEMITRAAN as National Implementing Entity (NIE). In delivering work plan and ensuring the project outcome, the Project Manager will be assisted by Outcome Component Leaders (3 persons – for each Outcome Component) for program-related matters, 1 MEL Specialist for technical support in project monitoring and evaluation and 1 Finance Officer to ensure financial planning and management of the overall project. The Outcome Component Leaders will be assisted by Field Supervisor, Finance and Admin Assistant and Field Facilitators (4 facilitators). The Field Facilitators will work at the village level and spend 15 working days in the village in a month. The Outcome Component Leaders will be assisted by the Finance and Administration Assistant who will handle the administrative and financial issues at the local level. The coordination mechanism including monitoring and evaluation will be jointly conducted in regular manner with the representative of the National Implementing Entity.
87. In ensuring that the planned activities will achieve its expected outputs and outcome, the PMU will receive technical assistance from pool of experts with different backgrounds and expertise including: Climate & Disaster Preparedness Specialist, Village Governance Specialist, Community Development Specialist, Hydro Civil Engineering Specialist, Mangrove Rehabilitation Specialist, Sustainable Agriculture Specialist, Sylvo-fishery Specialist, SMEs and Livelihood Specialist, Knowledge Management Specialist and Gender and Social Inclusion Specialist. These experts will provide inputs for technical knowledge in other relevant project component both at subnational and field/village level.

88. The project component will ensure that gender mainstreaming will be promoted and aligned within the Project cycle since planning, implementation until monitoring and evaluation. The Project will also apply gender balance and affirmation policy to ensure that gender-based approach and inclusion in the recruitment and staffing of the Project. To improve the understanding on how to mainstream and promote gender responsive planning and action plan, series of capacity building will be provided to ensure each facilitator will have the sound knowledge and guidance in the project implementation. The project will also apply gender tracking tools in its monitoring and evaluation framework to ensure that a gender responsive knowledge management and learning is in place.

Table 21. The Role of Each Institution

| Structure | Duties and responsibilities | Explanation |
|---------------------|---|---|
| Government Partners | The government partners will be engaged in coordination for policy direction and alignment for the project activities implementation. The government partners will also provide advice and recommendation for the successful implementation of the Project. Where feasible, government partners will also be engaged in the knowledge dissemination and learning platform. | At national level, the Ministry of Environment and Forestry (KLHK) will be engaged as the AF focal point. Other line ministries relevant to program component (e.g. Ministry of Marine and Fisheries Affairs, Ministry of Village, Ministry of Home Affairs, BNPB, BMKG and etc.) will be engaged when necessary for sectoral and technical coordination. At subnational level, key government agencies will be involved include: BAPPEDA, Office of Forestry, Office of Environment Affairs, Office of Marine and Fisheries, Office of Tourism Affairs, Office of Village Development, BFPD. |
| Executing Entity | <ol style="list-style-type: none"> 1. Program preparation, including selecting PMU and linking the Government partners 2. Program implementation, including communication and coordination with AF focal point and line ministries 3. Program monitoring and evaluation of PMU 4. Financial monitoring and assessment of project implementation | As the executing entity, KEMITRAAN will ensure the implementation of the program will follow and align with the Adaptation Fund Policy |
| Project Manager | <p>The Project Manager will direct PMU in delivering and implementing the project, such tasks will include:</p> <ol style="list-style-type: none"> 1. Together with PMU, the Program Implementation Plan will be prepared as a guide for implementing the program 2. Ensure that the program is carried out in accordance with the objectives and result framework 3. Assuring the monitoring of Project progress and results of achievement 4. Ensure the coordination mechanism with the related parties | The Program Manager is the Program leader who will be responsible for the National Implementing Entity through reporting results |
| Pool of Experts | <p>Will be responsible for technical advice and input towards project activities implementation, which include:</p> <ol style="list-style-type: none"> 1. Climate & Disaster Preparedness 2. Village Governance and Planning 3. Community Development 4. Hydro Civil Engineering for Sea Dyke 5. Mangrove Rehabilitation 6. Sustainable Agriculture/sylvofishery 7. SMEs and Livelihood Development 8. Knowledge Management 9. Gender and Social Inclusion | <p>The pool of experts will include at the minimum the following:</p> <ol style="list-style-type: none"> 1. Climate & Disaster Preparedness Specialist 2. Village Governance and Planning Specialist <p>Community Development Specialist</p> <ol style="list-style-type: none"> 1. Hydro Civil Engineering Specialist 2. Mangrove Rehabilitation Specialist 3. Sustainable Agriculture/Sylvofishery Specialist 4. SMEs and Livelihood Specialist 5. Knowledge Management Specialist 6. Gender and Social Inclusion Specialist |

| Structure | Duties and responsibilities | Explanation |
|--------------------|--|---|
| Finance Officer | The Finance Officer will be responsible for financial and administrative management of the overall project and assist the Project Manager in preparing financial forecast and planning as well as financial report in each reporting period | - |
| Component Leaders | Will be responsible for implementing for each main Outcome Component of the Project. The key tasks would include: 1. Together with the Field Supervisor, preparing program implementation plan for each main Outcome Component as implementation guideline 2. Ensuring that the program is carried out in accordance with the objectives and result framework 3. Lead in coordination on program progress and achievement with the field supervisor 4. Lead in establishing and maintaining coordination with the subnational government and relevant stakeholders | - |
| Field Supervisor | 1. Coordination with Outcome Component Leader in implementing the program 2. Manage and assist coordination with the subnational government at district level 3. Coordinating the field facilitators to ensure the activities implementation is in accordance with work plan and result to be achieved 4. Report to Outcome Component Leader and Project Manager in the progress, results and challenges of Project | Field facilitators will be based in the district and coordinate with the field facilitators in each village for the project activities implementation |
| Field Facilitators | Will come in direct contact with the beneficiaries 1. Act as Project contact point and establish communication and relationship with the project beneficiaries at village level 2. Together with the field supervisor developing work plan for the project activities execution at village level 3. Assist the Project team to implement the activities in the field/village level in accordance with the Project workplan 4. Report to the Field Supervisor for the Project activities implementation, result and challenges | The Field Facilitators will be based in each targeted village and will be responsible for the project execution at the ground/site. |

B. Describe the Measures for Financial and Project/Programme Risk Management

Table 22. Summary of Risks and Issues of the Proposed Project

| Risk Category | Risk Rating | Risk Description | Proposed Mitigation Measures | Indicator | Responsible Person |
|---|--------------|--|--|---|-------------------------------------|
| 1. Stakeholder Management Risk | | | | | |
| 1.1. Low participation in Project activities implementation | Low | Stakeholders (Local Fishermen, Women Group, Costume/ Traditional Figure, Youth, NGOs) have low buy in and support in the project approach and activities | <ul style="list-style-type: none"> Intensive awareness campaigns, clear communication is carried out to increase understanding and acceptance of the local community. The Project Operation Manual will be developed to align and comply with the assessed environmental and social risks and the Environmental Social Safeguards Management Plan. A program of alternative livelihood in the coastal areas (mangrove rehabilitation and climate smart agriculture) will be developed to provide adaptation measures co-benefits. | <ul style="list-style-type: none"> Number of activities implemented and level of participant attendance Availability of project manuals and level of implementation compliance Number of farmers involved, percentage of income increase, area of mangrove rehabilitated | Project Manager, Field Facilitators |
| 1.2. Changes of political leadership (government official) towards Project support and sustainability | Low-Moderate | Changing political leadership during the course of the Project may affect in the political support of the Project and pose risks for sustainability measures | <ul style="list-style-type: none"> The Project ensures that during implementation it will establish strong communication and manage a network of local leaders with Political Partners at the national and subnational levels. Whenever there is a change in political leadership, the Project will utilize the retained local leaders to transfer information, knowledge and Project approaches. | <ul style="list-style-type: none"> Documentation of meetings with local/national leaders Number of key persons bridging project information Knowledge transfer survey results | Project Manager |
| 2. Financial Risk | | | | | |
| 2.1 Fraud and Corruption | Low | Project staff may have the risks to commit fraud and corruption practices due to their lack of knowledge and integrity | <ul style="list-style-type: none"> Providing assistance, monitoring and audit for the Project Developing whistle blowing systems to provide prevention measures for such action | <ul style="list-style-type: none"> Number of monitoring and availability of audit reports Online portal and complaint box Confidentiality policy and whistleblower protection | Finance Officer |
| 2.2 Improper financial reporting | Low | The Project staff may have the likelihood to prepare improper financial reporting that is not in compliance with Project Guideline | <ul style="list-style-type: none"> Providing capacity building/training prior to project implementation, develop financial management guideline and conducting monitoring and technical assistance to finance and administrative staff at the project site | <ul style="list-style-type: none"> Number of training activities Participant attendance list Availability of financial guidance documents Guidance for financial and administrative staff | Finance Officer |
| 3. Executing Entity Risk | | | | | |
| 3.1 Capacity of Implementing Partners | Moderate | The consortium partners may have low capacity in Project implementation in accordance to AF project implementation guideline | <ul style="list-style-type: none"> Robust recruitment of project staffs and experts for project management Assistance and capacity building by KEMITRAAN to Consortium Partners to improve understanding on AF project implementation guideline Assignment of technical experts/advisors in each component for project implementation | <ul style="list-style-type: none"> Number of project implementers who attended induction and initial orientation Frequency of technical coordination Frequency of technical consultation and guidance | Project Manager |

KEMITRAAN and local partners (TRANSFORM and KONSEPSI), as the executing entity, holds primary responsibility for monitoring the implementation of mitigation measures. Monitoring-related activities will be carried out in close collaboration with relevant local government technical agencies, such as the Environmental Agency, the Regional Disaster Management Agency, the regional Development Planning Agency, as well as with community-based monitoring groups at the village level (e.g., Disaster Risk Reduction Forums or environmental awareness groups). KEMITRAAN will coordinate the reporting process, impact evaluations, and necessary corrective actions in accordance with the Environmental and Social Management Plan (ESMP) adopted by the project.

C. Describe the Measures for Environmental and Social Risk Management, in line with the Environmental and Social Policy and Gender Policy of the Adaptation Fund

Table 23. Environmental and Social Principles, Identified Risk and Impact, Measures to Minimize or Mitigate, dan Monitoring Indicator

| Environmental and Social Principles | Identified Risk/ Impact | Measures to Minimize or Mitigate | Monitoring Indicators | Person in Charge (PIC) |
|-------------------------------------|-------------------------|--|---|---|
| Compliance with law | Low | Synchronizing existing rules, for example rules on planning, implementation and maintenance. | <ul style="list-style-type: none"> ▪ Level of cross-sector involvement in planning; ▪ Level of compliance with operational standards and technical regulations; ▪ Availability of post-implementation maintenance and monitoring mechanisms. | Project Manager, MEL Specialist, Field Supervisor |
| Access and equity | Low- Moderate | Risk: Access of women and vulnerable groups to get involved and benefit from project implementation Mitigation: <ul style="list-style-type: none"> ▪ Participatory resource management ▪ The operational project will mandate gender mainstreaming in every activity implementation Connecting beneficiaries with the bank and facilitating business licensing and facilitating product marketing | <ul style="list-style-type: none"> ▪ Percentage of beneficiaries involved in each type of project activity (planning, training, implementation, monitoring) ▪ Identification of banking and market needs and access as outlined in the form of a report ▪ Percentage of women's groups receiving assistance in the form of processing equipment, and facilitated with banking and market access. | MEL Specialist, Field Supervisor |
| Marginalized and Vulnerable Groups | Low- Moderate | Taking inventory of directly affected communities as a basis for targets for providing assistance from the government and other parties | <ul style="list-style-type: none"> ▪ Identification of affected beneficiary communities ▪ Documentation of inventory report of affected communities | Field Supervisor |
| Human rights | Low | Apply consistency in the proportion of women's and men's involvement in project activities | <ul style="list-style-type: none"> ▪ Availability of SOP for complaint mechanism for communities at project sites ▪ Documentation of community or beneficiary agreement to reject or accept project activities (FPIC) that have the potential to affect livelihoods, the environment and others. Note: Padiatapa as the principle of Free, Prior and Informed Consent (FPIC). | Expert, MEL Specialist, Field Supervisor, Project Manager |
| Gender and Women Empowerment | Low | Develop SOPs regarding local community involvement in project infrastructure development. | <ul style="list-style-type: none"> ▪ Availability of SOP for local community involvement in project activity implementation. ▪ Percentage of women involved in each type of project activity (planning, training, implementation, monitoring). | Experts, MEL Specialist, Field Supervisor |
| Core Labour right | Low | Implement consistency in the proportion of involvement of local communities in project activities | <ul style="list-style-type: none"> ▪ Percentage/Number of local communities involved in project activities ▪ Documentation of local community involvement (photos, attendance lists, reports) | MEL Specialist, Field Supervisor |

| Environmental and Social Principles | Identified Risk/ Impact | Measures to Minimize or Mitigate | Monitoring Indicators | Person in Charge (PIC) |
|--|-------------------------|---|---|--|
| Indigenous People | Low | Building a dialogue process between the community, community leaders and the government to build an agreement in the event of resettlement | <ul style="list-style-type: none"> ▪ Frequency of dialogue between the community, figures and government to build agreements. ▪ Documentation of dialogue activities (photos, attendance lists) | MEL Specialist, Field Supervisor |
| Involuntary Resettlement | Low | The use of certified mangrove seeds and community assistance in carrying out maintenance and monitoring evaluations | <ul style="list-style-type: none"> ▪ Identification of affected communities who participate in voluntary resettlement. ▪ Documentation of the implementation of participatory planning and selection of appropriate locations. ▪ Documentation (photos, minutes). | Field Supervisor |
| Protection Habitat | Moderate | <p>Risk: The survival rate of planted mangrove seedlings is low, thus affecting the project results.</p> <p>Mitigation:</p> <ul style="list-style-type: none"> ▪ Ensure vegetation type selection and location for mangrove rehabilitation suits with the biophysical characteristics of mangrove ecosystems ▪ The Project will also promote the development of community-based nurseries for the mangrove seeds materials ▪ Develop clear work plan and operational support for maintenance and monitoring of the mangrove survival. <p>Cultivate mangrove seedlings consisting of several species that are suitable for the habitat conditions at the project site</p> | <ul style="list-style-type: none"> ▪ Number of groups involved in area protection, mentoring and mangrove nursery ▪ Document of group work plan for maintenance and monitoring. ▪ Number of mangrove species cultivated according to project location characteristics. Percentage of mangrove seeds used from certified sources. ▪ Documentation (photos, activity reports) | Project Manager, Experts, MEL Specialist, Field Supervisor |
| Conservation of Biological Diversity | Low | Use of vehicles that emit low emissions based on emission test results from the Department of Transportation. | <ul style="list-style-type: none"> ▪ Number of seedlings planted and progress of mangrove areas that have been planted ▪ Documentation (photos, activity reports) | Project Manager, Field Supervisor |
| Climate Change | Low | Conduct regular watering at project sites affected by dust. | <ul style="list-style-type: none"> ▪ Report on emission test results and periodic inspections of vehicles used by the Transportation Agency | MEL Specialist, Field Supervisor |
| Pollution prevention and resource efficiency | Low | Providing emergency facilities for handling public health at the time of a rob disaster including light medicines and provision of personal protective equipment | <ul style="list-style-type: none"> ▪ Availability of standard occupational health and safety (K3) facilities ▪ Photo documentation of watering activities at project locations affected by dust ▪ Number of training/socialization activities for plastic reduction | Experts, MEL Specialist, Field Supervisor |
| Public health | Low | Provide understanding and assistance to families of vulnerable groups and disabilities. | <ul style="list-style-type: none"> ▪ Emergency facilities for public health care during disasters, including light medicines and provision of protective equipment ▪ Documentation (attendance list, photos of activities) | MEL Specialist, Field Supervisor |
| Lands and soil conservation | Low- Moderate | <p>Risk: The coastal embankment built is not in compliance with the standard technical design and may have shorter period for sustainability</p> <p>Mitigation:</p> | <ul style="list-style-type: none"> ▪ Documentation and reports of routine soil quality monitoring ▪ Documentation of community involvement (photos, attendance lists) ▪ Availability of SOPs for soil and water conservation | Experts, MEL Specialist, Field Supervisor |

| Environmental and Social Principles | Identified Risk/ Impact | Measures to Minimize or Mitigate | Monitoring Indicators | Person in Charge (PIC) |
|-------------------------------------|-------------------------|--|---|------------------------|
| | | <ul style="list-style-type: none"> ▪ Ensuring that robust and proper feasibility study and detailed engineering design is prepared prior to embankment enhancement works ▪ Ensuring that vendor/subcontractor selection will follow best quality principle and efficiency ▪ Ensuring the improvement of the coastal embankment is in compliance with the DED ▪ Ensuring compliance with policies and technical standard in the environment and civil engineering sector <p>Develop clear cooperation rules in the implementation of projects infrastructure improvement, prepare Detailed Engineering Design Documents (DED) for physical buildings and consistently carry out monitoring and evaluation</p> | techniques to control soil degradation. | |

89. Based on the results of consultation with the Environment Office of West Lombok regency and referring to the regulation of the Minister of Environment and Forestry (LHK) number 4 of 2021 on the list of businesses and activities that must have an analysis of environmental impacts, environmental management efforts and environmental monitoring efforts or a statement of Environmental Management and monitoring capabilities shows that 2,350 meters of embankment improvement activities require UKL-UPL licensing. This is because the development in the coastal area range does not have the potential to change the ecology of the coastal area, so it does not significantly impact the balance of the ecosystem around the location. In the UKL-UPL document, the potential environmental impacts that can occur will be comprehensively identified, and environmental management and monitoring efforts will be developed to avoid and minimize the impacts. For the compilation of this UKL-UPL document, it has been estimated at output 3.1.4.b.

Table 24. Potential Risk, Level and Mitigation Related to Gender Equality and Women's Empowerment, Pollution Prevention and Resource Efficiency

| Component | Potential Risks | Level | Mitigation |
|-------------|--|-------|---|
| Component 3 | <ul style="list-style-type: none"> ▪ Women's participation and involvement in each project activity. Women get fewer opportunities than men due to the influence of community culture | Low | Apply consistency in the proportion of women's and men's involvement in project activities |
| Component 3 | <ul style="list-style-type: none"> ▪ Dust pollution due to the entry and exit of operational vehicles carrying project materials ▪ Noise pollution – the impact of the movement of vehicles when transporting materials and tools to the project site. ▪ Waste generated from the improvement of rob-resistant embankments. | Low | <ul style="list-style-type: none"> ▪ Conduct regular watering at project sites affected by dust. ▪ Obtain consent from potentially affected communities before beginning the improvement of embankment. ▪ Provide dust masks to community members to reduce the impact of dust exposure. |

GRIEVANCE MECHANISM

90. Complaints arising from stakeholders and the general public involved in the Executing Entity (EE) to be submitted to the Implementing Activities to be discussed together to find a way out. If consensus is not reached, a complaint can be submitted to the National Implementing Entity (NiE) using the form. Complaints that will be processed with the Grievance Mechanism are only related to all project activities. Complaints and complaints information must be submitted in writing via email or letter sent or delivered directly during the visit. Other channels such as text messages / SMS, or oral / telephone complaints can be rejected as official complaints or asked to be distributed in writing. EE and NiE must ensure the confidentiality of the complaint. In registering a complaint, the complainant must fill out and attach the Complaint Form. As the first point, the complaint form from stakeholders and the community related to the project uses the same form, so it will be easier to send it to the National Implementing Entity (NIE). Registered complaints that deserve to be followed up through the Complaint Settlement Plan.

The following is an example of a complaint form:

Grievance Form
Lombok Climate Change Consortium (LC3)

Filled by LC3 Consortium

| | |
|---------------------------|--|
| <i>Grievance No.</i> | |
| <i>Name of registerer</i> | Date: |
| <i>Source</i> | sms / email / letter / fax / phone / visit / others:..... *) |

*) Circle the appropriate

Filled by Complainant

| | |
|---|-------|
| Complainant Data | |
| <i>Name</i> | |
| <i>Address</i> | |
| <i>Phone No.</i> | |
| <i>Fax</i> | |
| <i>E-mail</i> | |
| Grievance Information | |
| <i>Location</i> | |
| <i>Program</i> | |
| <i>Parties was reported</i> | |
| <i>Date of occurrence</i> | |
| <i>Detail grievance:</i> | |
| <i>(Completed with related evidence or documents)</i> | |
| <i>(if this part is insufficient, then allowed to use additional paper)</i> | |
| <i>Complainant Name and Signature</i> | Date: |
| <i>Receiver name and signature</i> | Date: |

Notes: The form must be made 2 copies: 1 copy for complainant, and 1 copy for archives.

Complaints regarding projects/programmes can also be filed with the secretariat at the address provided below:

Adaptation Fund Board
Secretariat Mail stop: MSN P4-
400 1818 H Street NW
Washington DC 20433 USA
Tel: 001-202-478-7347
afbsec@adaptation-fund.org

91. The strategy to ensure all beneficiaries or communities can have access to the grievance mechanism is by providing socialization regarding the complaint mechanism at the beginning of the project, on the other hand project management will also provide complaint box facilities installed at the location of each intervention village (installed at the village office or facility others) to ensure this mechanism is affordable for all beneficiaries of project activities. Every month at the end of the week, the complaint box will be checked regularly to ensure that complaints can be received and evaluated regularly.

INSTITUTIONAL ARRANGEMENTS

The institutional arrangement includes the distribution of roles and responsibilities in the implementation of ESMP. The key players and their responsibilities will be as follows:

| Designation | Responsibility |
|-------------------------------|--|
| Program Management Unit (PMU) | <ul style="list-style-type: none">▪ Identification of Environmental and Social Problems at the Project Site▪ Coordinate with expert in social forestry for the screening of project impact to vulnerable groups▪ Public disclosure, and Creation of grievance mechanism at EE level▪ Reporting and disposal of grievances |
| Kemitraan (Partnership) | <ul style="list-style-type: none">▪ Monitor and review the process ESMP implementation▪ Set up the grievance mechanism at IE level▪ Disposal of grievances▪ Sample check and verify ESMP in the project village |

D. Describe the monitoring and evaluation arrangements and provide a budgeted M&E plan, in compliance with the ESP and the Gender Policy of the Adaptation Fund

92. The project will carry out a baseline assessment to establish the status of key project indicators and targets, which will serve as a reference for measuring project success at the end of the project completion. This assessment will be conducted at the outset of project implementation by the Monitoring and Evaluation Specialist, in coordination with the Project Manager and relevant members of the Project Management Unit.
93. Monitoring and evaluation of the project implementation will be conducted quarterly to assess the progress, issues, and challenges of project implementation, including what has been achieved, what is effective, what challenges have arisen, and the lessons learned. These activities will be led by the Monitoring and Evaluation Specialist, in coordination with the Project Manager and other relevant personnel, depending on the issues occurred in the field. The monitoring aspects will cover both financial and technical issues of the project.
94. In addition, an independent party will be appointed at the end of the project to evaluate the project's success and lessons from the project implementation and external annual financial audits will be conducted to verify the project's financial reports and ensure they align with the planned and approved budget.

Commented [SM8]: Mohon dilengkapi kembali pada bagian M&E Plan, karena ini tidak jelas.

Table 25. Monitoring and Evaluation Plan

| M&E Activities | Methods & Tools | Responsible | Target/Deliverables | Cost (USD) | Time |
|--|--|---------------------|--|---------------|--|
| Baseline Survey | <ul style="list-style-type: none"> Field survey FGD, interviews with targeted beneficiaries Participatory observation | | <ul style="list-style-type: none"> Baseline Data Report | 4,000 | Within first three months upon sign of agreement |
| Quarterly and Semester Report: Supervisions/Monitoring | <ul style="list-style-type: none"> FGDs/meetings Interviews with PMU Field Visit (interview with beneficiaries, observation) Supporting document review Financial analysis | IE Project Director | <ul style="list-style-type: none"> Quarterly and Semester reports Quarterly Financial Reports | 15,722 | Every 3/6 months |
| Annual, Midterm, and Final Report | <ul style="list-style-type: none"> FGD/meeting Interviews with PMU Field Visit (interview with beneficiaries, observation) Supporting document review Financial analysis | IE Project Director | <ul style="list-style-type: none"> Annual and Final Project Report Annual dan final PPR Annual & Final Financial Report | 6,604 | By the end of the first-year project dates (12 th month) and by the end of project dates (24 th month) |
| Independent Evaluator/ Terminal Evaluation | <ul style="list-style-type: none"> Independent Evaluator Recruitment FGD/meeting/workshop Interviews with PMU Field Visit (interview with beneficiaries, observation) Supporting document review Project Report Review | IE Project Director | <ul style="list-style-type: none"> Final Project Report PPR Final Project Financial Report | 5,206 | Due date: 6 months after closing |
| Audits | <ul style="list-style-type: none"> External audit Financial report analysis | IE | <ul style="list-style-type: none"> Audit report | 13,807 | At least 9 months after closing |
| Total M&E Cost | | | | 45,339 | |

E. Include a results framework for the project proposal, including milestones, targets and indicators, including one or more core outcome indicators of the Adaptation Fund Results Framework, and in compliance with the Gender Policy of the Adaptation Fun

Table 26. Result Framework for Project Proposal, Including Achievement, Target and Indicator

| Outcome/Output | Indicator | Baseline | End Target | Source of Verification | Responsible Entity | Risk and Mitigation |
|--|--|----------|---|---|---------------------------|--|
| Component 1. Strengthened governance and institutional capacity | | | | | | |
| Outcome 1. Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | # of village that has developed and adopted climate-resilient institutional governance | 0 | 4 | Project report, Evaluation Report | PMU | It is assumed that the village government have strong willingness to mainstream climate resilient approach in its governance process |
| Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | # of village draft policy (Perdes/SK Kades) that promote and/or adopt coastal adaptation actions | 0 | 4 | Policy Document (Village Regulation/Head of Village Decree) Villlage Decree | PMU & Village Facilitator | |
| | # of established task force for climate adaptation action at village level | 0 | 4 | | | |
| | # of guidelines/standards for climate related disasters (EWS) developed | 0 | 4 | Guideline document | | |
| | # of village draft annual development plan (RKPDes) that promote and/or adopt coastal adaptation actions | 0 | 4 | Annual village planning document (RKPDes) | | |
| | # of draft village annual fund (APBDes) allocation prepared for coastal adaptation actions | 0 | 4 | Village Budget (APBDes) | | |
| Output 1.2. Village community action plan on climate-related disaster risk reduction in coastal areas | # of participatory land use planning as reference and direction to develop adaptation action | 0 | 4 | Land use maps | PMU & | |
| | # of community action plans developed to respond towards climate change disaster | 0 | 4 | Community Action Plan | Village Facilitator | |
| Component 2. Capacity building on adaptation measures | | | | | | |
| Outcome 2. Improved and established adaptive capacity for rural coastal communities to climate-induced hazards | # of targeted direct beneficiaries (disaggregated by gender and marginal group) which reported to have increased knowledge on coastal adaptation actions | 0 | Male (1.119) Female (610) Disabilities (35) | Project report; baseline and endline survey | PMU | It is assumed that the direct and indirect beneficiaries would actively participate and learn in the capacity building and related project activities It is assumed that each |
| | # of targeted indirect beneficiaries which | 0 | 7.456 | Project report; | | |

| Outcome/Output | Indicator | Baseline | End Target | Source of Verification | Responsible Entity | Risk and Mitigation |
|--|--|----------|---|---|--------------------|---|
| | reported to have experienced knowledge exchange/learning on adaptation actions # of targeted direct beneficiaries (disaggregated by gender and marginal group) which reported to have adopted knowledge and best practice on coastal adaptation actions | 0 | Male (280) Female (153) Disabilities (9) | baseline and endline survey Project report; baseline and endline survey | | beneficiary influences 4-5 indirect beneficiaries It is assumed that 25% of direct beneficiaries |
| Output 2.1. Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions | # of training and capacity modules and guidelines (incl field school) for coastal adaptation actions developed | 0 | 4 | Training module/curriculum | PMU | It is assumed that 100% of direct beneficiaries |
| | # of targeted direct beneficiaries (disaggregated by gender and marginal group) which reported to have increased knowledge on coastal adaptation action by the Project support (capacity building and field school) | 0 | Male (1.119) Female (610) Disabilities (35) | Training report, Evaluation Report | | |
| | # of knowledge products developed and disseminated to targeted beneficiaries and stakeholders | 0 | 7 | Project report, knowledge publication, media coverage | | |
| Output 2.2. Models of coastal climate adaptation are developed and demonstrated at the targeted community | # of guidelines for demonstration activities on coastal adaptation models developed | 0 | 4 | Guideline document | PMU | |
| | # of success stories on adaptation activities which has been demonstrated during the course of the Project (e.g. indicative number of hectares, number of production rate etc.) | 0 | 8 | Knowledge & lesson publication; Communication materials; | | |
| Component 3. Coastal ecosystems resilience and sustainable livelihoods | | | | | | |
| Outcome 3. Improved resilience of the coastal ecosystem to strengthen community livelihood resources | # of hectares of mangrove ecosystems that has been brought under improved rehabilitation measures (including enrichment) | 0 | 20 | Project report; evaluation report | PMU | It is assumed that: 1. Village government, district government and private sectors shows strong support on the Project approach on improving community livelihood at coastal areas through policy and sustainability measures 2. Local communities are willing to learn and adopt the best practices on coastal ecosystems-based adaptation approach 3. Private sectors and other key stakeholders are willing |
| | # of diversified livelihood and income generating activities options established and/or enhanced with the support of the Project | 0 | 5 | Project report; evaluation report | | |

| Outcome/Output | Indicator | Baseline | End Target | Source of Verification | Responsible Entity | Risk and Mitigation |
|---|--|---|------------|------------------------------------|--------------------|---|
| | | | | | | to engage and provide support towards the Project intervention in creating enabling conditions for community livelihood |
| Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated | # of feasibility study and detailed engineering design for mangrove rehabilitation and coastal embankment | 0 | 3 | FS and DED document | PMU | |
| | #of community groups involved in the establishment of community-based nurseries and mangrove planting | 0 | 3 | Project report; Village Decree | | |
| | # of Ha mangroves areas intervened for mangrove planting in the targeted location | 0 | 20 | Project report, Evaluation report | | |
| | # of Ha mangroves areas intervened for mangrove enrichment and maintenance in the targeted location | 0 | 20 | Project report, Evaluation report | | |
| | # length of coastal embankment built and/or enhanced | Local embankment built to 2.350 km in South Lembar and Central Sekotong Village | 2.350 | Project report; Evaluation report | | |
| Output 3.2. Community income-generating and productive economic activities are increased | # of VCA on coastal community's livelihood developed, incl. market and financial access | 0 | 1 | VCA report/study | PMU | |
| | # of business case model for alternative livelihood in coastal communities developed | 0 | 5 | Business case/plan document | | |
| | # of Project beneficiaries trained or to have experienced increased knowledge on alternative livelihood based on nature-based solutions and EbA approach | 0 | 1.729 | Training report; Evaluation report | | |

F. Demonstrate how the project/programme aligns with the Results Framework of the Adaptation Fund

Table 27. Alignment of Projects/Programs with the Adaptation Fund Results Framework

| Project Objective(s) | Project Objective Indicator(s) | Fund Outcome | Fund Outcome Indicator | Grant Amount (USD) |
|---|---|--|---|--------------------|
| Outcome 1. Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | <ol style="list-style-type: none"> Village that has developed and adopted climate-resilient institutional governance Village draft policy (Perdes/SK Kades) that promote and/or adopt coastal adaptation actions Established task force for climate adaptation action at village level | Outcome 2: Strengthened institutional capacity to reduce risks associated with climate-induced socioeconomic and environmental losses | 2.1. # of staff has increased their capacity to respond and mitigate impacts of, climate-related events from targeted institutions. | USD 296.751 |

| Project Objective(s) | Project Objective Indicator(s) | Fund Outcome | Fund Outcome Indicator | Grant Amount (USD) |
|---|---|--|--|--------------------|
| <p>Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts</p> <p>Output 1.2. Village community action plan on climate-related disaster risk reduction in coastal areas</p> | <p>4. guidelines/standards for climate related disasters (climate risks assessment, climate EWS) developed</p> <p>5. village draft annual development plan (RKPDes) that promote and/or adopt coastal adaptation actions</p> <p>6. draft village annual fund (APBDes) allocation prepared for coastal adaptation actions</p> | | | |
| <p>Outcome 2. Improved and established adaptive capacity for rural coastal communities to climate-induced hazards</p> <p>Output 2.1. Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions</p> <p>Output 2.2. Models of coastal climate adaptation are developed and demonstrated at the targeted community</p> | <p>1. Training and capacity modules and guidelines (incl field school) for coastal adaptation actions developed</p> <p>2. Targeted direct beneficiaries (disaggregated by gender and marginal group) which reported to have increased knowledge on coastal adaptation action by the Project support (capacity building and field school)</p> <p>3. Knowledge products developed and disseminated to targeted beneficiaries and stakeholders</p> <p>4. Guidelines for demonstration activities on coastal adaptation models developed</p> <p>5. Success stories on adaptation activities which has been demonstrated during the course of the Project (e.g., indicative number of hectares, number of production rate etc.)</p> | <p>Outcome 3: Strengthened awareness and ownership of adaptation and climate risk reduction processes at the local level</p> | <p>3.1. # of individual from targeted population aware of predicted adverse impacts of climate change, and of appropriate responses</p> <p>3.2. # of individual from targeted population applying appropriate adaptation responses</p> | USD 260.863 |
| <p>Outcome 3. Improved resilience of the coastal ecosystem to strengthen community livelihood resources</p> <p>Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated</p> <p>Output 3.2. Community income-generating and productive economic activities are increased</p> | <p>1. Hectares of mangrove ecosystems that has been brought under improved rehabilitation measures (including enrichment)</p> <p>2. Diversified livelihood and income generating activities options established and/or enhanced with the support of the Project</p> <p>3. Feasibility study and detailed engineering design for mangrove rehabilitation and coastal embankment</p> <p>4. Community groups involved in the establishment of community-based nurseries and mangrove planting</p> <p>5. Mangrove seeds planted in the targeted location</p> <p>6. Length of coastal embankment built/enhanced</p> <p>7. VCA on coastal community's livelihood developed, incl. market and financial access</p> <p>8. Business case model for alternative livelihood in coastal communities developed</p> <p>9. Project beneficiaries trained or to have experienced increased knowledge on alternative livelihood based on nature-based solutions and EbA approach</p> | <p>Outcome 5: Increased ecosystem resilience in response to climate change and variability induced stress</p> <p>Outcome 6: Diversified and strengthened livelihoods and sources of income for vulnerable people in targeted areas</p> | <p># Hectares of mangrove ecosystem protected and rehabilitated</p> <p># of Community groups established for nursery and mangrove planting.</p> <p># mangrove seeds planted in selected area</p> | USD 300.721 |

¹ The AF utilized OECD/DAC terminology for its results framework. Project proponents may use different terminology but the overall principle should still apply

G. Include a detailed budget with budget notes, a budget on the Implementing Entity management fee use, and an explanation and a breakdown of the execution costs

Table 28. Outcome, Output, Activities, and Project Implementation Cost Details

| Budget Description | Budget Notes | Amount (USD) |
|---|--|----------------|
| Outcome 1: Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | | 296,751 |
| Output 1.1: Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | | 248,981 |
| Activity 1.1.1: Recruitment of village volunteers for climate-related disaster preparedness. | 1 workshop with target participants 30 person, Travels from Jakarta to Lombok for 2 persons, 7 consultants (4 village facilitator, 2 coordinator, 1 admin) for 20 months | 112,002 |
| Activity 1.1.2: Participatory climate risk consultation (PCRC) to explore and detail the characteristics and diversity of climate risks at the household level based on socio-economic aspects and GEDSI | 1 training for field facilitator with target participants 30 person, 1 workshop with target participants 30 person in 4 villages | 13,927 |
| Activity 1.1.3: Establishment of a village climate disaster preparedness work team from village volunteer members and added with other community components. | 1 Meeting and Collecting Data for 50 village with target participants 50 person | 24,461 |
| Activity 1.1.4: Series of training workshop for village government and village climate disaster preparedness work team | Basic training on community-based climate disaster, with target participants 30 person, 1 Training on EWS and contingency plan for disaster with target participants 30 person, 1 Training on village planning process that mainstream disaster management objective with target participants 30 person. | 20,868 |
| Activity 1.1.5: Formulation of local policies on climate resilience at village level | 1 Village Meeting with target participants 30 person, 1 FGDs with district stake-holders with target participants 30 person, 1 Workshop with district stakeholders with target participants 30 person. | 6,058 |
| Activity 1.1.6: Facilitation for formulating climate disaster-related guidelines/plans/standards (contingency plan, early warning system) | 1 Meeting per village (4 villages) with target participants 25 person, 1 Workshop (4 villages) with target participants 30 person | 3,872 |
| Activity 1.1.7: Formulation of policy brief/policy paper to strengthen climate resilience actions or policies at sub-national level | 1 FGDs with district stakeholders with target participants 30 person, 1 Workshop with district stakeholders with target participants 30 person | 2,611 |
| Activity 1.1.8: Technical assistance on strengthening knowledge management systems on climate adaptation | 1 FGDs with district stakeholders with target participants 30-person, 2 Consultants (Consultant Knowledge Management platform establishment and KML Expert), Hosting/plarform/ Domain for 2 yeras | 23,834 |
| Activity 1.1.9: Stakeholder capacity building on climate change rules and policies | 1 kick off workshop (35 participants), Regular meeting (25 persons , 4 time in 4 villages), workshop with consortium partner (30 persons, 3 days, 4 times) | 41,348 |
| Output 1.2: Village community action plan on climate-related disaster risk reduction in coastal areas | | 47,770 |
| Activity 1.2.1: Dissemination of PCRC's results to the wider community through presentation of work team representative in workshop for each village | 1 Meeting for 4 villages Meeting with target participants 25 person | 1,532 |
| Activity 1.2.2: Community Action Planning (CAP) on climate resilience through community discussion series and field workshop. Formulation of CAP also consider | 1 Workshop for 4 village with target participants 30 person | 2,316 |

| Budget Description | Budget Notes | Amount (USD) |
|---|--|----------------|
| input and comments in previous workshop regarding PCRA' results | | |
| Activity 1.2.3: Facilitation on integration Community Action Plan (CAP) with the village government's annual plan and budget through discussion series with village government | 1 Village meeting (scoping and inventory) with target participants 30 person, 1 Village workshop (integration on musrebangdes) with target participants 30 person | 5,380 |
| Activity 1.2.4: Facilitation of annual village development planning forum to decide on village development priority programs in the current year including CAP on climate-induced disaster resilience | 1 Village meeting (thematic musrebang) with target participants 30 person | 3,336 |
| Activity 1.2.5: Advocacy of CAP to sub-national government policies both at district and provincial levels through lobbying and discussion series by inviting sub-national government representatives both district and provincial levels. | 1 FGDs with district and provincial stakeholder with target participants 25 person, 1 Workshop with district stakeholders with target participants 25 person | 5,396 |
| Activity 1.2.6: Series of meeting and technical coordination on village CAP development | 1 Village meeting with target participants 25 person, Travels from Jakarta to Lombok for 2 persons, 1 consultant (ME Specialist) for 24 months | 29,810 |
| Outcome 2: Improved and established adaptive capacity for rural coastal communities to climate-induced hazards | | 260,836 |
| Output 2.1: Increased knowledge and skill of targeted communities including women and vulnerable groups on climate change actions. | | 134,988 |
| Activity 2.1.1: Trainings for targeted community on climate adaptation and resilience. | 1 Training with target participants 30 person | 6,767 |
| Activity 2.1.2: Conducting climate field school on adaptation actions on coastal areas conditions (mangrove, land-based farming in coastal, salt farming); in-class for 6 times in each targeted community, and preparing demonstration plots for climate adaptation (field practices). | Module and guideline development, Consultant Service; 1 Mangrove Specialist, 1 Rehabilitation Ecotourism Specialist, 1 Land Based Farming at Coastal Specialist, 1 GEDSI Specialist, Climate and Disaster Specialist, 1 Coordinator, and 1 Environment Advisor | 52,360 |
| Activity 2.1.3: Conducting simulation/exercise to respond to climate induced disaster by testing the contingency plans and early warning system | 1 Training with target participants 30 person, | 1,946 |
| Activity 2.1.4: Developing and implementing a learning platform and process for communities related to climate adaptation actions through regular learning forums in each village and cross visits to other areas | 1 Meeting meeting with target participants 30 person, | 4,050 |
| Activity 2.1.5: Procurement of climate-induced disaster information and documentation systems | Climate-induced disaster information and documentation systems 1 package | 21,332 |
| Activity 2.1.6: Documenting knowledge and best practices of community actions in climate change by producing Stories of Change (SoC) from targeted groups, videos, and book. | 1 workshop with target participants 30 person, Travels from Jakarta to Lombok for 2 persons, 1 consultant for 6 months | 28,721 |
| Activity 2.1.7: Preparation of climate change monitoring tools in the form of a platform with a GIS/sensor/IoT system. | 1 Meeting with target participants 25 person, Travels from Jakarta to Lombok for 2 persons, 1 consultant for 1 months | 19,812 |
| Output 2.2: Models of coastal climate adaptation are developed and demonstrated at the targeted community | | 125,848 |
| Activity 2.2.1: Conducting analyses and model development on climate adaptation in coastal areas to identify, analyze, design of | 1 Expert Mangrove Silvofishery, 1 Expert Ecotourism, 1 Expert Land Based Farming at Coastal, 1 Expert Climate Adaptation | 24,899 |

Commented [SM9]: Kenapa justru tidak ada kegiatan "penyusunan alat monitoring perubahan iklim (dalam bentuk platform)

| Budget Description | Budget Notes | Amount (USD) |
|---|--|----------------|
| model by hiring the expert team with taking into account PCRA's results and CAP. | Scenario, 1 Coordinator, meeting series (2 time) | |
| Activity 2.2.2: Procurement of climate-induced adaptation facilities/equipment: | Procurement (Equipment for ecotourism: Road enhancement, tourism signage, recreation facilities, sanitation facilities); Procurement (Equipment for land-based farming: Seeds, Fertilizers) | 25,328 |
| Activity 2.2.3: Demonstration of climate adaptation models of coastal climate adaptation at least 3 models i.e. Sylvofishery in the mangrove, climate-smart land-based farming in the coastal, and ecotourism services. | 1 Training in Silvofishery goodpractices (20 participants, 2 days), Village meeting for technical assistance (10 participants, 4 villages, 6 times each village), 1 Training and technical assistance in Climate smart land based farming practices (20 participants, 3 days, 1 time), Training in Ecotourism good practices (20 [articipants, 3 days, 1 time), 1 consultant admin | 42,000 |
| Activity 2.2.4: Documentation best practices and lesson learned from climate adaptation models in coastal area by producing practical guidebook and videos. | 1 Meeting and Cross Visit, Travels from Jakarta to Lombok for 2 persons, Campaign materials (documentary film, short video,etc) 4 pax/product | 23,209 |
| Activity 2.2.5: Capacity building for stakeholders related to adaptive models (climate resilient agricultural systems). | 2 Meeting Coordination with target participants 30 Person, Travels | 10,412 |
| Outcome 3: Improved resilience of the coastal ecosystem to strengthen community livelihood resources | | 300,721 |
| Output 3.1: Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated | | 258,721 |
| Activity 3.1.1: Participatory coastal area spatial plan integrated with climate-induced disaster resilience. | 1 workshop to communities on participatory land use planning with target participants 30 Person, 1 Technical assistance on participatory coastal land use plan development/ mapping with target participants 15 Person, | 12,509 |
| Activity 3.1.2: Development of Associated-Mangrove-Aquaculture (AMA) based on research and tourism. | Develop of mangrove nursery and technical assistant of multi species of mangrove; Develop of AMA adaptive management system | 71,001 |
| Activity 3.1.3: Mangrove enrichment planting in 20-hectare areas at selected sites | Mangrove enrichment planting in 20 hectare areas at selected sites | 20,000 |
| Activity 3.1.4: Facilitation in providing infrastructure packages for climate-disaster risk reduction in mangrove areas; infrastructures: rob-resistant embankments | 1 Environment Monitoring Specialist 1 Social-Economic Assessment Specialist 1 Marine/Coastal Specialist 1 Hydro engineering Specialist 1 Environmental Safeguards Specialist - Repairing of tidal embankments in Cemara Beach 1300 metres - Construction of tidal embankments in Cemara Beach 700 metres - Construction of boat mooring in Cemara Village 20 metre - Construction of tidal embankments in Sekotong Tengah 350 metres - Construction of boat mooring in Sekotong Tengah 5 metres | 155,221 |
| Output 3.2: Community income-generating and productive economic activities are increased | | 42,000 |
| Activity 3.2.1: Value chain development of smallholders' fishery products. | 1 Consultant Social Economy Expert, 2 FGD with target participants 25 Person, | 4,848 |
| Activity 3.2.2: Facilitation of training packages for sustainable smallholder fisheries and livelihood: good practices on fisheries cultivation; diversification of products/processing; marketing. | 4Training for sustainable smallholder fisheries and livelihood with target participants 25 Person | 5,888 |

| Budget Description | Budget Notes | Amount (USD) |
|---|---|----------------|
| Activity 3.2.3: Facilitation small-scale business licensing and product certification | 2 Meeting with target participants 25 Person | 4,404 |
| Activity 3.2.4: Procurement of equipment for productive economies and businesses i.e. production machines, packaging machines, etc. | Procurement of production machines, packaging machines for 4 Villagers | 12,000 |
| Activity 3.2.5: Technical assistance for developing market-demand commodities and products | 1 Training for developing market-demand commodities and products for 4 Villages with target participants 30 Person | 2,744 |
| Activity 3.2.6: Facilitation on access to finance (including venture capital) to support communities' businesses by developing network or collaboration with banks or private sectors | 4 Meeting with target participants 25 Person | 4,024 |
| Activity 3.2.7: Series of reviews and reflections on best practices for improving sustainable livelihood alternatives, and gender mainstreaming learning. | Conducting 1 workshop for review and reflection of learning with 25 participants | 8,092 |
| Project Execution Cost (9.5%) | | 62,189 |
| Project Manager | 24 months | 34,155 |
| Finance Admin Officer | 24 months | 17,604 |
| Audit | 1 time | 10,430 |
| Total Project/Programme Cost | | 920,497 |
| Project Cycle Management Services | | 78,242 |
| Project Identification and Development | This activity is scheduled to be conducted during the initial three months of the project. | 3,912 |
| Project Implementation and Supervision | This activity is scheduled to be conducted on a monthly basis for the duration of the project, Including Travels, and meetings | 39,421 |
| Monitoring and Evaluation | (Baseline Survey \$ 4,000; Quarterly and semester monitoring \$ 15,722; Annual, Midterm and final report \$ 6,604; Independent evaluator \$ 5,206, Audit (partial) \$ 3,377.) | 34,909 |
| Amount of Budget Requested | | 998,739 |

H. Include a Disbursement Schedule With Time-Bound Milestones

Disbursement Schedule with Time-bound Milestones

| | Upon signature of the Agreement | One Year after Project Start | Total |
|-------------------------|---------------------------------|------------------------------|------------------|
| Scheduled date | November 2025 | November 2026 | |
| Project Cost | \$ 546,490 | \$ 374,007 | \$920,497 |
| Implementing Entity Fee | \$ 46,942 | \$ 31,300 | \$78,242 |
| Total | \$ 593,432 | \$ 405,307 | \$998,739 |

Step3: Fill out the amount (USD) and Choose EE Type in green cells

| Project/Program Activity Cost: A | Amount (USD) | EE type | Error Check |
|--|--------------|-----------------------|-------------|
| Outcome 1 Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | 296.751 | Non-IE executes as EE | |
| Outcome 2 Improved and established adaptive capacity for rural coastal communities to climate-induced hazards | 260.836 | Non-IE executes as EE | |
| Outcome 3 Improved resilience of the coastal ecosystem to strengthen community livelihood resources | 300.721 | IE executes as EE | |
| Total Component: A | 858.308 | | |

Step4: Fill out the amount (USD) in green cells and adjust the figures until no error messages pop up

| | Amount (USD) | | Error Check |
|--|-----------------|----------|-------------|
| | Proposed Figure | Cap | |
| Total Component: A | 858.308 | | |
| Fees for IE acting as part of EE(s) | 3.999 | \$4.579 | |
| Fees for Non-IE acting as EE(s) | 58.190 | \$58.531 | |

| | | |
|-------------------------|---------|--|
| Total EE fee: B | 62.189 | |
| Total Program Cost: A+B | 920.497 | |
| IE fee: C | 78.242 | |
| Total Request: A+B+C | 998.739 | |

Table 29. Time Schedule For Project Activity

| Output | Main Activity | Subtotal (USD) | 2024-2026 | | | | | | | |
|---|--|----------------|-----------------------------|-----------------------|-----------------------|-----------------------|-----------------------------|-----------------------|-----------------------|-----------------------|
| | | | Q1 Nov 2025- Jan 2026 | Q2 Feb-Apr 2026 | Q3 May-Jul 2026 | Q4 Aug-Oct 2026 | Q5 Nov 2026- Jan 2027 | Q6 Feb-Apr 2027 | Q7 May-Jul 2027 | Q8 Aug-Oct 2027 |
| Outcome 1: Increased and established of awareness and ability of village and districts government as well as local community in decision making process about climate-related actions/policies based on local contexts | | | | | | | | | | |
| Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | 1.1.1 Recruitment of village volunteers for climate-related disaster preparedness. | 112.002 | | | | | | | | |
| | 1.1.2 Participatory climate risk consultation (PCRC) to explore and detail the characteristics and diversity of climate risks at the household level based on socio-economic aspects and GEDSI | 13.927 | | | | | | | | |
| | 1.1.3 Establishment of a village climate disaster preparedness work team from village volunteer members and added with other community components dan Facilitation of registration of 10 Proklim villages and village assistance towards the primary PROKLIM (3 villages targeted by the Project and 7 villages outside the project target). | 24.461 | | | | | | | | |
| | 1.1.4 Series of training workshop for village government and village climate disaster preparedness work team; | 20.868 | | | | | | | | |
| | 1.1.5 Formulation of local policies on climate resilience at village level | 6.058 | | | | | | | | |
| | 1.1.6 Facilitation for formulating climate disaster-related guidelines/plans/standards (contingency plan, early warning system); | 3.872 | | | | | | | | |
| | 1.1.7 Formulation of policy brief/policy paper to strengthen climate resilience actions or policies at sub-national level | 2.611 | | | | | | | | |
| | 1.1.8 Technical assistance on strengthening knowledge management systems on climate adaptation | 23.834 | | | | | | | | |
| | 1.1.9 Refreshment and coordination of program on institutionalization of village governance and policy making | 41.348 | | | | | | | | |
| Output 1.2. Village community action plan on climate-related disaster risk reduction in coastal areas | 1.2.1 Dissemination of PCRC's results to the wider community through presentation of work team representative in workshop for each village | 1.532 | | | | | | | | |
| | 1.2.2 Community Action Planning (CAP) on climate resilience through community discussion series and field workshop. Formulation of CAP also consider input and comments in previous workshop regarding PCRC' results | 42.316 | | | | | | | | |
| | 1.2.3 Facilitation on integration Community Action Plan (CAP) with the village government's annual plan and budget through discussion series with village government | 5.380 | | | | | | | | |

| Output | Main Activity | Subtotal (USD) | 2024-2026 | | | | | | | |
|---|---|----------------|-----------------------------|-----------------------|-----------------------|-----------------------|-----------------------------|-----------------------|-----------------------|-----------------------|
| | | | Q1 Nov 2025- Jan 2026 | Q2 Feb-Apr 2026 | Q3 May-Jul 2026 | Q4 Aug-Oct 2026 | Q5 Nov 2026- Jan 2027 | Q6 Feb-Apr 2027 | Q7 May-Jul 2027 | Q8 Aug-Oct 2027 |
| | 1.2.4 Facilitation of annual village development planning forum to decide on village development priority programs in the current year including CAP on climate-induced disaster resilience | 3.336 | | | | | | | | |
| | 1.2.5 Advocacy of CAP to sub-national government policies both at district and provincial levels through lobbying and discussion series by inviting sub-national government representatives both district and provincial levels. | 5.396 | | | | | | | | |
| | 1.2.6 Series of meeting and technical coordination on village CAP development | 29.810 | | | | | | | | |
| Outcome 2: Improved and established adaptive capacity for rural coastal communities to climate-induced hazards | | | | | | | | | | |
| Output 2.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | 2.1.1 Trainings for targeted community on climate adaptation and resilience. | 6.767 | | | | | | | | |
| | 2.1.2 Conducting climate field school on adaptation actions on coastal areas conditions (mangrove, land-based farming in coastal, salt farming); in-class for 6 times in each targeted community, and preparing demonstration plots for climate adaptation (field practices). | 52.360 | | | | | | | | |
| | 2.1.3 Conducting simulation/exercise to respond to climate induced disaster by testing the contingency plans and early warning system | 1.946 | | | | | | | | |
| | 2.1.4 Developing and implementing a learning platform and process for communities related to climate adaptation actions through regular learning forums in each village and cross visits to other areas | 4.050 | | | | | | | | |
| | 2.1.5 Procurement of climate-induced disaster information and documentation systems | 21.332 | | | | | | | | |
| | 2.1.6 Documenting knowledge and best practices of community actions in climate change by producing Stories of Change (SoC) from targeted groups, videos, and book. | 28.721 | | | | | | | | |
| | 2.1.7 Review and reflection of learning and program coordination on climate adaptation capacity building. | 19.812 | | | | | | | | |
| Output 2.2. Models of coastal climate adaptation are developed and demonstrated at | 2.2.1 Conducting analyses and model development on climate adaptation in coastal areas to identify, analyze, and design of model by hiring the expert team with taking into account PCRC's results and CAP. | 24.899 | | | | | | | | |
| | 2.2.2 Procurement of climate-induced adaptation facilities/equipment: | 25.328 | | | | | | | | |

| Output | Main Activity | Subtotal (USD) | 2024-2026 | | | | | | | |
|---|--|----------------|-----------------------------|-----------------------|-----------------------|-----------------------|-----------------------------|-----------------------|-----------------------|-----------------------|
| | | | Q1 Nov 2025- Jan 2026 | Q2 Feb-Apr 2026 | Q3 May-Jul 2026 | Q4 Aug-Oct 2026 | Q5 Nov 2026- Jan 2027 | Q6 Feb-Apr 2027 | Q7 May-Jul 2027 | Q8 Aug-Oct 2027 |
| the targeted community | 2.2.3 Demonstration of climate adaptation models of coastal climate adaptation at least 3 models i.e. silvo-fishery in the mangrove, climate-smart land-based farming in the coastal, and ecotourism services. | 42.000 | | | | | | | | |
| | 2.2.4 Documentation best practices and lesson learned from climate adaptation models in coastal area by producing practical guidebook and videos. | 23.209 | | | | | | | | |
| | 2.2.5 Sharing best practices and learning, and program coordination on climate adaptation capacity building | 10.412 | | | | | | | | |
| Outcome 3: Improved resilience of the coastal ecosystem to strengthen community livelihood resources | | | | | | | | | | |
| Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated | 3.1.1 Participatory coastal area spatial plan integrated with climate-induced disaster resilience. | 12.509 | | | | | | | | |
| | 3.1.2 Develop of Associated-Mangrove-Aquaculture (AMA) based on research and tourism, consist of activities: | 71.001 | | | | | | | | |
| | 3.1.3 Mangrove enrichment planting in 20 hectare areas at selected sites | 20.000 | | | | | | | | |
| | 3.1.4 Facilitation in providing infrastructure packages for climate-disaster risk reduction in mangrove areas; infrastructures: rob-resistant embankments | 155.211 | | | | | | | | |
| Output 3.2. Community income-generating and productive economic activities are increased | 3.2.1 Value chain development of smallholders' fishery products. | 4.848 | | | | | | | | |
| | 3.2.2 Facilitation of training packages for sustainable smallholder fisheries and livelihood: good practices on fisheries cultivation; diversification of products/processing; marketing. | 5.888 | | | | | | | | |
| | 3.2.3 Facilitation small-scale business licensing and product certification | 4.404 | | | | | | | | |
| | 3.2.4 Procurement of equipment for productive economies and businesses i.e. production machines, packaging machines, etc. | 12.000 | | | | | | | | |
| | 3.2.5 Technical assistance for developing market-demand commodities and products | 2.744 | | | | | | | | |
| | 3.2.6 Facilitation on access to finance (including venture capital) to support communities' businesses by developing network or collaboration with banks or private sectors | 4.024 | | | | | | | | |
| | 3.2.7 Review best practices and lesson learned on alternative livelihood improvement | 8.092 | | | | | | | | |

PART IV: ENDORSEMENT BY GOVERNMENT AND CERTIFICATION BY THE IMPLEMENTING ENTITY

A. Record of endorsement on behalf of the government⁹

Provide the name and position of the government official and indicate date of endorsement. If this is a regional project/programme, list the endorsing officials all the participating countries. The endorsement letter(s) should be attached as an annex to the project/programme proposal. Please attach the endorsement letter(s) with this template; add as many participating governments if a regional project/programme:

| | |
|---|---------------------|
| H.Syahdan, ST, MT, Head of Regional Disaster Management Agency, Province of West Nusa Tenggara | Date: July 15, 2022 |
| Julmansyah, S.Hut, M.A.P, Head of Regional Office of Environment and Forestry, Province of West Nusa Tenggara | Date: July 15,2022 |
| Muslim, ST, M.Si, Head of Regional Office of Marine and Fisheries Province of West Nusa Tenggara | Date: July 15,2022 |

B. Implementing Entity certification

Provide the name and signature of the Implementing Entity Coordinator and the date of signature. Provide also the project/programme contact person's name, telephone number and email address

| | |
|---|--|
| <p>¹⁰ certify that this proposal has been prepared in accordance with guidelines provided by the Adaptation Fund Board, and prevailing National Development and Adaptation Plans (President Decree No. 16/2015; P.13/MENLHK/Setjen/OTL.0/1/2016; P.33/MENLHK/Setjen/Kum.1/3/2016; Indonesia Intended Nationally Determined Contribution/INDC; COP 21; Paris Agreement signed by Government of Indonesia; Book and Map of Information System of Vulnerability Index Data (SIDIK); Climate Change Adaptation National Action Plan) and subject to the approval by the Adaptation Fund Board, <u>commit to implementing the project/programme in compliance with the Environmental and Social Policy of the Adaptation Fund</u> and on the understanding that the Implementing Entity will be fully (legally and financially) responsible for the implementation of this project/programme.</p> | |
|  | |
| <p>Laode M Syarif Executive Director of Kemitraan Implementing Entity Coordinator</p> | |
| Date: July 15, 2022 | Tel. and email: +62-21-2278-0580 Laode.syarif@kemitraan.or.id |
| Project Contact Person: Hasbi Berliani | |
| Tel. And Email: +62-21-2278-0580, +62 812-3752-077; Hasbi.berliani@kemitraan.or.id | |

⁹ Each Party shall designate and communicate to the secretariat the authority that will endorse on behalf of the national government the projects and programmes proposed by the implementing entities



KEMENTERIAN LINGKUNGAN HIDUP DAN KEHUTANAN
DIREKTORAT JENDERAL PENGENDALIAN PERUBAHAN IKLIM

Alamat : Gedung Manggala Wanabakti, Blok VII Lantai 12, Jl. Gatot Subroto – Jakarta 10270
Telp. : +62 21 5730144 Fax. : +62 21 5720194

Website : <http://ditjenppi.menlhk.go.id>

email : tusetditppi@gmail.com

Nomor : S. 201/PP1/AP1/PP1.018/2022
Sifat : Biasa
Lampiran : 1 berkas
Hal : **Dukungan untuk Proposal Inovasi AF dan Perubahan Implementasi Proyek di Pekalongan**

5 Agustus 2022

Yth. Direktur Eksekutif Kemitraan
di -
tempat

Merujuk surat Saudara nomor K344/SKB/SGS/Agu/2022 tanggal 1 Agustus 2022 Hal Permohonan Surat Dukungan untuk 10 Concept Note Terpilih Proyek Adaptation Fund Batch II, disampaikan beberapa hal sebagai berikut:

1. Pada dasarnya kami selaku *National Designated Authority* Adaptation Fund dapat menyetujui 10 concept note AF Batch II dengan catatan sebagai berikut:
 - Setiap concept note yang telah terseleksi harus mendukung pencapaian target ketahanan dalam NDC dan sejalan dengan Rencana Strategi Kementerian LHK 2020-2024, serta mempunyai target capaian kuantitatif agar terukur
 - Setiap *concept note* yang terseleksi agar diarahkan untuk mendukung pencapaian target 20.000 Program Kampung Iklim (Proklim) tahun 2024. Oleh karena itu, setiap *concept note* yang terseleksi dapat diberi target registrasi Proklim sebanyak 100 lokasi
2. Kriteria tersebut agar menjadi catatan pada saat pendetilan *concept note* menjadi proposal kegiatan
3. Terlampir disampaikan *endorsement letter* untuk 10 *concept note* proyek AF batch II.

Demikian disampaikan, atas perhatian dan kerjasamanya diucapkan terima kasih.

Direktur Jenderal
selaku National Designated Authority
Adaptation Fund Indonesia

Ir. Laksmi Dhevanthi, MA., IPU.
NIP.196503231992032001





MINISTRY OF ENVIRONMENT AND FORESTRY
DIRECTORATE GENERAL OF CLIMATE CHANGE

Manggala Wanabakti Building Block VII 12th Floor, Jalan Gatot Subroto – Senayan, Jakarta 10270
Phone +62 21 5730144 Fax. : +62 21 5720194

Website : <http://ditjenppi.menlhk.go.id>

email : tusetditppi@gmail.com;

Our Ref. : *S. 282/PP1/ARI/PP1.0/8/2022*
Attachments :
Subject : Letter of endorsement

Jakarta, 5 August 2022

To:
The Adaptation Fund Board
c/o Global Environment Facility
Mail stop: N 7-700
1818 H Street NW
Washington DC 20433, USA

Dear Board Member,

Directorate General of Climate Change Ministry of Environment and Forestry as the National Designated Authority of Adaptation Fund in Indonesia through *Kemitraan* – Partnership for Governance Reform as the National Implementing Entity, have received and appraised 37 incoming concept notes.

After a thorough assessment process of the incoming concept notes, we come to the decision that the following 10 (ten) concept notes from 10 (ten) different organizations have met and are in accordance with the national priorities in the implementation of adaptation programs and activities to increase adaptive capacity and to reduce the impact and risks of climate change in vulnerable regions in Indonesia:

1. Yapeka; *Ecosystem-based Adaptation to Support Climate Resilience in Coastal and Small Islands of Rote Ndao and Sabu Raijua Districts in the Savu Sea*
2. TLKM; *Sustainable Landscape Governance; Towards Climate Resilience of Community in Tempe Lake Ecosystem*
3. KAPASITAS; *Adaptation to climate change through integrated forest management and sericulture business to achieve ecosystem resilience to food security for the Lake Tempe Catchment Area Community*
4. Garis Biru; *Strengthening the Adaptive Capacity of Coastal Village Communities in Supporting Food Security as a Response to Climate Change Through Stakeholder Elaboration Actions in West Sulawesi Province*
5. Sajogyo Institute; *Collaboration for the Conservation of Cimandiri Watershed Landscapes through the Potential of Silvopasture and Community Agroforestry*
6. KOAKSI; *Building Climate Resilient District in Indonesia: Case of Sigi District*
7. KEMITRAAN; *Village Based Coastal Adaptation and Resilience in Lombok Province of West Nusa Tenggara*
8. HUMA; *Change Climate and Adaptation in the Buffer Area of the New National Capital*
9. Mitra Aksi; *Increasing the resilience of smallholders from climate impacts through Smart Agriculture based on Livelihood Diversification in Indonesia*
10. KUAT (KARSA); *Strengthening Community Adaptation toward Climate Change through ProKlim in Ecoregion Neck of Sulawesi Island*

With this consideration, and in my capacity as the National Designated Authority of Adaptation Fund in Indonesia, I recommend the above proposals be granted support from the Adaptation Fund Board. All those programs will be executed by each of the submitting entities under the supervision of *Kemitraan* – Partnership for Governance Reform.

Sincerely Yours,



Laksmi Dhewanthi
Director General of Climate Change
Ministry of Environment and Forestry
as Indonesia Designated Authority of Adaptation Fund

Copy to:
Kemitraan (Partnership Governance Reform in Indonesia)

Appendix List:

Annex 1. Letter of Support from the West Nusa Tenggara Provincial Government, and Letter of Potential Joint Financing Support

Annex 2. ~~Environmental and Social Management Plan~~

Annex 3. Gender Assessment in Project Location

Annex 4. Report on Social-Economic Study and Vulnerability to Climate Change Disasters in The Coastal Areas of Lombok

Annex 5. Documentation of Stakeholder Consultation

Annex 6. Operational Definitions

Annex 7. Core Outcome Indicator from the Fund's Results Framework

Annex-8. ~~Gender Action Plan~~

Annex-9. Risk Identification in Activities That have a Significant Impact

Commented [SM10]: pindahkan menjadi Annex 2

Commented [SM11]: Jadikan annex dengan menambahkan informasi tentang align dengan output project dan anggaran

Annex 1. Letter of Support from the West Nusa Tenggara Provincial Government, and Letter of Potential Joint Financing Support

PEMERINTAH PROVINSI NUSA TENGGARA BARAT
BADAN PENANGGULANGAN BENCANA DAERAH
 Jln. dr Soepono Lingkar Selatan Telp./Fax (0370) 646972 Mataram (83010)

LETTER OF SUPPORT
 Number : 350 / 56 /BPBD.NTB/VII/2022

Responding a letter from the Transform organization, a member of the Lombok Climate Change Consortium, for the ideas for tackling rob and its impact in West Lombok Regency, we hereby express our support for the Proposed Program (Concept Note) entitled "Village Based Coastal Adaptation and Resilience in Lombok, Province of West Nusa Tenggara" proposed to the Programme Funding for Adaptation Fund

We consider this activity very important and strategic in supporting the local government's efforts to reduce the risk of tidal flooding and create a disaster-resilient community in West Nusa Tenggara Province.

Thus, we convey this Letter of Support, and we hope that it will become part of the strategic considerations of the proposals submitted to the Programme Funding for Adaptation Fund.

Mataram, 15 July 2022
 Head of Regional Disaster Management Agency
 Province of West Nusa Tenggara,

 H. Suldan, ST.MT.
 NIP. 19641231 198503 1 140

PEMERINTAH PROVINSI NUSA TENGGARA BARAT
DINAS LINGKUNGAN HIDUP DAN KEHUTANAN
 Jl. Majapahit No. 54, Mataram-NTB, 83126. Telepon: (0370) 638071

LETTER OF SUPPORT
 Number : 050/5405/Sekret-DISLH/2022

Responding a letter from the Transform organization, a member of the Lombok Climate Change Consortium, for the ideas for tackling rob and its impact in West Lombok Regency, we hereby express our support for the Proposed Program (Concept Note) entitled "Village Based Coastal Adaptation and Resilience in Lombok, Province of West Nusa Tenggara" proposed to the Programme Funding for Adaptation Fund

We consider this activity very important in supporting local government efforts to create community resilience through the climate village program (Praklim) which has been carried out by the Environment and Forestry Office in West Nusa Tenggara Province.

Thus, we convey this Letter of Support, and we hope that it will become part of the strategic considerations of the proposals submitted to the Programme Funding for Adaptation Fund.

Mataram, 15 July 2022
 Head of the Regional Office of Environment and Forestry
 Province of West Nusa Tenggara,

 Zulmansyah, S.Hut.M.A.P.
 NIP. 19740701 200212 1 005

PEMERINTAH PROVINSI NUSA TENGGARA BARAT
DINAS KELAUTAN DAN PERIKANAN
 Jalan Samudra Nomor 3 Mataram Kode Pos 83122
 Telpun (0370) 632083 Faks. (0370) 623963
 Email : ditukamb@dnpp.go.id Website : ditukamb.ntprov.go.id

LETTER OF SUPPORT
 Number : 575/146.1/DP/401/KLW/12423

Responding a letter from the Transform organization, a member of the Lombok Climate Change Consortium, for the ideas for tackling rob and its impact in West Lombok Regency, we hereby express our support for the Proposed Program (Concept Note) entitled "Village Based Coastal Adaptation and Resilience in Lombok, Province of West Nusa Tenggara" proposed to the Programme Funding for Adaptation Fund

We consider this activity very important in supporting local government efforts to create community resilience and in the same time improve their livelihood in facing climate change in Province of West Nusa Tenggara.

Thus, we convey this Letter of Support, and we hope that it will become part of the strategic considerations of the proposals submitted to the Programme Funding for Adaptation Fund.

Mataram, 15 July 2022
 Head of the Regional Office of Marine and Fisheries
 Province of West Nusa Tenggara,

 Muslim, ST.MSi
 Pembina Tk. I IVb
 NIP. 197606012001121009

PROVINCIAL GOVERNMENT OF WEST NUSA TENGGARA
REGIONAL DEVELOPMENT PLANNING AGENCY (BAPPEDA)
 Address : Jl. Patungge No. 2, Mataram Kota Pos 83101. Telpun/Fax: (0370) 631081
 Email : bappeda@ntbprov.go.id Website : bappeda.ntbprov.go.id

Mataram, 5 January 2023

Number : 050 / 24 / 01-Bappeda
 Attachment : -
 Re : Recommendation for Adaptation Fund Batch II 2022 Proposal

Attention to:
 The Adaptation Fund Board
 Secretariat 1818 H Street NW
 MSN N7-700, Washington, D.C., 20433 U.S.A.

Dear Sir/Madam,

I hope my letter finds you in a good health and happiness. First of all, I would like to introduce myself. I am Iswandi, I work as the head of the Regional Development Planning Agency (Bappeda) of West Nusa Tenggara (NTB) Province, Indonesia. Our development planning trajectories aim to integrate the concept of sustainability for bringing more prosperity for the society in terms of economic, social, and environmental benefits. This will contribute to the global Sustainable Development Goals, especially Goal Number 13 regarding climate change. In doing our actions for mitigation and adaptation of climate change, we work together and form partnership with society, non-government organizations, academics, media, and other institutions.

The government of NTB Province has enacted the Local Regulation Number 2 Year 2021 regarding the Regional Medium-Term Development Plan (RPJMD) Year 2019-2023 of the West Nusa Tenggara Province. This RPJMD act as a guideline for all government departments and non-government organizations in undertaking development programs and activities to achieve the development goals. However, in undertaking the development programs, especially climate-related programs, financing is one of the challenges. Therefore, to support climate financing, it is important to have creative and innovative financing that can help all local actors to work together for the benefits of the society.

Further, I have discussed the proposal for climate adaptation fund with Lombok Climate Change Consortium, with the title "Village-Based Coastal Adaptation and Resilience in Lombok Province of West Nusa Tenggara". This great idea helps to accelerate the village development and form resilience to reduce the impacts of climate change in the society. This will contribute to reduce the impacts of climate change and promote a sustainable and inclusive development in West Nusa Tenggara Province. Our climate-related development programs are aligned with the Consortium proposal. Further, it will lead to more productive collaboration to achieve the SDGs and society welfare. The list of potential programs and activities for alignment with coastal climate adaptation program is attached in the annex.

In conclusion, I fully support this proposal to receive the grant from Adaptation Fund Batch II. If you have any questions regarding this, I am happy to discuss this further with you, by email: i.iswandi@bappeda.go.id, or +62 811 39463080. Thank you very much for your attention and I look forward to more productive collaboration for climate change programs in the near future.


 Head of Bappeda of NTB Province,
 Dr. Ir. H. ISWANDI, M.Si
 NIP. 19651221 199403 1 153

CC to:
 1. Governor of West Nusa Tenggara Province.



PROVINCIAL GOVERNMENT OF WEST NUSA TENGGARA
REGIONAL DEVELOPMENT PLANNING AGENCY (BAPPEDA)
Address : Jl. Flamboyan No. 2 Mataram Kode Pos 83126, Telepon/Faksimile (0370) 631581
Email : bappeda@ntbprov.go.id Website : bappeda.ntbprov.go.id

ANNEX: NTB PROVINCIAL GOVERNMENT PROGRAMS IN LINE WITH
THE PROPOSAL OF ADAPTATION FUND YEAR 2023

| No | Name of Program | Activities | Budget (USD) | Leading Sector |
|----|---|--|--------------|---------------------------------|
| 1 | Marine, coastal and small islands management | Coastal community empowerment | 8,887 | Marine and Fisheries Office |
| 2 | Fisheries and aquaculture management | fish farming techniques, processing and marketing | 34,973 | Marine and Fisheries Office |
| 3 | Development of Tourism Resources and Creative Economy | Implementation of Human Resource Capacity Building in Tourism and Creative Economy | 9,130 | Tourism office |
| 4 | Watershed Management | Application of soil and water conservation techniques | 13,220 | Environment and Forestry Office |
| | Amount | | 66,277 | |

Head of Bappeda of NTB Province,


Dr. Ir. H. ISWANDI, M.Si.
NIP. 19651231 199403 1 153

Annex 2. Environmental and Social Management Plan

Commented [SM12]: pindahkan menjadi Annex 2

| <u>ESP Adaptation Fund Principle</u> | <u>Possible Risks and Impacts</u> | <u>Action and Mitigation Measures</u> | <u>Target or MoV</u> | <u>Assigned Persons/Units</u> |
|--|--|--|---|-------------------------------|
| Compliance with law | <ul style="list-style-type: none"> ▪ The project is not complied with the relevant laws | <ul style="list-style-type: none"> • Permit for the use of coastal areas to the NTB Provincial Marine Service by attaching an application letter, technical plan for planting and recommendations from the village/sub-district government • The project ensures the suitability of the location in accordance with the RTRW of West Lombok Province and Regency • The project ensures the location is included in the area for mangrove rehabilitation | <ul style="list-style-type: none"> • Permit for the use of coastal areas to the NTB Provincial Marine Service • Documentation and Minutes of Meeting • The project ensures the location is included in the area for mangrove rehabilitation | PMU, Field Facilitator |
| Marginalized and Vulnerable Groups | <ul style="list-style-type: none"> ▪ Marginalized and vulnerable groups felt excluded and do not have the opportunity to participate in the project. | <ul style="list-style-type: none"> ▪ Ensure participation of marginalized and vulnerable groups (if relevant) in project activities. | Documentation of inventory report of affected communities | PMU, Field Facilitator |
| Gender and Women Empowerment | <ul style="list-style-type: none"> ▪ Low participation of women in project activities due to various factors ▪ Fewer opportunities for women compared to men, influenced by prevailing cultural norms, which may limit women's engagement in project interventions that are otherwise open to their participation. ▪ | <ul style="list-style-type: none"> ▪ Ensure consistent and balanced participation of both women and men in all project activities; ▪ Actively encourage women's involvement in all relevant aspects of the project interventions (training, workshops, discussions) ▪ Ensure that women's perspectives are equally valued, and that they have the right to express their ideas freely, without pressure, discrimination, or intimidation from men or the wider community. | <ul style="list-style-type: none"> ▪ Women's participation in relevant project-related training activities is targeted to reach up to 30% of total participants. ▪ Meeting minutes and documentation will record instances where women actively participate in project interventions or meetings, ensuring their involvement is voluntary and free from any community pressure or coercion. | PMU, Field Facilitator |
| Pollution prevention and resource efficiency | <ul style="list-style-type: none"> ▪ Dust pollution due to the entry and exit of operational vehicles carrying project materials ▪ Noise pollution – the impact of the movement of vehicles when transporting materials and tools to the project site. ▪ Waste generated from the improvement of rob-resistant embankments. | <ul style="list-style-type: none"> ▪ Conduct regular watering at project sites affected by dust. ▪ Obtain consent from potentially affected communities before beginning embankment improvement. ▪ Provide dust masks to community members to reduce the impact of dust exposure. | <ul style="list-style-type: none"> ▪ Documentation of activities and the management of waste materials. ▪ Obtain consent from local communities regarding the planned improvement of the embankments. | PMU, Field Facilitator |

Annex 3. Gender Assessment in Project Location

GENDER STUDY REPORT

Results of Rapid Assessment of Disaster Risks Due to Climate Change and Related Matters, as well as the Potential for Gender-Responsive Adaptation in the Southern Part of West Lombok Region

1. INTRODUCTION

1.1. Background

Climate change is a phenomenon whose impacts have begun to be felt worldwide. The alteration in natural conditions, exacerbated by human activities that are detrimental or damaging to the environment, has also been felt. Lombok Island, which exhibits diverse natural characteristics including various climates, has areas that are vulnerable to the impacts of climate change. Coupled with the poverty conditions of the inhabitants in these vulnerable areas, this situation exacerbates their livelihoods.

The diversity of communities and their livelihoods in each region must recognize their differences. They are not homogeneous societies, thus having different capacities to confront the impacts of climate change and other changes that worsen the effects of climate change on communities. This diversity includes gender, disabilities, age, health conditions, welfare, religion, ethnicity, and so forth.

Climate change has severe implications for communities in general. However, these effects will be more pronounced for women and other vulnerable groups due to the limitations caused by patriarchal cultures. Therefore, initiatives are needed to assist communities, especially women and other vulnerable groups, in becoming more resilient to the impacts of climate change and related challenges. Initiatives to enhance the adaptation capacity of these populations are with the hope of a fairer and more equitable community by ensuring equal opportunities for all communities in enhancing adaptation capacity.

To gain a deeper understanding of vulnerability based on a gender perspective and other vulnerable groups, a rapid assessment was conducted on the disaster risks due to climate change and related aspects, as well as the potential for gender-responsive adaptation. Based on the findings of previous studies, the southern region of Lombok Island is one of the most vulnerable areas to the impacts of climate change, including the southern part of West Lombok Regency. Therefore, this study was conducted in this particular region.

1.2. Objective

The objective of this study is to obtain baseline data regarding the conditions of disaster risk due to climate change and related aspects, as well as the potential for gender-responsive adaptation, including:

- Gender characteristics and vulnerable groups
- Income and family income management from a gender perspective
- Disaster risks and responses from a gender perspective
- Survival strategies and disaster adaptation
- Gender roles in existing institutions and development programs

1.3. Urgency of GEDSI study outcomes in this project going forward

The outcomes of this study will be extremely beneficial for community development programs, especially those related to the adaptation of climate change impacts and associated issues. This study helps to ensure interventions are more suitable to the community's needs, as viewed through the lens of gender and marginalized or vulnerable groups. This gender study will assist in identifying project/program-related risks concerning gender equality and women's empowerment, including elaborating on specific gender cultures and norms where the project will operate. The study also provides the potential differences in gender impacts from the intended adaptation activities. Responsive gender consultations, identifying primary gender goals and target groups, formulating gender-responsive project indicators, and conducting gender assessments in the project development phase are essential. By considering the diversity of communities in terms of gender, disabilities, ethnicity, age, religion, poverty, and others, efforts to enhance community adaptation capacity to climate change are expected to be more equitable and widespread.

2. IMPORTANCE OF GENDER ASPECT IN CLIMATE CHANGE ADAPTATION

This section refers to: Guidance Document for Implementing Entities on Compliance with the Adaptation Fund Gender Policy (Updated 2022).

3. METODOLOGY

- Study Methodology

The methodology used in this study is qualitative descriptive, aimed at providing descriptions related to phenomena examined from the perspective of gender and other vulnerable groups.

- Study Location

This study is conducted in 4 (four) villages: Cendi Manik, Central Sekotong, West Sekotong, and South Lembar.

- Participants

Respondents in the survey and informants in the FGD consist of representatives from diverse community groups, including different genders, people with disabilities, youth, and ethnicities.

- Types of Data

The data collected in this study include both quantitative and qualitative data.

- Data Collection Techniques

Secondary data are obtained from institutions and online sources. Primary data, on the other hand, are acquired through survey techniques (interviews), focus group discussions (FGDs), and observations.

- Data Analysis

The data are qualitatively analyzed to capture general phenomena and elaborate on variations occurring within them.

4. STUDY RESULTS

Based on the study conducted considering gender aspects, vulnerable groups, and marginalized communities, below are a few identified components:

4.1. Characteristics of the community from the perspective of gender, age, ethnicity, and religion

The available secondary data is relatively limited when viewed from the perspective of gender and marginalized groups. In this study, the available secondary data in the studied villages are based solely on gender (sex). However, data on the number of poor populations, ethnicity, and religion are only available in a few surveyed villages and can be accessed at the village office. Cendi Manik village is the only one that has begun to record the number of disabled people, but it is still in the process of data collection at the time of the study, hence not yet accessible.

Table 1. Population Data based on Gender, Household Poverty Status, Religion, and Ethnicity

| Village | Gender (number of people) | | Population in Poverty (households) | Religion (number of people) | | | | Ethnicity | |
|------------------|---------------------------|--------|------------------------------------|-----------------------------|-----------|-------|-------|-----------|-----------|
| | Male | Female | | Islam | Protestan | Hindu | Budha | Sasak | Non-Sasak |
| Cendi Manik | 2831 | 2868 | 3126 | 6699 | 0 | 0 | 0 | 5648 | 51 |
| South Lembar | 5422 | 5301 | ? | 10669 | 16 | 38 | 0 | ? | ? |
| Central Sekotong | 4664 | 4699 | ? | ? | ? | ? | ? | ? | ? |
| West Sekotong | 1987 | 2071 | ? | 8302 | 5 | 471 | 3 | ? | ? |

Source : Secondary Data 2020

Based on the secondary data available in the studied villages, there are slight differences in the population by gender. Among the four studied villages, only South Lembar has a smaller population of females compared to males. Only Cendi Manik has data on poor households, totalling 3126 households. Regarding religious affiliation, Islam is the majority religion in all villages, while minority religions include Protestantism, Hinduism, and Buddhism. In terms of ethnicity, the majority are Sasak. Meanwhile, the minority ethnicities include non-Sasak groups, consisting of Javanese, Bima, Padang, and Sumbawa ethnicities.

4.2. Household income and income management from a gender perspective

In this study, it was identified that men are considered as the backbone and main earners of the family. If there is income from household members such as the wife, children, or others, they are seen as additional earners in the household. Table 2 below provides an overview of the dominance of men and women in terms of primary and additional income earners, as well as dominance in several income sources based on gender perspective and other vulnerable groups. Below is the detailed analysis of the survey results regarding household income:

a. Head of household and primary and secondary household income sources.

For income sources, several gender, disability, and social inclusion phenomena were identified in this study. Like in many patriarchal societies, the communities in the studied villages are also patriarchal. Men are considered to be the main breadwinners of the family, except for when the mother is the head of the household. Women consider themselves primarily as housewives, and their income is seen as additional earnings, as working for a living is considered a secondary job outside the duties of a housewife. Women or wives play a role in managing the family's finances from all sources of income. This money is managed for the family's consumption needs and children's school expenses. More details are outlined in Table 2 below.

Table 2. Table of Dominance in Household Income Providers Generally Based on Gender and Types of Vulnerable/Marginal Groups

| Dominance Type | Male | Female | Disabled | Youth | Other | Notes |
|------------------------------|------|--------|----------|-------|-------|--|
| Main household income earner | | | | | | For female household heads, women are considered the primary earners |
| Household income manager | | | | | | |
| Additional/ side income | | | | | | Others can include a child or other family members living in the same household. |

The data is processed from the survey. The color of the boxes indicates the dominant groups

When managing household domestic affairs, women usually bring their children to work if their job is flexible and allows them to do so, for instance, when selling goods at tourist spots. If their work does not allow them to bring their children, they leave them with grandparents or their husband (the child's father) when the husband is not working. However, if there is no place to leave the child because they are too young, the mothers will not take that job. When the children are older and can stay at home playing with their friends, then the mothers can take part-time work. Additionally, wives usually wake up early to cook for their families before they leave for work.

Similarly, for teenagers or young adults, they are not considered the breadwinners of the family if their father can still work. The role of teenagers or young adults in earning a living is similar to that of wives, as contributors to additional income. For young adults, they prefer to seek alternative jobs outside the family business because if they work in the family business, they do not receive an income (they are not paid). If they work outside the family business, they can earn money. Many young adults work outside agriculture and fisheries. They work in shops, as migrant workers, in mines, and in online sales. However, there are quite a few unemployed young adults because they do not have any skills. When they feel the need to find a source of income, they take odd jobs as farm labourers or fishermen, or go fishing for fish or crabs. In the past, many young people worked at sea, but now, they are more interested in working as gold miners. However, working as a miner does not necessarily make them prosperous. They might be able to build a house by working as migrant labourers, but working in the mines is sufficient for daily living expenses.

b. Marine sector

The primary and most commonly pursued livelihood of the community in the study area is as fishermen, considering their residential location in a coastal area. The following Table 3 presents details of the occupations in the marine sector and their dominance based on gender and vulnerability group types.

Table 3. Table of Dominance of Household Income in the Marine Sector based on Gender and Vulnerable/Marginal Group Types.

| Dominance Type | Male | Female | Disabled | Youth | Others | Notes |
|-----------------------------------|------|--------|----------|-------|--------|--|
| Fisherman | | | | | | Although rare, there are also males with disabilities who become fishermen |
| Collecting shells, shrimps, crabs | | | | | | Although not dominant, other types of groups also collect |
| Selling marine products | | | | | | |

Note : The data is processed from the survey. The color of the boxes indicates the dominant groups

The work of fishing at sea is primarily done by men within the family, while women sell the marine produce in the market, such as acting as collectors, retailers, or selling directly to consumers. Women are most dominant in collecting shells, shrimps, or other pond products. They also catch these products at the

shoreline during low tide. These products are sold when they have a considerable amount (at least 1 kg). They also consume the catch when the quantity is small or when they need food for their family.

In this study, there are disabled groups who also earn income from this sector. In the villages under study, there are disabled individuals engaged in fishing and have access to government assistance. In Cendi Manik, there are disabled individuals actively involved in tourism activities and other community engagements. Although the participation of disabled individuals in these activities is relatively limited and scarce, the study identifies that some disabled individuals access several available jobs, albeit limited ones.

c. Agriculture and Livestock Sector

For the agricultural and livestock sector, both men and women play roles in these activities. Further details regarding dominance data can be observed in Table 4 as follows:

Table 4. Table of Dominance of Household Income Sources from Agricultural and Livestock Sector by Gender and Types of Vulnerable/Marginal Groups

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|--|------|--------|----------|-------|--------|--|
| Large livestock farming (cattle and goats) | | | | | | Women are dominant except for female heads of households |
| Small livestock farming (chickens, ducks and others) | | | | | | |
| Selling large livestock (transactions) | | | | | | |
| Determining the price | | | | | | |
| Selling small livestock | | | | | | |
| Cultivating agricultural products | | | | | | There is a labour allocation based on the physical work burden |

The data is processed from the survey. The color of the boxes indicates the dominant groups

In the livestock sector, there's little variation in the roles of men and women. In some villages, men predominantly take care of and sell cattle. Meanwhile, women assist their husbands in livestock care when their husbands are away fishing or not at home. Although men usually meet middlemen or buyers for the sale of cattle, the pricing decisions are mutually agreed upon between husband and wife within a farming family. In certain villages and cases where women are the heads of households, they play a major role in raising the family's livestock and participate in deciding when to sell the animals.

Livestock farming is considered a form of savings for families in the study area. Livestock such as cows, goats, chickens, and ducks are raised. These animals are usually sold when the family needs money, especially during disasters or when there's no income from their primary or side jobs. Larger livestock like cows or goats are sold with the agreement of both spouses or the family when there's a need for significant expenses, such as for a child's wedding or higher education (university). Smaller animals are sold when the family lacks income for daily needs.

On the other hand, staple crop farming is usually for the family's consumption. However, in some areas where the production is limited (such as hillside rice farming with minimal yields), the harvest is solely sufficient for the family's consumption. Both men and women are involved in the cultivation (from land preparation to harvesting) and sale of food crops. Men typically negotiate with middlemen for the sale of the produce, while women manage the sales proceeds for the family's needs.

d. Tourism and Micro, Small, and Medium Enterprises (MSMEs) Sector

Most types of livelihoods are predominantly dominated by men. However, in the micro, small, and medium enterprises (MSMEs), women dominate this sector. Working as small-scale traders at home or mobile sellers, retail sellers at markets, culinary businesses, laundry services, and being traders in coastal/ponds/mangrove tourism areas are the jobs undertaken by women and young women. In some of the studied villages, several young women already have online businesses.

Detailed research findings are presented in the following Table 5.

Table 5. Table of Dominance of Household Income in MSMEs Activities and Tourism Sector Based on Gender and Types of Vulnerable/Marginal Groups

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|--------------------------------|------|--------|----------|-------|--------|-------|
| Coarse salt pond | | | | | | |
| Fine salt pond | | | | | | |
| Home-based/mobile small trader | | | | | | |

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|-------------------------|------|--------|----------|-------|--------|---|
| Online sales | | | | | | |
| Culinary business | | | | | | |
| Laundry | | | | | | |
| Craftsperson | | | | | | |
| Trader in tourist areas | | | | | | People with disabilities and youth also get access to this job type |

The data is processed from the survey. The color of the boxes indicates the dominant groups

In some of the studied villages (not all villages), women are also salt farmers and craftswomen. Regarding salt farming, women tend to choose the fine salt farming business as it's physically lighter compared to the coarse salt farming, which is primarily done by men. The income generated from fine salt farming is considerably lower than that from coarse salt farming. For instance, in a day, women can earn between 120,000 to 150,000 by selling 4-5 kilograms of fine salt to a local salt cooperative. On the other hand, in coarse salt farming, men in a group of 12-14 people can produce 3 tons of coarse salt per month, earning a total income of around Rp 12 million. Unfortunately, in other villages, many salt farms have been damaged and permanently closed due to flooding disasters.

In some studied villages, the income of salt farmers, especially women farmers, comes from profit-sharing with the owners of the salt farm land. These salt farms are not actually owned by the farmers themselves. Their status is as cultivators, where their salt production is divided into an 80:20 ratio, with 80% going to the cultivators and 20% to the landowners.

The tourism sector, especially mangrove and coastal tourism, serves as a secondary livelihood source for many fishermen along the coasts of Lembar and Sekotong Districts. This sector provides opportunities for all segments of society to participate in generating income. Men, women, people with disabilities, and youth are identified as accessing and working in this sector in several surveyed areas.

However, in Cendi Manik Village, the mangrove tourism managed by young people collapsed and ceased operation due to a lack of understanding about tourism management, especially in maintaining tourist facilities. As a result, young men who previously had income sources from the mangrove shifted to becoming fishermen or traditional miners. Meanwhile, young women chose to engage in micro, small, and medium enterprises (MSMEs), participate as social activity cadres (posyandu), or remain unemployed at home (not contributing to family income). Meanwhile, in other coastal villages, coastal and mangrove tourism continue to be income sources for various community groups.

e. Other Service Sectors

The job of service labourers in several sectors is a type of work accessed by both men and women in the target areas of the study. The types of labourer jobs vary depending on the potential available in the surveyed villages. Some work as farm labourers, construction labourers, sanitation workers, and salt packaging labourers. More detailed aspects of this are presented in the following Table 6.

Table 6. Table of Dominance of Household Income Generation in Micro, Small, and Medium Enterprises (MSMEs) and Tourism Sectors Based on Gender and Types of Vulnerable/Marginal Groups

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|--------------------------------|------|--------|----------|-------|--------|---|
| Coarse salt pond | | | | | | |
| Fine salt pond | | | | | | |
| Home-based/mobile small trader | | | | | | |
| Online sales | | | | | | |
| Culinary business | | | | | | |
| Laundry | | | | | | |
| Craftsperson | | | | | | |
| Trader in tourist areas | | | | | | People with disabilities and youth also get access to this job type |

The data is processed from the survey. The color of the boxes indicates the dominant groups

Although some fields of work are dominated by male labourers, women can still work in these sectors. Jobs requiring physical strength, such as transporting goods, are typically dominated by men. Women usually engage in tasks considered physically "lighter."

Payment standards vary based on the type of work and the duration of work hours or production targets. Jobs requiring lighter physical exertion usually have lower payment standards compared to physically

demanding work, which is predominantly carried out by women. Conversely, physically demanding jobs command higher payments, and these roles are mostly occupied by men.

One common service job performed by men in the study area is working as traditional gold miners. Women do not work in this field due to its remote and physically demanding nature. This occupation is considered to only meet daily needs when the primary job fails to provide sufficient income. Additionally, mining jobs do not provide enough to enable workers and their families to thrive (expressed as "unable to build a house").

A popular choice of work for both men and women in the study area is to become migrant workers or Indonesian Migrant Workers (TKI). Both genders opt for migrant work because it allows them to earn more money, enabling them to buy property or assets like land or houses. When jobs available in the village are deemed insufficient to sustain their livelihoods, residents, including young people, opt to work abroad as migrant labourers.

4.3. The Community's Perception of Climate Change-Induced Disaster Risks and Responses from the Gender and Vulnerable Groups' Perspectives

Tidal flooding is the most frequent natural and hydrological disaster experienced by coastal area residents across all villages in this study. Tidal flooding is intensified by floods resulting from rainfall or river overflow. Its consequences in some villages can lead to flash floods and economic losses for affected communities. Damaged buildings, destroyed fish ponds with their yields swept away, unproductive agricultural and plantation lands (with a productivity decrease of up to 75%) due to high salt content in inundated areas are among the impacts caused by tidal flooding and floods.

Aside from tidal floods and floods, they also encounter several hydrological disasters. During the dry season, some villages in this study face drought for several months every year. This drought significantly affects their agricultural, livestock, and fish farming activities.

According to respondents and informants, these disasters are becoming more frequent compared to 20-30 years ago. Moreover, the weather is increasingly unpredictable, making it difficult to foresee the timing and duration of disasters. Although tidal floods occur in almost every village, the frequency varies, happening between 2 times a year to every month. Similarly, the unpredictable bad weather continues to pose challenges. Even though it lasts for 3 (three) months, during this period, there are 2 days of bad weather, 1 day of good weather, and it's often unpredictable when it will occur. Heavy rainfall also contributes to frequent flooding and landslides. The impact of these disasters (rob, floods, drought, bad weather) is exacerbated by human activities. For example, the current increase in "rob" frequency and its disturbance to the residents' livelihoods is attributed to coastal land reclamation carried out by companies near the port areas.

Table 7. The dominance related to vulnerability to hydrological disasters and the role of preparedness from the perspective of gender and vulnerable/marginalized groups

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|---|------|--------|----------|-------|--------|-------------------------------------|
| Vulnerability to hydrological disasters | | | | | | The elderly & children are dominant |
| Saving vulnerable residents | | | | | | Male youth |
| Saving large livestock | | | | | | |
| Unable to carry out livelihood activities | | | | | | |
| Household management becomes more difficult due to decreased income | | | | | | |
| Household water management during dry seasons | | | | | | |

The data is processed from the survey. The color of the boxes indicates the dominant groups

Based on the study presented in Table 7, the most vulnerable groups to hydrological disasters according to respondents and participants are children and the elderly, followed by sick/pregnant individuals, and then others. The population prioritizes rescuing those who may not be able to save themselves during a disaster. When tidal waves and floods occur, families are on alert to save their parents (the elderly) and children first, as they are considered less likely to rescue themselves quickly. Women are considered vulnerable because this group is deemed more prone to panic than men and young men.

Families with livestock typically relocate their animals to higher ground. They are concerned that their livestock might be submerged in floods or devoured by pythons. Usually, during floods or tidal waves, men in the family are predominantly responsible for relocating their livestock to safer areas, while women are

responsible for cleaning their flood-affected homes. This becomes more challenging in families where the head of the household are elderly women. Their livestock also needs to be relocated far away, which, from a gender perspective, burdens female farmers to transport their livestock to safe places far from their flooded homes.

During floods, flash floods, and tidal waves, women also lose their sources of livelihood, such as salt pond and mangrove businesses for collecting clams, shrimp, and crabs that are washed away. Flooded houses and impassable flooded roads hinder their job search. In agriculture, floods drastically decrease agricultural yields. Many agricultural lands can no longer be cultivated at all due to high salt content. This affects the livelihoods of both men and women who rely on farming and agricultural labour.

The increasingly severe economic impact is also felt by women during droughts for farmers and bad weather for fishing families. Main sources of income for daily sustenance are threatened. Women, as managers of family consumption, also contemplate how to fulfil the family's consumption needs. Especially when disasters like floods and tidal waves cause house flooding, and families have to stay alert at home to prevent water from rising, the family's economic activities are disrupted. This becomes even more challenging when these disasters are difficult to predict in terms of occurrence and duration, posing an increasing burden, especially for women as family financial managers.

Regarding droughts, the community's need to purchase water is as crucial as purchasing food. In this case, women face difficulties in disasters due to domestic needs that require a substantial amount of water. They must manage the family's water consumption while maintaining family sanitation with limited water supply.

For cases involving the impact of disasters in the study area (such as cases of sexual harassment, domestic violence, or child labour), further investigation was not carried out in-depth during the FGDs or surveys. From the questions asked, these issues do not seem to be considered crucial societal issues yet. Moreover, deeper studies are required for cases that are still considered taboo to discuss openly in the community. Secondary data also does not record these cases. However, according to the interviews, cases of child marriage still occur frequently.

4.4. Survival and Adaptation Strategies to Disasters from a Gender and Vulnerable Group Perspective

During floods, several livelihood activities come to a halt, while women take on the role of finding sources to continue providing food for their families. Floods are especially burdensome for those earning daily wages. If the floods last only a short while or a few hours, fishermen can still go out to sea or fish. Women can still gather shellfish. However, when floods or tidal surges last for an extended period, affected individuals reliant on daily income will lose their sources of livelihood. Therefore, to meet the daily consumption needs of the household, women become the backbone, especially since inhabitants express that they don't alter their dietary patterns and nutrition during disasters. Women fulfill these daily consumption needs through various strategies. These strategies are detailed in Table 8 below.

Table 8. Dominance Related to Vulnerability to Hydrological Disasters and the Role of Preparedness from the Perspective of Gender and Vulnerable/Marginalized Groups

| Dominance type | Male | Female | Disabled | Youth | Others | Notes |
|---|------|--------|----------|-------|--------|-------|
| Fish trading business in the market | | | | | | |
| Collecting clams, shrimps and mangrove products | | | | | | |
| Salt business | | | | | | |
| Selling/pawning non-cash savings assets | | | | | | |
| Accessing and utilizing SME loans | | | | | | |
| Borrowing rice to families/relatives | | | | | | |

The data is processed from the survey. The color of the boxes indicates the dominant groups

First, when the fishermen (men) are unable to go fishing, women or wives engage in fish trading. They buy fish in large quantities from traders coming from outside the village and sell them retail in the market or door-to-door among residents.

Second, they also gather shellfish, catch shrimp, and crabs in the mangrove swamps as a means of livelihood. They feel that the mangroves significantly support their livelihoods because these areas allow them to get more catches compared to when there are no mangroves. However, ownership of these mangrove areas is personal, so they solely rely on the available resources from these mangrove forests. Consequently, it's challenging for them to cultivate commodities that can thrive in the mangrove area.

Third, women who previously owned salt ponds are no longer able to produce salt due to the continuous occurrence of floods, which disrupts the traditional salt processing from coarse to fine salt and selling it in the market.

Fourth, another strategy involves selling their non-cash assets or savings, such as selling plates, small livestock (chickens or ducks), pawning or selling their gold, and household items that they can sell or pawn.

Fifth, women also access SME (Small and Medium Enterprises) credit. Women greatly benefit from credit from SME cooperatives like the "Mekar" Cooperative. This cooperative specifically caters to female borrowers because the goal of SMEs is to empower women's economy through SME development. If these women have previously borrowed, they will compensate the debt. Initially, the SME cooperative provided business management training and bookkeeping administration assistance to female customers. However, the cooperative lacks adequate support. Some women who borrowed from this cooperative used it for developing their SMEs. Nevertheless, frequent disasters result in loans being more directed toward meeting family consumption needs. To repay the cooperative loan, women rely on their husbands' income.

Lastly, if women cannot obtain loans from credit institutions, they borrow from family or close relatives. Usually, they borrow in the form of staple foods like rice. Borrowing from friends or relatives is relatively rare because they and their family or relatives are all victims of the disaster. Regarding disaster-related social assistance, participants in this study stated that they rarely receive external aid when facing disasters. This is because these disasters are routine and occur every month, limiting external assistance.

4.5. The Role of Gender and Vulnerable/Marginal Groups in Institutional and Development Programs

This study identifies several institutions and support programs involving women, young women and men, and vulnerable and marginalized groups in the study area. This is presented in Table 9 below.

Table 9. Dominance Related to the Gender Role and Vulnerable/Marginal Group in Institutions and Development Programs

| Dominance Type in Institutions | Male | Female | Disabled | Youth | Others | Notes |
|--|------|--------|----------|-------|--------|---|
| SMEs | | | | | | |
| Agriculture, fishery, farming | | | | | | |
| Celebrations & religious festivals (Maulid) | | | | | | |
| Integrated Health Service Post (Posyandu) | | | | | | Female teenagers do access although not dominant |
| Volunteers for disaster emergencies | | | | | | Male youth is dominant |
| Mangrove and coastal tourism | | | | | | People with disabilities do access although not dominant |
| Annual development program from government funds | | | | | | Public figures are usually involved in the planning and decision making (control) |
| Physical development and development that requires human physical labour | | | | | | |
| Social inclusion program | | | | | | Not available |
| Social Assistance | | | | | | Includes female heads of household |

The data is processed from the survey. The color of the boxes indicates the dominant groups

- a. In this study, the empowerment programs conducted in the research area include the empowerment of micro, small, and medium enterprises (MSMEs) through MSME cooperative programs, prominently mentioned by the target participants across all villages known as the "Mekar" Cooperative. Additionally, there are specific empowerment programs for women available only in select villages, such as the female small-scale salt producers' MSMEs supported by a local salt cooperative. Furthermore, there's the Women Farmers Group (Kelompok Wanita Tani - KWT) that received training and assistance for utilizing home gardens for cultivating vegetables and other backyard crops.
- b. In agricultural, fisheries, and livestock institutions, men take on dominant roles. Women usually assist at the household level in managing agricultural activities in a broader sense. Women and children are considered 'assistants' in this field.

- c. Some young women engage in social and community activities such as Posyandu (integrated health services post) and religious festival celebrations (Maulid, etc.). In formal institutions like Posyandu, the involvement of young people as cadres is limited due to many women marrying at a young age and focusing on their families. Cadres in Posyandu are usually dominated by adult women and female figures, for instance, members of women's organizations or social groups. Regarding social and religious festival events, more young people participate, albeit temporarily, mainly during the preparation and execution of the events. Afterward, it's challenging to gather them for volunteer activities as they are busy seeking livelihoods.
- d. Concerning youth organizations, some villages have disaster preparedness volunteer groups, predominantly comprising young men. However, the status of these organizations varies, with some remaining active and others not. Even in active groups like in Cendi Manik village, their optimal assistance is limited as they are occupied with rescuing and aiding their own affected families. The management of these youth-dominated institutions seems quite minimal. Training and mentoring are only received by a few villages, while in others, these institutions are lacking.
- e. Men, women, and individuals with disabilities (identified in some villages) have access and participate in institutions involved in tourism and mangrove fields. The government and other stakeholders have intervened in this sector's development, providing training and mentoring in certain villages. Social assistance, social activities, and social media groups have been accessed by everyone—men, women, and marginalized groups with internet literacy. They utilize and benefit from these social aspects.
- f. Regarding the annual development programs funded by the government, community aspirations and participation are inadequately considered based on gender and the vulnerability conditions of various societal groups. Only some selected figures designated as representatives of the community are invited during the planning stages (Musrenbangdes). The explicit involvement of these figures in the planning process advocating for marginalized and vulnerable groups is not mentioned as these parties are still not gender-sensitive. They are not fully aware of the emphasis on the importance of involving diverse societal groups with different backgrounds or conditions, which is an essential part. Ultimately, they fail to recognize certain groups such as women who are household heads or disabled groups that need to be encouraged to participate from the outset. From this study, it's evident that the implementation of programs remains predominantly top-down, not fully tapping into the aspirations of the community, particularly the vulnerable and marginalized conditions. Nevertheless, in terms of benefits, the community acknowledges the perceived benefits by both men and women in the target villages, even though they sometimes have limited participation from planning to execution.
- g. Meanwhile, the community typically engages in implementing activities when community self-reliance is required, such as during mangrove planting or embankment improvement. In practice, both men and women are involved and feel given the opportunity to participate. Usually, in each household, one or both participate in implementing community development programs. However, specific evaluations and socialization of results are generally not performed. Nonetheless, some physical development programs by the government do not involve the local community but use contractor services. Despite this, the community perceives the embankments as genuinely beneficial.
- h. For minority groups concerning religion, ethnicity, and disabilities, the residents in the study area seem less aware of these different groups in this sector. Even in social activities like the Focused Group Discussions (FGDs) conducted in this study, the importance of identifying and encouraging the participation of these marginalized groups is not a priority for village stakeholders, despite being encouraged by the study's implementing team. Several groups of people with disabilities, elderly women, and women heads of households attended some FGDs. However, based on the responses from participants in the FGDs and respondents in the survey, many stakeholders and residents are not fully aware of the importance of paying attention to these marginalized groups and encouraging their participation in social and community activities.
- i. From observations during this study, it appears that local leaders, both formal government leaders and informal leaders, are open to these involvements. However, they lack initiative because inclusive empowerment programs for women and marginalized groups are still lacking.
- j. Social aid, whether in the form of money, goods, or food, can be accessed by all groups in society. They are only recipients but are not involved in planning, decision-making, or evaluations.

5. DISCUSSION

Based on the findings of the study above, several lessons can be learned:

5.1. It shows nearly equal access and opportunities between men and women to generate income and perform tasks that are nearly identical in their respective jobs.

However, the difference in job types arises because certain occupations, considered hazardous and requiring heavier physical work, are typically dominated by men, such as fishing or labor-intensive jobs. Meanwhile, women are more involved in managing household expenditures and engaging in micro, small, and medium enterprises (UMKM). Women also have access to labor work across various fields such as agriculture, animal husbandry, tourism, small-scale industries, and so forth. People with disabilities and young individuals also have opportunities in family livelihood activities.

Considering the available opportunities and access, with women, disabled individuals, and other marginalized groups entering the workforce in the public sector, it demonstrates that within social norms, everyone has the opportunity to be empowered. However, the conditions of these different groups and their varying needs need to be taken into account. It requires both moral support and facilitation to ensure that the participation of all elements of society can generate optimal impact. It is important to understand in which sectors and within what division of labor are men, women, and adolescents or young people more dominant and why certain groups have access and are more prevalent in those sectors. These sectors can be optimized to empower marginalized groups further. Meanwhile, in the current scenario within the studied area, despite the access and participation of these groups in identified sectors, there might be certain groups, such as disabled individuals and specific ethnicities, who might not yet fully utilize these opportunities.

Furthermore, future implemented programs need to consider specific areas (for example, specific villages). In this study, the potential of natural resources and human resources varies, which consequently affects the potential of existing and developable enterprises.

Therefore, strategies should be contemplated to encourage the participation of marginalized groups in order to improve their livelihoods as an adaptation effort to climate and environmental changes.

5.2. Dominance of Roles and the Importance of Identifying Gender Roles within the Household

In this study, gender roles within the household were relatively less acknowledged as a determining factor in adaptation patterns and the decisions made by the community concerning their livelihoods. Men primarily held the role of primary breadwinners in the household. Public work related to household income remained the primary burden of men. Women took on the role of managing household income and played a supportive role in assisting family expenditures or running micro-businesses by selling goods in the market.

However, women, in fact, held the primary domestic roles and became the backbone of the family's economy during disasters. Women had greater access to credit institutions. They played a significant role in utilizing family savings such as small livestock, pawning belongings, borrowing money or rice from neighbors or relatives, and gathering shellfish. These tasks or roles underscored that women also have crucial responsibilities in ensuring the family's nutritional and daily food security. Meanwhile, the family's consumption patterns remained unchanged even during difficult times caused by disasters or when the head of the family couldn't generate income.

5.3. Gender roles and vulnerable/marginalized groups play pivotal roles in institutional aspects and community empowerment programs

Overall, many people in the community still do not have access to actively participate and have their aspirations heard, even though the local government's development planning programs claim to employ participatory approaches, especially in community empowerment programs related to climate change adaptation or other institutional activities. They do not feel that they benefit much or understand that development efforts are being made for their sake.

This is due to their limited involvement from the planning stage to the evaluation phase. People are not equally and fairly engaged in the empowerment and institutional processes; their participation is usually limited to instances requiring physical support, such as planting mangroves or constructing embankments. There are self-help efforts involving the community to mitigate the impact of disasters, such as limited initiatives by affected communities to build embankments against floods or dig wells. However, these initiatives are often handled or delegated to contractors in implementation.

5.4. Aspects of Community Development in the Context of Adaptation to Disaster Impacts

Specifically concerning the aspect of climate change adaptation, both men, women, and other marginalized groups in nearly all study areas have not been fully aware of the need to adapt to climate change. Related parties such as the government and other organizations have not emphasized initiatives related to guiding

the community in adapting to climate change and its associated impacts. Some affected communities in this study even complained that the preparedness and assistance provided for affected communities were still minimal. Due to the frequent occurrence of disasters, affected residents often do not receive assistance, be it for consumption or other needs, while economic activities halt due to flooding or extreme weather conditions.

Similarly, in terms of adaptation efforts, there are hardly any programs provided by any party to the residents, except for mangrove development and its utilization as a tourist destination. However, this is still faced with sustainability issues due to the limited capacity of local residents in management and maintenance. The number of people involved is also limited and exclusive. Therefore, regarding gender and marginalized groups, there are no significant issues because some residents have never received assistance programs or support to enhance their adaptive capacity to climate change.

Considering the crucial role of women and the existence of disabled groups that still actively participate in social and economic activities, the empowerment of these groups needs to be a focus of future endeavours. Moreover, in this study, there is minimal attention given to minority ethnic and religious groups. In most of the villages studied, these groups are marginalized since their involvement in social community activities at the village level, such as these FGDs, largely involves the majority population of Sasak ethnicity and Muslim religion. In contrast, involvement from other religious and ethnic groups is very limited, and in most villages, participants are primarily Muslims and Sasak, representing the majority community.

5.5. The potential issues related to gender and social inclusion in climate change adaptation programs

For the design of climate change adaptation programs in this study area, there are several potential issues that are important to consider:

- a. Segregated data based on gender, age, disability, poverty status, health condition, ethnicity, religion, and others related to marginalized groups are still very minimal and outdated. The scarcity of detailed data begins at the village level and extends to grassroots levels. Meanwhile, this segmented data is crucial for monitoring the progress of empowerment activities.
- b. Socio-cultural barriers can hinder the process of encouraging participatory and inclusive planning, decision-making, implementation, and evaluation. The gender-based division of domestic, public, and institutional roles potentially hampers the achievement of goals in future adaptation projects. Social and cultural norms have regulated the appropriateness and inappropriateness of behaviour from a gender perspective, often hindering women and adolescent girls from participating in empowerment activities related to the public sector. Furthermore, neglecting the cultural division of domestic and public work has the potential to burden one gender if they respond well and take on roles in future adaptation programs. Early marriage for women poses a potential issue in future inclusive approaches. This issue leads to a lack of involvement and contribution by adolescent girls in the public sector as they focus on household duties and have limited involvement in the public sector. Young household groups can be potential targets in the future provided there is sensitivity, support from their surroundings, and specific programs for them.

6. CONCLUSION AND RECOMMENDATION

Based on this study, there are several conclusions and recommendations that can be provided regarding fair, equitable, and gender-responsive programs.

- a. There are many opportunities for programs to ensure the involvement of men, women, and marginalized groups in empowerment programs aimed at adapting to climate change. To ensure inclusive participation in climate change adaptation, the types of potential activities should be specific to locations that already provide access to marginalized groups but have not been optimized. Men play a significant role in the public sector and are the main earners for the family. However, upon closer examination, women also have dominance not only in managing the domestic sector but also as family breadwinners in the public sector, albeit culturally and normatively referred to as secondary family earners. In this regard, society truly acknowledges the significant role of women and vulnerable/marginalized groups in their livelihoods, especially during difficult times such as disasters. Women also have roles (access, participation, control, and benefits) in public sector fields such as SMEs, agriculture, livestock farming, tourism, and institutions. However, certain social norms create behavioural differences concerning gender and vulnerable/marginalized groups. Therefore, the involvement of these different groups needs to consider social norms to adjust timing, dominant roles, and encourage the engagement of these different groups in sectors that are still absent (those already existing need optimizations, while those

absent require gradual enhancement of their roles). This is to prevent double burdens and conflicts of horizontal, vertical, domestic, and public interests.

- b. To optimize the adaptive capacity of disaster-affected families more efficiently and easily mobilized, it is essential to encourage the development of existing potentials that align with cultural norms, making leverage more accessible. The role of the project is to facilitate the functions of these existing potentials to have a more effective economic leverage. In this regard, activities involving active roles for women are crucial to be promoted and optimized. For instance, providing training and mentorship for existing economic activities (various types of SMEs where women dominate) to transform into creative, commercial economic activities with a broader market reach. Similarly, the family financial management system could be considered for improvement through training in financial management, bookkeeping, and strategies for managing family economics. This is expected to aid in improving the economy and making more resilient livelihood choices against future disasters. For example, if families can afford to purchase land outside disaster-prone areas, a more orderly relocation can be encouraged. From the research findings, there are several sectors and public domains where women and other vulnerable groups have gained access and actively participated.
- c. The presence of relatively open local leaders presents a crucial opportunity to encourage fair and equal approaches for women and other vulnerable groups. Continuous development of communication with both formal and informal figures is essential since their gender awareness and responsiveness remain low. Every empowerment program within the project needs to engage the community from the planning phase to implementation and evaluation to ensure that no group or party is overlooked in any activity.
- d. Meeting or training methods should be tailored to fit the local culture and norms, enabling women and marginalized groups to speak up, express opinions, aspirations, and actively participate in forums or engage in learning during training sessions. At present, women and youth tend to be reluctant to speak in larger forums, especially when these forums include various influential figures or a wide range of groups. This poses a significant challenge in preparing institutions to anticipate issues related to social interactions involving vulnerable groups. Therefore, it's crucial to employ more homogeneous approaches so that voices from grassroots levels can be collected, for example, by creating separate meeting groups for village leaders and women or persons with disabilities.
- e. There is a need to develop safeguarding mechanisms to ensure that all groups can fulfill their roles safely and comfortably. All parties need to recognize the importance of social protection and preventing violence against specific groups, especially women and other vulnerable groups. Currently, such mechanisms are absent in the study area due to a lack of awareness regarding the significance of protecting the rights and safety of all parties, and culturally, this subject is still considered taboo. A progressive and proactive approach involving stakeholders from diverse backgrounds, including formal leaders (government officials) and informal figures like women leaders, children, religious leaders, among others, is necessary to agree upon these safeguarding mechanisms.
- f. To support a more comprehensive approach and ensure the inclusion of vulnerable groups in future programs, the role of field officers (FO) or field agents is crucial. Intensive monitoring can be conducted with the presence of FOs who understand the local socio-cultural context, serving as communication channels between the project team and the target groups in the field.
- g. The segregated data based on gender and vulnerability conditions in the target areas is still very lacking.
- h. The presence of Field Officers (FOs) would facilitate the refinement of this segregated secondary data. Engaging with community leaders at the village level (such as sub-village heads, neighborhood chiefs, and Posyandu cadres) organized within an institution or forum to update segregated population data based on vulnerability is essential. Over the project duration, refining this segregated data will become a crucial resource in mapping the development of roles for vulnerable groups to achieve more effective, fair, and equitable outcomes.

Furthermore, evaluation-based interventions are important to be conducted regularly to understand the progress that has occurred and the subsequent needs for more equitable and fair outcomes.

Annex 4. REPORT ON SOCIAL-ECONOMIC STUDY AND VULNERABILITY TO CLIMATE CHANGE DISASTERS IN THE COASTAL AREAS OF LOMBOK

I. INTRODUCTION

1.1. Background

The southern part of West Lombok area, located in the Lembar and Sekotong Districts, is a region vulnerable to hydrometeorological disasters. Several common disasters include tidal floods, regular floods, droughts, and tornadoes. In several coastal villages, tidal floods occur almost every month, inundating settlements, agricultural areas, and fishponds. The escalation of tidal floods gradually increases from year to year, triggered by rising sea levels and higher flood intensity due to increased rainfall. The impact of tidal floods becomes more massive when floods occur simultaneously, causing higher inundation of water into mainland areas.

The Lembar and Sekotong Districts are classified as dry climate regions with hilly topography. Hence, these areas are highly susceptible to drought disasters. Entering the months from June to October is when communities start facing difficulties in accessing water, limited agricultural production, scarcity of animal feed, and the spread of diseases due to poor sanitation. The costs of adapting to such situations become significantly high, especially for clean water, animal feed expenses, and the low value of rain-fed agricultural production.

The hilly topography with low to moderate vegetation coverage creates vulnerability to floods. Floods quickly flow into the sea not only through existing rivers but also through many eroded land crevices, creating a swift flow of water through residential roads toward the sea and subsequently causing larger tidal flood areas. The flood situation worsens with high and unpredictable rainfall due to climate change.

The impact of these various disasters in this region significantly affects many aspects. Tidal floods and regular floods have disrupted social, institutional, and economic activities, as well as a decline in environmental quality and public health.

The Lombok Climate Change Consortium (LC3) has taken the initiative to address the disaster conditions in this area with funding support from the Adaptation Fund program. This support aligns with efforts by the government and communities to reduce and mitigate disasters through several programs and activities.

Currently, LC3 is in the final stages of drafting a proposal and requires empirical data support related to various aspects, particularly social, economic, disaster-related, gender, and others. This underlines the importance of conducting a 'Social-Economic, Institutional, and Disaster Study,' specifically in the southern part of West Lombok's coastal areas, in the Lembar and Sekotong Districts.

1.2. Objective

- 1.2.1. Understanding the social, institutional, and economic conditions of communities in the coastal areas of six villages in the Sekotong and Lembar Districts
- 1.2.2. Analyzing climate disaster risks concerning various aspects: social, institutional, economic, and environmental
- 1.2.3. Providing input for data and information support related to the development of the project proposal proposed by LC3

1.3. Output

- 1.3.1. Overview of the community's condition based on their social capital, institutional roles, livelihood sources, and income from various community initiatives
- 1.3.2. Overview of the various disasters and their impacts on different aspects faced by the community
- 1.3.3. Formulation of recommendations to support the needs for drafting proposals for the Adaptation Fund program

II. METHODOLOGY

2.1 Method

The study employs a descriptive method, which is a research approach aimed at describing and analyzing phenomena or events according to their actual conditions or situations. The main objective of the descriptive method is to provide a clear and detailed overview of a problem, occurrence, or population without manipulating variables or inferring cause-and-effect relationships.

2.2 Study Location

The study's location is in the coastal areas of two districts, namely Lembar District and Sekotong District in West Lombok Regency. From these two districts, there are three villages bordering the beach, as follows:

Table 2.1 Location of Study, District, Number of Villages, and Number of Huts

| Name of District | Number of Villages | Name of Village |
|------------------|--------------------|---------------------|
| 1. Lembar | 3 Villages | 1. Lembar |
| | | 2. South Lembar |
| | | 3. Labuhan Tereng |
| 2. Sekotong | 3 Villages | a. Cendi Manik |
| | | b. Central Sekotong |
| | | c. West Sekotong |

2.3 Data Collection

Data collection utilizes observation techniques, in-depth interviews, and Focus Group Discussions (FGD). Observation involves systematically observing and recording the behavior, events, or phenomena observed in the research object. In-depth interviews are a technique for deeply exploring information with preselected respondents. FGD is a technique for gathering information from a group of people or informant sources in one place, guided by prepared key questions.

2.4 Data Source

The data sources include secondary and primary data. Secondary data is collected from documents such as reports, publications, maps, and other available materials in village government, regional government, and other sources. Primary data is collected from the results of interviews and FGDs.

Determination of Respondents

Respondents are selected based on cluster sampling quotas. Each village is allocated a quota of 12 respondents, and clustering involves the representation of elements present in the village, including: village officials, fishermen, farmers, micro, small and medium enterprises (MSMEs) owners, community leaders, religious figures, youth, and female representation. Therefore, the total number of respondents across the 6 villages is 72 respondents.

2.5 Variables

- The social and institutional variables assess several parameters: social capital includes social and institutional parameters that positively contribute to creating harmony in family and community life. The mentioned social value can be related to both formal and informal aspects.
- The economic variable assesses parameters related to community economic activities across various sectors, community income, and potential business opportunities that can be developed.
- The disaster vulnerability variable examines parameters of various disasters and their potential impacts on various aspects: social, economic, environmental, institutional, health, and infrastructure.

2.6 Data Analysis

- Social data analysis, involving descriptive analysis, includes interpreting data obtained from observations, interviews, and FGDs, to identify patterns, relationships, and meanings from the collected data, providing a deeper understanding of the social phenomena under investigation.
- Economic data analysis includes descriptive analysis to explore community economic sources, diversity of businesses, and community income in various economic activities.
- Climate disaster vulnerability analysis applies the RCRA (Risk Climate Rapid Assessment) approach. Data analysis uses (1) disaster assessment formats, and (2) scoring models to determine the severity level of disasters by combining the likelihood and consequences scales.

Table 2.2 Determination of disaster level based on likelihood and disaster consequence

| Hazard Matrix | | | Consequence | | |
|---------------|----------------|---------|-------------------------|------------------------|------------------------|
| | | | Extraordinary Score=3 | Medium Score=2 | Not Present Score=1 |
| Likelihood | Almost Certain | Score=3 | Extremely Hazardous (6) | Hazardous (5) | Somewhat Hazardous (4) |
| | Possible | Score=2 | Hazardous (5) | Somewhat Hazardous (4) | Less Hazardous (3) |
| | Rare | Score=1 | Somewhat Hazardous (4) | Less Hazardous (3) | Not Hazardous (2) |

III. RESULTS & DISCUSSION

3.1 General Description of Study Location

a. Population Size

The study focuses on villages located along the coastline. Based on geographical positioning, six villages meeting these criteria have been identified. These six villages are situated across two districts, with varying numbers of hamlets. Below is an overview of the study area, ranging from the district level to the hamlet level.

Table 3.1 Location of study based on district, village, and hamlet level

| Sub District | Village Name | Number of Hamlets | | Nama of Coastal Hamlet |
|--------------|---------------------|-------------------|-----------------|-------------------------------------|
| | | Hamlets | Coastal Hamlets | |
| 1. Lembar | 1. South Lembar | 11 | 2 | Cemara dan Puyahan |
| 2. Sekotong | 2. Cendi Manik | 17 | 3 | Madak I, Madak II, Madak Beleg |
| | 3. Central Sekotong | 24 | 3 | Tanjung Batu, Aik Tangi, Lendang Re |
| | 4. West Sekotong | 11 | 2 | Jerjeng, Aik Semin |

Source: Village Profile, 2020.

Each village has a varying number of hamlets, some even falling into the category of having a substantial number of hamlets. Consequently, several villages are currently in the process of village expansion (Labuhan Central Sekotong Village, Cendi Manik, and West Sekotong). The six villages possess hamlets directly bordering the coastline, as depicted in the table above.

However, the number of hamlets does not necessarily linearly represent the population count in each village. South Lembar Village, with a total of 11 hamlets, is the village with the highest population, while Lembar Village, with 7 hamlets, has the smallest population. The population and number of households (HH) for each village are presented in the following table, along with the population count based on gender (refer to Table 3.2 and Table 3.3).

Table 3.2 Population size and Number of Households in each village

| Sub District | Village Name | Population Size | |
|--------------|---------------------|-----------------|----------------------|
| | | Population Size | Number of Households |
| 1. Lembar | 1. South Lembar | 10.723 | 3.442 |
| 2. Sekotong | 2. Cendi Manik | 5.699 | 1.863 |
| | 3. Central Sekotong | 9.339 | 2.918 |
| | 4. West Sekotong | 8.781 | 4.058 |

Source : Village Profile , 2020.

Table 3.3 Population Size in each Village based on Gender

| Sub District | Village Name | Population Size | |
|--------------|---------------------|-----------------|--------|
| | | Male | Female |
| 1. Lembar | 1. South Lembar | 5.436 | 5.287 |
| 2. Sekotong | 2. Cendi Manik | 2.831 | 2.868 |
| | 3. Central Sekotong | 4.664 | 4.699 |
| | 4. West Sekotong | 4.055 | 4.736 |


Source : Village Profile, 2020

Observing the distribution of the population based on gender in the table above, there appears to be a proportional number of males and females in each village.

3.2 Characteristics of Natural Resources in Coastal Areas

a. Variety of Natural Resources in Coastal Areas

There are at least five prominent natural resources considered important by the inhabitants residing in coastal areas. The significance of these resources is not only from an economic perspective but is also associated with their roles in social and environmental aspects. These five natural resources include mangroves, agriculture, livestock farming, beaches/sea, and fishponds (Figure 3.1).

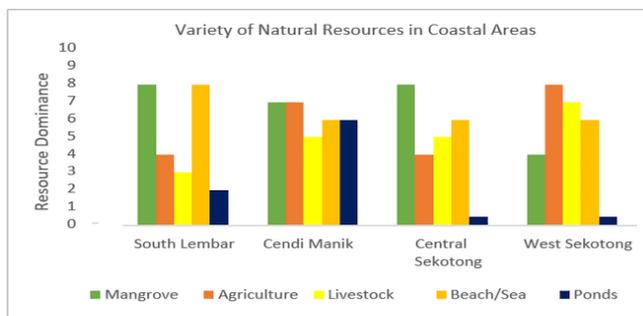

Picture 3.1 Variety of resources in study location

Based on the above image, it is evident that the mangrove resources holds significant value, especially in three villages: South Lembar, Cendi Manik, and Central Sekotong. The largest distribution of mangroves exists in Cendi Manik, South Lembar, and Central Sekotong. Beaches and the sea hold importance in all villages, as a majority of the population depends on livelihoods as fishermen.



Picture 3.2 Map of studied village and spread of mangrove resources

Figure 3.2 above illustrates the distribution of prominent mangrove resources in three villages. Other resources such as agriculture, livestock farming, and fishponds are the mainstays for the other three villages: Lembar, Labuhan Tereng, and West Sekotong. The beach is considered highly significant for South Lembar village, as the Cemara beach area is a focal point for beach tourism.

b. Various use of natural resources in Coastal Areas

Mangrove Resources

There are 8 species of mangroves found in the study area, with the most abundant being the *Rhizophora apiculata* species, followed by two other species: *Avicennia marina* and *Ceriops tagal* (Japa L and Didik S., 2019). The *Rhizophora* species are highly prominent and distributed across all study locations. The utilization of mangroves varies significantly in each village, and in general, 6 types of mangrove utilization have been identified (Table 3.4).

Table 3.4 Various utilization of coastal and mangrove resources in Coastal Areas

| Village Name | Various Utilization | | | | | |
|------------------|---------------------|----------------------------|--------------------------|---------------------|-------|---------------|
| | Mangrove Tourism | Shellfish/ Crab Collection | Silvo-fisheries Mangrove | Mangrove By-Product | Ponds | Beach Tourism |
| South Lembar | √ | √ | √ | | | √ |
| Cendi Manik | √ | √ | √ | | √ | √ |
| Central Sekotong | √ | √ | √ | √ | | √ |
| West Sekotong | √ | √ | √ | | | √ |


Note: √ Low Utilization √√√√√ Very High Utilization

Mangroves can be assuredly considered as one of the sources of income for the coastal community. Every

day, they gather crabs, clams, and fish beneath the mangroves and utilize them to develop fish farming or silvofisheries. Prominent mangrove utilization for tourism is observed in Central Sekotong Village, South Lembar Village, and Cendi Manik Village. The management of tourism is conducted by the Pokdarwis (Tourism Awareness Group) in collaboration with the BUMDes (Village-Owned Enterprises). Lembar Village has the least amount of mangroves or could be said to have nearly depleted them because the mangroves grow sporadically. Most of the mangrove areas have been utilized for milkfish ponds. Cendi Manik Village utilizes mangroves in various ways and still possesses a relatively large mangrove area. Central Sekotong Village is the only village capable of utilizing mangroves for processed products, specifically producing mangrove coffee. However, this venture has been suspended for some time to ensure the safety of the product for consumption.

The community also relies on income from mangrove seedlings. Communities in three villages is Cendi Manik, South Lembar, and Central Sekotong—have the capability for mangrove seedling cultivation. Their seedling products have been sold to various parties, including the BPDAS NTB (Regional Watershed Management Agency of West Nusa Tenggara), used for the Forest and Land Rehabilitation program.

The precise data on the extent of mangroves in each village is not well-identified. From interviews, respondents provided varied answers, with many not knowing the accurate information. However, it can be estimated that villages with relatively large mangrove areas are Cendi Manik, South Lembar, and Central Sekotong. Regarding the estimated mangrove area, two versions are presented: based on interview results and spatial data (Figure 3.3).

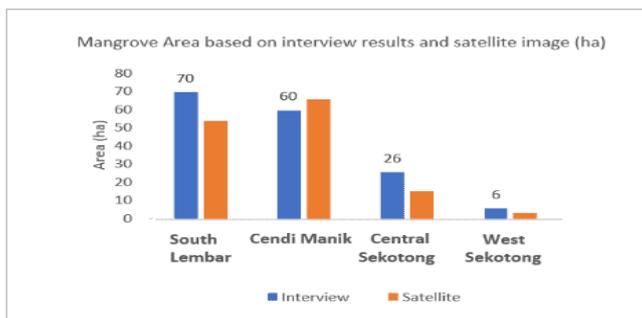

Picture 3.3 Mangrove area based on 2 versions, interview results and satellite images in 6 villages

The total mangrove area based on interview results is 179 hectares, whereas the satellite image data indicates 148 hectares. Actually, these figures can be understood, and the difference is not too significant because the satellite image estimation (Google Earth, August 9, 2023) calculates based on the expanse of mangrove areas, excluding small scattered spots distributed across several areas. These small areas, for instance, exist between ponds, among paddy fields, or in gardens, with sizes ranging from 1 to 10 square meters. In contrast, the interview-based calculation considers the mangrove area based on these scattered spots.

Agricultural Resources

The agricultural resources in coastal areas are quite diverse, ranging from utilization for paddy fields, dry fields, gardens, home gardens, and livestock. The study did not determine the specific area for each of these uses but only estimated the value of their utilization, as presented in Table 3.5.

Table 3.5 Various utilization of agricultural resources in coastal Areas

| Village Name | Various utilization | | | | | |
|------------------|---------------------|------------|--------|--------------|-------------------|-------------|
| | Paddy Field | Dry Fields | Garden | Plotted Yard | Livestock Farming | Tide System |
| South Lembar | √ | √ | √ | √ | √√ | |
| Cendi Manik | √√ | √√ | √ | √ | √√ | |
| Central Sekotong | √ | √ | √ | √ | √ | |
| West Sekotong | √√ | √√ | √ | √ | √√ | |

Note : √ Low utilization √√√√ Very high utilization

The prominent agricultural resources in coastal areas include dry fields, paddy fields, gardens, and livestock farming. No evidence of tidal agriculture systems was found. Paddy fields in coastal areas offer the opportunity for planting 2-3 times a year due to relatively available water compared to farming on higher topography, where planting occurs only 1-2 times a year. Rice yields in paddy fields can reach 3-5 tons/ha, whereas in dry fields or gardens, rice production ranges from 1-2 tons/ha.

The livestock commonly raised by the inhabitants are cows and goats. Typically, goats are individually owned, while cows are managed under the 'ngadas' system. Under this system, cows belong to someone but are raised by the community on a profit-sharing basis. The number of cows raised ranges from 2 to 4, and with the profit-sharing system (owner: caretaker ratio is 1:1), on average, farmers can produce 1-2 calf offspring per year.

Sea Resources

The sea is the mainstay for most of the inhabitants living in coastal areas. The sea is not just an activity for men as fishermen, but women also significantly contribute to activities on the beach and at sea. Sea-related activities include fishing, boat utilization services, MSMEs in beach tourism areas, crab, clam, and fish collection, salt and fish pond activities. These activities are also accompanied by downstream activities involving sea product marketing by women and processing sea products (shrimp paste, salted fish, crackers).

3.3 Social and Institutional Aspects

In terms of social and institutional aspects, the profiles of the six villages bear similarities to each other. The community exhibits a strong social capital in their participation in activities related to public interests. The inhabitants assist each other when a family faces difficulties or when they collectively strive for common goals. Practices of mutual assistance during times of death, illness, marriage, or childbirth are still strongly upheld as social norms to maintain community harmony.

Social capital is also evident in community efforts to mitigate both flood-related disasters and other calamities. For instance, to reduce the impact of floods, residents in South Lembar and Cendi Manik engage in collective efforts to build embankments as a form of protection. In Cemara, South Lembar, an independently constructed embankment spans approximately 2 kilometers and stands at a height of 0.5 meters. Estimated in monetary terms, the improvement of this 2-kilometer embankment has cost around 0.7 to 1 billion Indonesian Rupiah.

Regarding institutional aspects, the community has formed social groups based on sectoral and thematic needs. For instance, in the studied village locations, there are groups of fishermen, farmers, tourism awareness groups, and business groups. Concerning disaster mitigation, the community has responded to their village conditions by establishing disaster preparedness instruments, designating these six villages as Disaster-Resilient Villages (Destana), Climate Change Program Villages (Proklam), and Community-Based Disaster Preparedness (SIBAT).

The significance of these various institutional groups depends largely on the context. During emergency situations, groups formed for disaster management play a crucial role. However, generally, the role of village leaders is considered essential as they act as the front liners in responding and taking action during significant events at the village or sub-village levels.

3.4 Livelihoods and Income

The variety of livelihoods among the coastal area inhabitants is diverse, prominently involving fishing, farming, and livestock rearing. Household members engaged in economic activities aren't limited to just fathers; wives also participate in specific tasks. Villages that have fish or salt ponds observe involvement from fishermen and farmers in these activities.

Typically, people do not rely solely on a single occupation. Relying on just one job may not guarantee sufficient income, and it can pose risks to their food security or overall livelihood. Consequently, individuals engage in multiple livelihoods, such as being both a fisherman and a farmer, a fisherman and a livestock farmer, a farmer and a gold miner, among other combinations. The following provides an overview of the variety of livelihoods and estimated earnings for each type of livelihood (Table 3.6).

Table 3.6 Various livelihoods of population in coastal areas

| Various Livelihoods | Description | Estimated Income (IDR) |
|---------------------|--|------------------------|
| 1. Farmer | Farmers in dry land, cultivate twice a year, planting rice once and planting | 2.100.000 |

| Various Livelihoods | Description | Estimated Income (IDR) |
|--|---|------------------------|
| | other crops like legumes and vegetables once. Rice yield ranges from 1.5 to 2 tons per hectare for personal consumption. The average land ownership is 0.5 hectares. | |
| | The yields of legumes and other crops are consumed by the farmers themselves and sold. Commonly grown legumes include soybeans, corn, while vegetables include beans. | 600.000 |
| 2. Cattleman | Most farmers rear livestock using a sharecropping system (ngadas), with an average of 2-4 head of cattle per family. Each year, one cow gives birth, and the price of a 6-12 months old cow is approximately 6 million rupiahs per head. | 6.000.000 |
| 3. Fisherman | Fishermen engage in capturing fish, exploring areas up to 2 km using small boats, with around 5 horsepower. They employ netting and fishing techniques. The average catch per day ranges from 3-5 kg, with a selling value of IDR 90,000 – 150,000 per day. On average, they spend about 20 days per month at sea. | 4.800.000 |
| | Crab and shellfish fishermen are commonly found within the mangrove area. Crab catching is predominantly performed by men, while shellfish catching is carried out by women. The yield varies, ranging from IDR 30,000 – IDR 50,000 per day. The effective time spent catching crabs and shellfish is around 20 days per month. | 4.800.000 |
| 4. Micro, Small, and Medium Enterprises (MSME) | The predominant business in the coastal area is micro and small businesses, such as selling from small kiosks or stalls at home and around tourist spots. The items sold vary from basic necessities, snacks, processed products, to food and beverages. During Saturdays and Sundays, sales volume at tourist locations can be 3-5 times higher than usual days. Normal daily income ranges from 75,000 to 100,000 IDR, while during peak times it reaches around 300,000 IDR per day. | 18.000.000 |
| | The food processing business is conducted at a household scale, usually performed individually or in groups. Various processed foods include making snacks and cakes. Production takes place every day with an effective time of about 25 days per month. Daily income ranges from 50,000 to 100,000 IDR. | 12.000.000 |
| 5. Ponds | The milkfish and crab ponds are managed by the local community with an area ranging from 10 x 10 meters. The crabs are raised in the same area as the milkfish ponds. The land status varies, with some milkfish ponds being rented by farmers since the pond owners come from outside the village. | 3.000.000 |
| | Salt ponds, managed by the community with | 6.000.000 |
| 6. Services | Tourism Services | 12.000.000 |
| | Agricultural laborers, construction workers, and craftsmen, daily wage averages around 80,000 IDR, with a job opportunity of 60 days per year. | 4.800.000 |
| 7. Village Official | Village officials are waged between 2 – 3 million/month. | |
| 8. Other | Odd jobs or miscellaneous work involve individuals seizing every job opportunity they can take on as long as they are capable of doing it. Typically, these miscellaneous jobs encompass various tasks like agricultural labor, construction work, and small-scale mining. Most people engage in small-scale mining with unpredictable earnings as it is subject to chance or luck. | 6.000.000 |

Source: Primary Data

As previously explained, generally, inhabitants do not rely solely on one type of livelihood. Within a year, they engage in several types of work. Their ability to partake in diverse activities is feasible due to sufficient available time. For instance, fishermen work during the night and engage in farming or livestock activities during the day. Similarly, when they are farmers, they are busy with agricultural activities for only 3-6 months a year, and the rest of the time, they may work as laborers or in other occupations. The following presents an estimation of the income of inhabitants engaged in primary farming and fishing livelihoods, whose earnings stem from a combination of diverse job types (Table 3.7).

Table 3.7 Estimated income of population based on various income sources

| Main Profession | Income Source Combinations | Total Income (Rp) |
|-----------------|-----------------------------------|-------------------|
| 1. Farmer | ▪ Farmer – Cattleman | 8.700.000 |
| | ▪ Farmer – Cattleman – Services | 13.500.000 |
| | ▪ Farmer – Cattleman – Gold Miner | 14.700.000 |
| 2. Fisherman | ▪ Fisherman – Farmer | 12.300.000 |

| | | |
|--|----------------------------------|------------|
| | ▪ Fisherman – Farmer – Cattleman | 18.300.000 |
| | ▪ Fisherman – Gold Miner | 15.600.000 |

Source: Processed Primary Data

If linked to the per capita income, considering an average family size of 4 individuals per household, the range of earnings for Farmers and Fishermen falls around Rp 5,958 to Rp 12,534 per capita per year.

3.5 Disaster Aspects

a. Various Disasters

There are four types of disasters experienced by the inhabitants of the six coastal villages, ranging from mild to severe intensity. The most frequent disasters experienced by the population are tidal floods, floods, droughts, and strong winds/cyclones. Here is an overview of these disasters (Table 3.8).

Table 3.8 Overview of various disasters and the intensity of disaster occurrences

| Disaster Type | Description | Impacted Village | | | |
|-----------------|---|------------------|-------------|------------------|---------------|
| | | South Lembar | Cendi Manik | Central Sekotong | West Sekotong |
| 1. Tidal Floods | Floods occur every month with a duration of 2-3 days. The duration of each flood lasts approximately 3-5 hours. | 5 | 3 | 4 | 3 |
| 2. Flood | Major floods occur 2-3 times a year and have an exacerbating impact on worsening the situation during floods. | 4 | 4 | 4 | 3 |
| 3. Drought | Drought leads to difficulties in obtaining clean water, scarcity of animal feed, crop failures, and deteriorating public health | 4 | 4 | 4 | 4 |
| 4. Strong Winds | The occurrence of strong winds and tornadoes usually happens during the west wind season, but according to the residents, these occurrences of strong winds can now vary in timing. These strong winds are followed by abrasion, which damages coastal infrastructure, including embankments. | 4 | 3 | 4 | 4 |

Source: Primary Data

Note: 1. Very lightly impacted, 2 Lightly impacted, 3 Impacted, 4 Heavily impacted, 5 Very heavily impacted

The frequency and impact of tidal floods have increased over time. According to interviews conducted in Central Sekotong, about 10 years ago, the distance between settlements and the coastline was around 50 meters. However, presently, settlements are situated at the very edge of the coastline, such that when the waves rise by just 2 meters, water enters the houses. Severe tidal flood incidents occurred in the Cemara hamlet, affecting 450 households. According to residents, tidal floods occur more frequently, not only during full moon periods but also unexpectedly at other times. Here is an overview of tidal floods:

- Occur every month, lasting 2-3 days during full moon, with a duration of 3-5 hours; the impact intensity ranges from low to moderate, with water levels reaching 10-30 cm into residential areas.
- Occur 2-3 times a year triggered by floods, lasting 1 day or more, with moderate to high impact intensity; water levels reach 30-60 cm.
- Tidal floods worsen when floods occur simultaneously. Flood inundation can last 1-3 days with moderate to high impact intensity.

Floods occur due to two main factors: high-intensity rainfall and degradation of land cover due to encroachment and illegal small-scale mining activities in the study area. Although floods are not entirely caused by climate change, their impact triggers larger tidal floods. This happens because the floodwater volume meets the tidal flood, causing water levels to rise further and infiltrate agricultural and residential areas.

b. Number of Hamlets and Household Affected by Tidal Floods


From the six surveyed villages, there are 19 hamlets located along the coast that are at risk of experiencing significant impacts, particularly from tidal floods. Each hamlet exhibits varying levels of severity in terms of disaster impact. However, generally, the residents living near the coast experience tangible effects from tidal

floods, regular floods, and strong winds (cyclones). Overall estimates suggest that tidal floods have the potential to affect approximately 3,658 households across these 19 hamlets. The distribution of the number of tidal flood impacts can be observed in the following figure.

Table 3.9. Population size affected by Tidal Floods

| District | Village Name | Number of Hamlets | Number of Households |
|-------------|---------------------|-------------------|----------------------|
| 1. Lembar | 1. South Lembar | 2 | 495 |
| 2. Sekotong | 2. Cendi Manik | 2 | 208 |
| | 3. Central Sekotong | 6 | 394 |
| | 4. West Sekotong | 7 | 429 |

Source: Primary Data

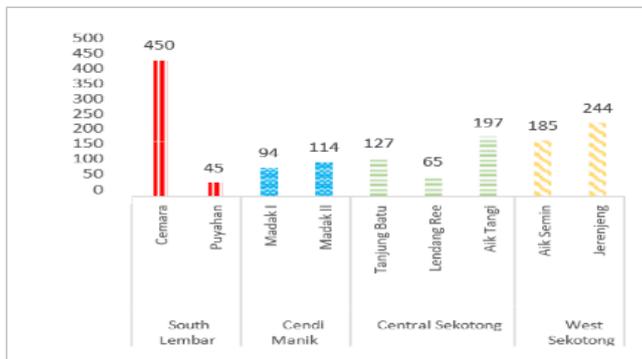

Picture 3.4 Number of hamlets and households affected by tidal floods

The potential impact ranges from mild to severe across 17 hamlets, with an estimated 1,848 households affected. Assuming an average household size of 4 individuals, the potential impact of tidal flooding affects around 7,392 people. Tidal floods have been occurring for quite some time, but their intensity has increased over the past five years. Historically, when tidal floods happen, the community tends to resign themselves to the situation and hope for the water to recede quickly. The most concerning events occur during the night, as each household can only endure the situation within their own homes.

Official gathering points or evacuation sites have been designated by the government. However, these locations have never been utilized by the affected residents during tidal flood incidents. This is due to the inadequate conditions at these sites, such as lack of provisions for food, rest, and healthcare. As a result, when tidal floods occur, individuals choose to independently endure the situation within their own residences, waiting for the waters to subside.

3.6 Analysis of Disaster Hazard Level and Vulnerability

a. Danger Level Analysis

The analysis assesses the level of danger by combining two parameters: the likelihood scale and the consequence scale. The likelihood scale evaluates disasters based on three levels: frequent or almost certain, possible, and rare. Meanwhile, the consequence scale evaluates the level of disaster danger across three categories: extreme, moderate, and not evident. The description of these two parameters is presented in the following Table 3.10:

Table 3.10 Hazard risk level assessment based on likelihoods and consequence parameter

| Likelihood Scale | | |
|-------------------|-------|---|
| Category | Score | Description |
| 1. Almost Certain | 3 | <ul style="list-style-type: none"> Can occur several times a year Probability of occurrence is more than 50% |
| 2. Possible | 2 | <ul style="list-style-type: none"> Occurs once in 5-10 years Probability of occurrence is 25-50% |
| 3. Rare | 1 | <ul style="list-style-type: none"> Occurs once in a period of more than 10 years Probability of occurrence is less than 25% |
| Consequence Scale | | |

| Likelihood Scale | | |
|--|-------|--|
| Category | Score | Description |
| 1. Extreme | 3 | <ul style="list-style-type: none"> ▪ The impact of damage occurs in most areas of the village/city ▪ May hinder the achievement of government development targets ▪ Requires additional specialized capacity over the long term ▪ Requires a significant additional cost (central government assistance) |
| 2. Moderate | 2 | <ul style="list-style-type: none"> ▪ The impact of damage occurs in a small part of the village/city ▪ May disrupt the achievement of government development targets ▪ Requires certain additional capacity ▪ Requires additional budget from own funds (reallocation) from the Local Government (District/Province) |
| 3. Not evident | 1 | <ul style="list-style-type: none"> ▪ The impact of damage is almost non-existent ▪ Does not hinder the achievement of government development targets ▪ Does not require any additional capacity ▪ Does not require any additional costs |
| Total Interval Score | 2-6 | |
| Hazard Level Categorization based on Total Score | | |
| Total Score | 6 | ● Extreme Hazard |
| | 5 | ● Hazard |
| | 4 | ● Light Hazard |
| | 3 | ● Less Hazard |
| | 2 | ● No Hazard |

Source: The Climate Risk Assessment Guideline by Mercy Corps adapted from ICLEI-OCEANIA, 2008

Based on the analysis format above, the disaster hazard level profile at the study location is as follows:

Table 3.11 The results of the analysis of disaster hazard levels at the study location.

| Hazard Level | Village | | | |
|-------------------|----------------------|--------------------------|------------------------|--------------------------|
| | South Lembar | Cendi Manik | Central Sekotong | West Sekotong |
| 1. Extreme Hazard | Tidal Floods | Floods | Tidal Floods | Tidal Floods |
| 2. Hazard | High Waves, Abrasion | Tidal Floods | Floods, Droughts | Floods, Droughts |
| 3. Lightly Hazard | Droughts | Strong Winds, High Waves | Strong Winds, Abrasion | Strong Winds, High Waves |
| 4. Less Hazard | Landslide | | | |
| 5. Not Hazard | | | | |

Source: Focus Group Discussion Results, 23-25 August 2023

Based on the table above, it is evident that prominent disasters falling under the extreme category include tidal floods, regular floods, and droughts. These three disasters are considered events that consistently worry the coastal area residents. The occurrences of these types of disasters happen periodically, within days, months, or years. Hence, when considering the likelihood scale, these disasters fall under the nearly certain parameter. In terms of consequences, they fall within the extreme and moderate categories.

b. Disaster Vulnerability Analysis

The vulnerability analysis below will present an exploration of the types of disasters and their impact on various aspects. This information is crucial in predicting the level of risk and losses that may arise due to these disasters. A more detailed analysis of the results is presented in the following Table 3.12.

Table 3.12 Disaster Vulnerability Analysis at Study Location

| In-risk Asset | Vulnerability Form | Estimated Impact/Risk Value |
|---------------|---|--|
| 1. Humans | <ul style="list-style-type: none"> ● Death | <ul style="list-style-type: none"> ● As of now, there haven't been any fatalities due to tidal waves (rob). However, a flood disaster occurred in January 2020. It affected 1,820 households or 5,578 individuals in 13 hamlets in Sekotong District. Another tidal wave (rob) occurred in December 2021, affecting 3 hamlets, 431 households, and 1,742 individuals. ● In February 2023, a tidal wave occurred in South Lembar, impacting 450 households across 2 hamlets. ● On February 13, 2023, a flood disaster affected 5 hamlets, with 529 households impacted. Unfortunately, one child lost their life after being |

| In-risk Asset | Vulnerability Form | Estimated Impact/Risk Value |
|------------------|--|---|
| | | hit by debris during the flood (source: West Lombok Regional Disaster Management Agency). |
| | <ul style="list-style-type: none"> ● Illness | <ul style="list-style-type: none"> ● Tidal wave (rob) occurrences often happen during the night, causing anxiety and disrupting daily activities. Eating patterns are disrupted, work schedules are affected, and schooling is disrupted. Additionally, environmental conditions are disturbed, particularly in terms of household cleanliness, yard maintenance, and access to clean water. These disturbances worsen if there's a power outage. ● Poor psychological conditions, coupled with irregular eating patterns, make the population more susceptible to illnesses, especially among the elderly and children. ● Based on interviews with respondents, some common illnesses that frequently appear due to tidal waves (rob) or floods include itchy skin, respiratory tract issues, and coughs/colds. |
| 2. Economy | <ul style="list-style-type: none"> ● Loss of workdays for fishermen, farmers, service providers, and others | <ul style="list-style-type: none"> ● During tidal wave (rob) occurrences, fishermen refrain from going to sea as they prioritize their families' safety. Consequently, they lose approximately 3-5 days per month or around 60 days per year without fishing. If their average net income per fishing trip ranges from Rp 30,000 to Rp 50,000, they lose an annual income of approximately Rp 1.8 to 3 million per person per year |
| | <ul style="list-style-type: none"> ● | <ul style="list-style-type: none"> ● Although tidal waves (rob) frequently occur at night, according to respondents, it often affects their work motivation as farmers or their activities as service providers (construction workers, miners, etc.). If the average daily wage for a farmworker or construction laborer is Rp 70,000, farmers, construction workers, and artisanal miners could lose income of up to Rp 4.2 million per person per year. |
| | <ul style="list-style-type: none"> ● Losses in paddy fields and dryland/fallow fields | <ul style="list-style-type: none"> ● Losses in paddy fields due to inundation by seawater result in a reduction of up to 50% in production. Each hectare of land is capable of producing an average of 2 tons per hectare, valued at Rp 6 million per hectare. Therefore, the potential loss per hectare is 6 million rupiahs per year for paddy fields and Rp 2.1 million per hectare for upland rice (planted in fallow land and gardens). |
| | <ul style="list-style-type: none"> ● Losses in salt ponds and milkfish ponds | <ul style="list-style-type: none"> ● Losses in fish ponds for milkfish and salt ponds: There are approximately 70 hectares of ponds across three villages, Lembar, Labuhan Tereng, and Cendi Manik. The pond sizes range from approximately 10 x 10 square meters to 20 x 20 square meters. The investment for each pond varies between 10 - 20 million rupiahs. ● During tidal waves (rob), production failure can reach 50 - 100%. When the ponds are inundated, the farmed fish can escape. Therefore, the loss due to tidal waves for pond farmers can reach Rp 5-10 million per year. |
| 3. Social | <ul style="list-style-type: none"> ● Hindered participation, disruption of school activities | <ul style="list-style-type: none"> ● The impact of tidal waves (rob) can minimize productive social activities, such as communal efforts to build mosques, mutual assistance during wedding or funeral processions, and childbirth. Residents are more preoccupied with cleaning their homes due to the entry of mud, debris, and other waste into houses and settlements. ● School activities for children can be disrupted because the effects of tidal waves may make it difficult for them to attend school. |
| 4. Environmental | <ul style="list-style-type: none"> ● Clean water quality | <ul style="list-style-type: none"> ● There is a disruption in accessing clean water for drinking, bathing, and washing due to water contamination with mud and debris. |
| | <ul style="list-style-type: none"> ● Poor sanitation and waste accumulation | <ul style="list-style-type: none"> ● The disruption of access to clean water resources affects poor sanitation. Sanitation facilities (MCK - Mandi, Cuci, Kakus or Bathing, Washing, Toilet facilities) are disturbed due to waterlogging and the accumulation of carried debris. |
| | <ul style="list-style-type: none"> ● Disruption in the growth of mangrove seedlings | <ul style="list-style-type: none"> ● Newly planted mangrove seedlings, if exposed to seawater inundation for more than 12 hours, may suffer from growth disturbances. The mortality rate of mangrove seedlings due to prolonged seawater inundation could reach 40-60%. |
| 5. Infrastruct | <ul style="list-style-type: none"> ● Damages to embankments | <ul style="list-style-type: none"> ● The dykes that were independently built by the community are now starting to deteriorate, especially those in Cendi Manik village. The |

| In-risk Asset | Vulnerability Form | Estimated Impact/Risk Value |
|---------------|--|---|
| ure | and business premises | damage to the dykes is caused by high waves, which have the potential to lead to coastal erosion. |
| | <ul style="list-style-type: none"> Road and drainage damage | <ul style="list-style-type: none"> The damage to the facilities of businesses owned by the coastal residents, such as stalls for selling daily necessities and food, could be due to both tidal flooding and high waves. There are approximately 80 business stalls located in the coastal areas of South Lembar, Cendi Manik, and Lembar. Due to tidal flooding and floods, both asphalt and paved roads have been damaged. Water has eroded certain road sections, leading to potholes and overall road degradation. An estimated length of 12 kilometers of roads has been affected by flooding and tidal damage. The culverts, drainage ditches, and irrigation channels have also been affected by tidal flooding and floods. These events cause siltation, reducing their effectiveness in channeling water. |

Source; Primary data from interview and FGD results, 2023.

3.7 Community Perception and Capacity in Facing Disasters

a. Community Perception on Disasters

The community's perspective on facing the disasters they have been experiencing varies significantly. This can be traced through several assessment aspects related to psychological, economic, social, and environmental factors.

From a psychological perspective, generally, they experience anxiety and discomfort when they become aware of signs or when facing disasters. Despite experiencing these events for a long time, their concern always revolves around the magnitude of the disaster they might encounter at that moment and the risks they will face. The anomalies in recent disasters make it increasingly difficult for them to predict. A small fraction, however, seems resigned to disasters, considering such events as predestined by a higher power.

From a social aspect, despite frequently experiencing disasters, the desire to stay in their original place is high. The existing social system among them acts as a strong cohesive force, keeping them attached to their environment. There are strong social values of mutual assistance within families, neighbors, and community groups, providing the affected population with good resilience to cope with their environment.

Economically, it appears that they have strategies to cope with financial shortages due to reduced income from disaster impact. The readiness of the population to engage in various jobs during economic difficulties is one factor enabling them to survive tough times. Additionally, there's a practice among community members of lending assistance to those facing financial difficulties.

Regarding the environment, they recognize changes that have occurred in their surroundings. More frequent occurrences of high tides, unpredictable large waves, and increased instances of flooding are observed. The known causes are attributed to climate change and the degradation of forest and land resources. Deforestation due to farming and illegal gold mining is perceived as the cause of flooding. Meanwhile, high tides and big waves are associated with climate change and the development of infrastructure (port facilities).

b. Community Capacity to Face Disasters

In dealing with disasters, especially tidal flooding (rob), the community has taken actions for both mitigation and adaptation. These community activities related to mitigation and adaptation are primarily conducted independently. Thus, the community inherently possesses sufficient capacity to respond to the disasters they face. The following is an overview of the mitigation and adaptation measures and the social capital they employ in addressing these disasters.

Table 3.13. Mitigation, adaptation, and social capital

| | |
|--|---|
| Improvement of self-made flood embankments | In Cemara, the community has independently built a 2 km long embankment with a height of 0.5 meters. |
| Development of mangrove seedlings for source seedlings in mangrove rehabilitation and enrichment to reduce the rate of tidal flooding and high waves | In Cemara, Cendi Manik, and Central Sekotong, the community has the capability of seedling cultivation and has undertaken mangrove rehabilitation. The community's initiative to reduce disaster risk includes raising house foundations or constructing stilt houses |
| Construction of houses with higher | The community's initiative to reduce disaster risk includes |

| | |
|---|---|
| foundations | raising house foundations or building raised houses on stilts. |
| Community collaboration in building public infrastructure and social care. | Building embankments, places of worship, and mutual assistance when neighbors face difficulties. |
| The establishment of institutions supporting social resilience across economic, social, and disaster-related aspects. | Small business groups, groups for Fishermen, Farmers, and fishpond breeders, SIBAT (Community-Based Disaster Preparedness), Destana, and ecotourism-aware groups. |
| Support from policy regulations at the village level regarding disaster readiness formed by BPBD (Regional Disaster Management Agency) and village initiatives. | Village regulations regarding disasters, village support in providing infrastructure for mangrove tourism. |
| The community's self-preparedness in facing emergency situations during disasters | Responsive actions to immediately secure oneself during disasters. |

Source: Primary data from interview and FGD results, 2023

IV. CONCLUSION AND RECOMMENDATIONS

4.1 Conclusion

- a. The socio-economic conditions of the coastal area's community can be described as follows: The community holds a strong social capital in terms of mutual assistance in resolving individual, household, kinship, group, and community issues. This positive social value is also crucial in the context of disasters for mitigation and adaptation measures to climate change. The livelihood sources of the coastal area's population are quite diverse. Prominent activities include fishing, farming, animal husbandry, aquaculture, small and medium enterprises, agricultural services, carpentry, and artisanal mining. Generally, the people engage in multiple occupations, such as fishermen also being farmers, farmers also rearing livestock, livestock keepers and miners, among others. Income from these varied sources ranges from Rp 8,700,000 to 15,600,000 per year. If associated with the per capita income, with an average family size of 4 members per household, the income range for farmers and fishermen is around Rp 5,958 to Rp 12,534 per capita per year.
- b. The various disasters frequently faced by the coastal communities in the six villages include tidal flooding (rob), floods, droughts, high waves, and coastal erosion. Tidal flooding occurs every month, lasting 3-5 days, with sea water entering residential areas at heights of 20-30 cm. However, the impact of tidal flooding becomes more severe if floods occur simultaneously 2-3 times a year. Tidal flooding affects approximately 1,729 households in the four villages.
- c. Based on the analysis of the disaster hazard level, tidal flooding falls into the category of extremely high or very hazardous, while floods and droughts are classified as hazardous. Additionally, strong winds/high waves and coastal erosion are categorized as somewhat hazardous. The community's perceptions in dealing with disasters are quite varied. From a psychological aspect, there is always anxiety regarding the dangers of tidal flooding or floods due to the unpredictability of their cycle and scale of impact.

4.2 Recommendations

- a. The Four study villages have diverse natural resources and distinct characteristics in terms of their social, economic, and community institutional aspects. Mangrove resources are present in South Lembar, Cendi Manik, Central Sekotong, and West Sekotong. However, prominent utilization of mangroves is observed in South Lembar, Cendi Manik, Central Sekotong, and West Sekotong. Considering four aspects: the condition and value of mangroves, the level of tidal flooding impact, social capital, and the level of vulnerability to climate change-related disasters, the villages suitable for the project site are South Lembar, Cendi Manik, Central Sekotong, and West Sekotong.
- b. The discussions mentioned above still rely on quantitative values using estimated interview results, such as the area of fishponds, agricultural land, infrastructure size, and the number of affected people for mild, moderate, and severe scales. These aspects need further exploration and should be approached using specific methods, including the utilization of spatial data.
- c. The extent of the disaster's impact from various aspects-economic, social, environmental-in relation to the magnitude of the project's investment benefits needs a deeper analysis using the cost-benefit analysis tool.

Annex 5. Documentation of Stakeholder Consultation



The activity was carried out on Tuesday, December 27, 2022, using a venue at the West Lombok Regency Bappeda Office. The activity involved 19 people (14 men and 5 women) from elements including West Lombok BAPPEDA, BPBD NTB, Provincial PU PR, DLHK, BMKG, NGOs, Lembar Sub-District Head, Village Government, Fishermen's Groups and Environmental Youth Leaders. This FGD activity aims to deepen information related to various events, periods of occurrence, social and environmental impacts, as well as adaptation and mitigation programs from existing *rob* disasters. Some of the points from the discussion results include:

- Head of Emergency and Logistics BPBD Lobar said several villages were affected by the tidal flood, including the villages of Lembar Selatan, Pelangan, Sekotong Tengah, Sekotong Barat, Buwun Mas, Lembar, Cendi Manik, Taman Ayu and Labuhan Tereng. It is estimated that there are 1,450 more people affected.
- Rob floods in the West Lombok district are frequent occurrences. The last time it happened was Friday 17 June 2022 in Lembar Village. Monitoring results from BPBD at least \pm 207 households were affected by the Rob flood. in Buncit hamlet at least \pm 70 families, Kebon Bongor hamlet as many as \pm 97 families and Petak hamlet as many as \pm 40 families.
- The impact of the Rob flood resulted in losses for residents in the form of inundating residents' homes, agricultural land and ponds owned by residents. West Lombok Regency BPBD has coordinated with the Provisional BPBD and other stakeholders for emergency management at the incident location.
- According to the BMKG Climatology Station Class I West Lombok, the Rob incident in West Lombok Regency was due to the La Nina phenomenon (extreme weather) in the form of strong winds and heavy rainfall. Rainfall in the NTB region on the third of September 2022 is dominated by the low category (<50 mm). The highest recorded rainfall occurred at Gunung Sari Rain Post, Kab. West Lombok of 154 mm/dasarian. The nature of rain on the third of September 2022 in the West Lombok Regency tends to vary from Below Normal (BN) to Above Normal (AN).
- Cemara Hamlet, Lembar Village is one of the areas that is prone to Rob disasters. Lastly, the water level can reach the knees of adults and lasts up to \pm 2 hours. Residents who know that sea water is entering the settlement panic. However, residents remained in their homes.
- Tidal floods also occurred in several villages in Sekotong. Tagana Lobar said that there were three villages affected by the tidal flood. Among them, Madak Belek Hamlet 1, Empol Preparation Village, Kemanuk Hamlet, Buwun Mas Village, Pewaringan Hamlet, Pelangan Village.
- The South Lembar Village Government has not budgeted a special allocation of funds for handling Rob because the 2022 budget is still not optimal. Refocusing is still on handling Covid-19. We are still waiting for changes in budget allocations from the central government, so that in the future the budget for handling Rob can be implemented with the existence of a legal budget umbrella.

- However, in 2022 the government together with self-help communities, especially Cemara Hamlet, have made a talud/trap to prevent the rob from entering the settlement. However, the talud that was built is felt to be lacking because it has not covered several Robust entry points into residents' settlements. Through this forum we hope that there will be notes that can serve as recommendations to the relevant agencies to jointly develop the Village, especially in handling the Rob disaster which often occurs in Lembar Selatan Village.
- When a Rob flood occurs, the sub-district and village governments immediately coordinate with BPBD Agency, Social Affairs and the Head of Maritime Office to evacuate residents affected by the disaster so that they can be dealt with immediately. So that the process of evacuating residents can be carried out.
- The government has also mediated with private parties close to the port area to jointly contribute to adaptation and handling of Rob floods. The mediation process is still ongoing, hopefully in the future there will be a green light.
- Adaptation activities have been carried out by several groups including: DLH West Lombok Regency, together with the South Lembar Village Government, BRI Bank and youth such as by planting 2,000 mangroves in the Cemara Beach tourist area and planting activities with the Indonesian Air Force in commemoration world mangroves day.
- Careful planning is needed for the roadmap for the coastal area of the Cedar Hamlet so that tourism development and management plans can be integrated with disaster response development. Because this location is very vulnerable to the tidal water disaster. So that all stakeholders such as NGOs, Government, Entrepreneurs, Community Leaders, Youth Leaders and other elements to sit together to build Cedar Hamlet and West Lombok.
- Whereas the 2023 Village Fund Budget (ADD) has not yet been determined, but there has been a commitment from village officials to oversee the disaster budget, both for improving the community's economy and the environment to be discussed in hamlet and village meetings as a priority program.

Annex 6. Operational Definitions

| Component | Outputs | Activities | Operational Definitions |
|---|--|---|---|
| Component 1. Village governance and institutional capacity | Output 1.1. Institutions, policy and planning at the village level that are responsive to climate change disaster impacts | 1.1.1. Recruitment of village facilitators for climate-related disaster preparedness. | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : project management (Partnership, Transform, Konsepsi) ▪ Objectives: announcement of recruitment of village facilitators for project implementation at village level |
| | | 1.1.1.a. Interview/Selection for Village Facilitators | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi manik and West Sekotong ▪ Parties : project management (Partnership, Transform, Konsepsi) ▪ Objectives: selecting suitable candidates to perform the role of village facilitators for village-level project implementation |
| | | 1.1.1.b. Mentoring and training on project framework for village facilitators | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village facilitators, project management (Partnership, Transform, Konsepsi) ▪ Objectives: increase knowledge through training and guidance related to project scope for village facilitators |
| | | 1.1.1.c. Contracting and assignment of village facilitators | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village facilitators, project management ▪ Objectives: existence of an employment contract for village facilitators |
| | | 1.1.2. Participatory climate risk analysis (PCRA) by community to identify and assess aspects related to hazard characteristics, existing capacities, vulnerabilities, risk mapping, as well as risk level assessment | <ul style="list-style-type: none"> ▪ Scope : West Lombok Regency Level, Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) ▪ Parties : Village facilitators, PCRA experts, risk mapping experts, project management ▪ Objectives : Preparation of assessment report related to hazard characteristics, existing capacities, vulnerabilities, risk mapping, as well as risk level assessment |
| | | 1.1.3. Establishment of a village climate disaster preparedness work team from village volunteer members and added with other community components. | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi manik and West Sekotong ▪ Parties : Farmer groups, fishermen, village governments, village facilitators, project management ▪ Objectives: Establishment of village-level climate disaster preparedness work |
| | | 1.1.4. Training packages for village government and village climate disaster preparedness work team; | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi manik and West Sekotong ▪ Parties : Members of the village disaster preparedness work team (SK village disaster preparedness team), village facilitators, project management ▪ Objectives: Increased knowledge of village government and village disaster preparedness work team. |
| | | 1.1.5. Formulation of local policies on climate resilience (both at village and district levels) | <ul style="list-style-type: none"> ▪ Scope : West Lombok Regency Level, Village Level (Central Sekotong Village, South Lembar, Cendi manik and West Sekotong) ▪ Parties : West Lombok District Government, Village Government, Village Facilitator, Project Management ▪ Objectives: formulate policies on climate resilience at the village and district levels |
| | | 1.1.6. Facilitation for formulating climate disaster-related guidelines/plans/standards (contingency plan, early warning system); | <ul style="list-style-type: none"> ▪ Scope : Village Level (Central Sekotong Village, South Lembar, Cendi manik and West Sekotong) ▪ Parties : Village Government, Village Facilitator, Project Management ▪ Objectives: Preparation of guidelines/plans/standards related to climate disasters including contingency plans and early warning systems. |

| Component | Outputs | Activities | Operational Definitions |
|-----------|---|---|--|
| | | 1.1.7. Formulation of policy brief/policy paper to strengthen climate resilience actions or policies at sub-national level | <ul style="list-style-type: none"> Scope : West Lombok Regency Parties : West Lombok District Government, Experts, Project Management Objectives: Prepare a policy brief/policy paper to strengthen climate resilience actions or policies at the local level |
| | | 1.1.8. Technical assistance on policy making and governance process at subnational level to support climate adaptation measures at village level (including strengthening knowledge management systems) | <ul style="list-style-type: none"> Scope : West Lombok Regency Parties : West Lombok District Government, Experts, Project Management Objectives: Prepare a policy brief/policy paper to strengthen climate resilience actions or policies at the local level |
| | Output 1.2. Village community action plan on climate-related disaster risk reduction in coastal areas | 1.2.1. Dissemination of PCRA's results to the wider community through presentation of work team representative in workshop for each village | <ul style="list-style-type: none"> Scope : West Lombok Regency Level, Village Level (Central Sekotong Village, South Lembar, Cendi manik and West Sekotong) Parties : Village disaster preparedness work team, Village facilitators, PCRA experts, risk mapping experts, project management Objectives : Dissemination of project assessment related to hazard characteristics, existing capacities, vulnerabilities, risk mapping, as well as risk level assessment. |
| | | 1.2.2. Community Action Planning (CAP) on climate resilience through community discussion series and field workshop. Formulation of CAP also consider input and comments in previous workshop regarding PCRA' results | <ul style="list-style-type: none"> Scope : Village Level (Central Sekotong Village, South Lembar, Cendi manik and West Sekotong) Parties : Village disaster preparedness work team, Village facilitators, PCRA experts, risk mapping experts, project management Objectives: Develop community-based climate resilience action plans at the village level |
| | | 1.2.3. Facilitation on integration Community Action Plan (CAP) with the village government's annual plan and budget through discussion series with village government; | <ul style="list-style-type: none"> Scope : Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) Parties : Village disaster preparedness work team, village facilitators, PCRA experts, risk mapping experts, project management Objectives: Integrate community-based climate resilience action plans with village government annual plans and budgets (RKP) |
| | | 1.2.4. Facilitation of annual village development planning forum to decide on village development priority programs in the current year including CAP on climate-induced disaster resilience | <ul style="list-style-type: none"> Scope : Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) Parties : Village disaster preparedness work team, Village facilitators, PCRA experts, risk mapping experts, project management Objectives: Develop priority village development programs included in climate resilience action plans in village development planning. |
| | | 1.2.5. Advocacy of CAP to sub-national government policies both at district and provincial levels through lobbying and discussion series by inviting sub-national government representatives both district and provincial levels. | <ul style="list-style-type: none"> Scope : West Lombok Regency, West Nusa Tenggara provincial level Parties : West Lombok District Government, NTB Provincial Government, Experts, Project Management Objectives: Advocating local government policies both Caupatent and Province related to climate resilience action plans. |

| Component | Outputs | Activities | Operational Definitions |
|---|---|---|--|
| Component 2. Capacity Building on Climate Adaptation | Output 2.1. Increased knowledge and skill of the targeted communities, including women and vulnerable groups on climate adaptation actions | 2.1.1. Trainings for targeted community on climate adaptation and resilience. | <ul style="list-style-type: none"> ▪ Scope : Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management ▪ Objectives: Increase community knowledge through training and skills in climate adaptation and resilience |
| | | 2.1.2. Conducting climate field school on adaptation actions on coastal areas conditions (mangrove, land-based farming in coastal, salt farming),; in-class for 6 times in each targeted community, and and preparing demonstration plots for climate adaptation (field practices). | <ul style="list-style-type: none"> ▪ Scope : Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management. ▪ Objectives: Increase knowledge of community groups through field schools for mitigation actions accompanied by preparing demonstration pilot activities (field practices) |
| | | 2.1.3. Conducting simulation/exercise to respond to climate induced disaster by testing the contingency plans and early warning system | <ul style="list-style-type: none"> ▪ Scope : Village Level (Central Sekotong Village, South Lembar, Cendi manik and West Sekotong) ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management ▪ Objectives: Community groups have the ability to respond to climate-induced disasters using contingency planning instruments and early warning systems. |
| | | 2.1.4. Developing and implementing a learning platform and process for communities related to climate adaptation actions through regular learning forums in each village and cross visits to other areas; | <ul style="list-style-type: none"> ▪ Scope : Village Level (Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong) ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management ▪ Objectives: The existence of regular learning forums and mutual learning between villages for the learning process of climate adaptation actions |
| | | 2.1.5. Procurement of climate-induced disaster information and documentation systems: | <ul style="list-style-type: none"> ▪ Scope : 1 information system covering the villages of Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management ▪ Objectives: Creation of information systems and documentation of climate-related disasters. |
| | | 2.1.6. Documenting knowledge and best practices of community actions in climate change by producing Stories of Change (SoC) from targeted groups, videos, and book. | <ul style="list-style-type: none"> ▪ Scope : 1 information system covering the villages of Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village disaster preparedness work team, village apparatus, sub-district government representatives, community groups, village facilitators, project management ▪ Objectives: The existence of videos and books documenting knowledge and best practices of community action |

| Component | Outputs | Activities | Operational Definitions |
|-----------|---|---|---|
| | Output 2.2. Models of coastal climate adaptation are developed and demonstrated at the targeted community | 2.2.1. Conducting analyses and model development on climate adaptation in coastal areas to identify, analyze, and design of model by hiring the expert team with taking into account PCRA's results and CAP. | <ul style="list-style-type: none"> ▪ Scope : 1 information system covering the villages of Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village disaster preparedness work team, community groups, village facilitators, project management ▪ Objectives: Availability of climate adaptation model design based on PCRA dan Climate action plan |
| | | 2.2.2. Procurement of climate-induced adaptation facilities/equipment: construction of fish pond, fish seed, stationaries (silvofishery in mangrove); | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Village facilitators, project management ▪ Objectives: Construction of climate adaptation facilities |
| | | 2.2.3. Demonstration of climate adaptation models of coastal climate adaptation at least 3 models i.e silvofishery in the mangrove, climate-smart land-based farming in the coastal, and ecotourism services. | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Community groups, village facilitators, project management ▪ Objectives: The existence of climate adaptation models in coastal areas in the form of demonstration plots |
| | | 2.2.4. Documentation best practices and lesson learned from climate adaptation models in coastal area by producing practical guidebook and videos. | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Expert tim, project management ▪ Objectives: Practical guidebooks/videos for best practice documentation and learning of climate adaptation models in coastal areas |
| | Output 3.1. Rehabilitation and enhancement of coastal ecosystems to adapt to climate impacts at selected sites are demonstrated | 3.1.1. Participatory coastal area spatial plan integrated with climate-induced disaster resilience. | <ul style="list-style-type: none"> ▪ Scope : West Lombok Regency, West Nusa Tenggara provincial level ▪ Parties : West Lombok District Government, NTB Provincial Government, Experts, Project Management ▪ Objectives: Advocating local government policy plans (districts and provinces) for climate resilience action plans |
| | | 3.1.2. Facilitation on development of community-based nurseries for mangrove rehabilitation | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Community groups, village facilitators, project management ▪ Objectives: availability of community-based nurseries for mangrove rehabilitation activities |
| | | 3.1.3. Mangrove planting in 20-hectare areas at selected sites; | <ul style="list-style-type: none"> ▪ Scope : South Lembar, Cendi Manik ▪ Parties : Community groups, village facilitators, project management ▪ Objectives: mangrove rehabilitation on an area of 20 ha. |
| | | 3.1.4. Facilitation in providing infrastructure packages for climate-disaster risk reduction in mangrove areas; infrastructures: rob-resistant embankments and rob-resistant houses; | <ul style="list-style-type: none"> ▪ Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong ▪ Parties : Community groups, village facilitators, project management ▪ Objectives: Availability of climate risk reduction infrastructure in mangrove areas, dikes and tidal-resistant houses. |
| | | 3.1.5. Monitoring and evaluation for mangrove rehabilitation | <ul style="list-style-type: none"> ▪ Scope : South Lembar, Cendi Manik ▪ Parties : Community groups, village facilitators, project management ▪ Objectives: Mangrove rehabilitation on an area of 20 ha. |
| | Component 3. Coastal | Output 3.2. Community | 3.2.1. Value chain analyses to develop the potential supply chain for smallholder |

| Component | Outputs | Activities | Operational Definitions |
|---|--|--|--|
| ecosystem resilience and Sustainable Livelihood | income-generating and productive economic activities are increased | fisheries and coastal community livelihood | <ul style="list-style-type: none"> Objectives: Availability of value chain documents for supply chain development for the livelihoods of coastal communities. |
| | | 3.2.2. Identification of business opportunities and product development through study use mixed method (both participatory/qualitative and survey/quantitative technique); | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: Availability of business opportunity identification and product development documents |
| | | 3.2.3. Facilitation of training packages for sustainable smallholder fisheries and livelihood: good practices on fisheries cultivation; diversification of products/processing; marketing. | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: Implementation of training for community livelihood development (aquaculture, product diversification, marketing) |
| | | 3.2.4. Facilitation small-scale business licensing and product certification | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: The group has small-scale business licensing and product certification |
| | | 3.2.5. Procurement of equipment for productive economies and businesses i.e production machines, packaging machines, etc; | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: Equipment assistance for a productive economy for groups that already have business licenses |
| | | 3.2.6. Technical assistance for developing market-demand commodities and products | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: The project assists target groups for commodity development and product marketing both on a local and regional scale |
| | | 3.2.7. Facilitation on access to finance (including venture capital) to support communities' businesses by developing network or collaboration with banks or private sectors. | <ul style="list-style-type: none"> Scope : Central Sekotong Village, South Lembar, Cendi Manik and West Sekotong Parties : Community groups, village facilitators, project management Objectives: Facilitate and promote access to financing and cooperation with private sectors/banks/financial institutions to support communities group enterprises |

Annex 7. Core Outcome Indicator from the Fund's Results Framework

| Expected Result | Indicators |
|--|---|
| Outcome 3. Strengthened awareness and ownership of adaptation and climate risk reduction processes at local level | 3.1. Percentage of targeted population aware of predicted adverse impacts of climate change, and of appropriate responses 3.2. Percentage of targeted population applying appropriate adaptation responses |
| Output 3.1: Targeted population groups participating in adaptation and risk reduction awareness activities | 3.1.1. Number of news outlets in the local press and media that have covered the topic |

| 3.1. Percentage of targeted population aware of predicted adverse impacts of climate change, and of appropriate responses | | | |
|---|--|---|--|
| | Percentage of targeted population aware of predicted adverse impacts of climate change, and of appropriate responses | Percentage of targeted population applying appropriate adaptation responses | |
| Baseline | 5% | - | |
| Target (by Mid-term) | 50% | 50% | |
| Target (by end of project) | 90% | 90% | |

Definition:

Total population based on age group over 17 years in four villages: **8.689** person (Total population in Four Villages are **34.756** person)

| 3.1.1. Number and type of risk reduction actions or strategies introduced at local level | | |
|--|------------------------------|------|
| | Number of actions strategies | Type |
| Baseline | - | |
| Target (by end of project) | | |

| Expected Result | Indicators |
|---|---|
| Outcome 4. Increased adaptive capacity within relevant development sector services and infrastructure assets | 4.2. Physical infrastructure improved to withstand climate change and variability-induced stress |
| Output 4: Vulnerable development sector services and infrastructure assets strengthened in response to climate change impacts, including variability | 4.1.1. No. and type of development sector services modified to respond to new conditions resulting from climate variability and change (by sector and scale) 4.1.2. No. of physical assets strengthened or constructed to withstand conditions resulting from climate variability and change (by sector and scale) |

| 4.1.2. No. of physical assets strengthened or constructed to withstand conditions resulting from climate variability and change (by sector and scale) | | | |
|---|------------------|------------------------------|---|
| | Number of Assets | Type of Assets | Project Intervention |
| Baseline | 1 | Talud (Sea Wall/ Embankment) | Already constructed |
| Target (by end of project) | 1 | | Rehabilitation and Improvement of + 2.350 meters embankment |

| Expected Result | Indicators |
|--|--|
| Outcome 5. Increased ecosystem resilience in response to climate change and variability induced stress | # Hectares of mangrove ecosystem protected and rehabilitated |
| Output 5: Vulnerable ecosystem services and natural resource assets strengthened in response to climate change impacts, including variability | 5.1 No. of natural resource assets created, maintained or improved to withstand conditions resulting from climate variability and change (by type and scale) |

| 5.1. No. of natural resource assets created, maintained or improved to withstand conditions resulting from climate variability and change (by type and scale) | | | |
|---|-------------|-----------------------|---|
| | Number (Ha) | Type of Natural Asset | Intervention |
| Baseline | - | Mangrove Ecosystems | Rehabilitation of ± 20 hectares of mangrove ecosystems, Monitoring, Maintenance and preservation of mangrove areas) |
| Target (by mid of project) | 10 | | |
| Target (by end of project) | 20 | | |

Note: types of beneficiary in 4 villages (South Lembar, Central Sekotong, Cendi Manik, West Sekotong)

| Adaptation Fund Core Impact Indicator "Number of Beneficiaries" | | | | | |
|---|--------------|--|--|-------------------------------|----------------------|
| Beneficiaries | Baseline | Target at Project Approval (absolute number) | Adjusted target first year of Implementation | Target by Mid –end of Project | Actual at completion |
| Direct beneficiaries supported by the project | | | | | |
| Farmer* | 4.635 | 518 | 233 | 284 | 518 |
| Fisherman/women* | 1.661 | 605 | 272 | 333 | 605 |
| Cattlemen* | 1.066 | 172 | 78 | 95 | 172 |
| Trader* | 1.816 | 434 | 196 | 238 | 434 |
| | 9.178 | 1.729 | 779 | 950 | 1.729 |
| Indirect beneficiaries supported by the project | | | | | |
| Farmer | 4.121 | | - | - | - |
| Fisherman/women | 1.056 | | - | - | - |
| Cattlemen | 894 | | - | - | - |
| Trader | 1.385 | | - | - | - |
| | 7.456 | | | | |

Annex-8. Gender Action Plan

Impact : There are no barriers for women and other vulnerable groups to actively participate in improving livelihood resilience and climate change adaptation activities, especially from mangrove ecotourism.

Outcome : Approximately 30% women and other vulnerable groups of project beneficiaries increase their awareness and able to contribute to enhancing livelihood resilience and climate change adaptation.

Output : Increasing women and other vulnerable groups participation in enhancing livelihood resilience and climate adaptation activities through.

Commented [SM13]: Jadikan annex dengan menambahkan informasi tentang align dengan output project dan anggaran

| No | Activities | Indicators | Targets | Timeline | Responsibilities | Costs | Aligned with Project Budget |
|----|---|--|--|----------------|------------------------------|-------------|---|
| 1 | Encourage women's involvement in training and work teams in formulating policies and strengthening climate change adaptation knowledge | Collaboration between the Village Government and 20 GEDSI representatives in training and work teams in formulating policies and strengthening climate change adaptation knowledge | <u>Mid-term</u> : A formal group with the Village Government and 10 GEDSI representatives in formulating policies and strengthening climate change adaptation knowledge <u>Project Finalization</u> : A formal group with the Village Government and 20 GEDSI training and work teams in formulating policies and strengthening climate change adaptation knowledge | Star by year-1 | Executing Entity, Government | USD 207.633 | Activities: 1.1.2. Participatory climate risk consultation (PCRC) to explore and detail the characteristics and diversity of climate risks at the household level based on socio-economic aspects and GEDSI 1.1.3. Formation of village climate disaster preparedness working teams from village volunteer members and supplemented by other community components. 1.1.4. Series of training workshops for village governments and village climate disaster preparedness working teams; 1.1.5. Formulation of local policies on climate resilience at the village level 1.1.6. Facilitation of formulation of guidelines/plans/standards related to climate disasters (contingency plans, early warning systems); 1.1.7. Formulation of policy briefs/policy papers to strengthen climate resilience actions or policies at the sub-national level 1.1.8. Technical assistance to strengthen the knowledge management system on climate adaptation. |
| 2 | Inclusive Group-Based Planning and Action for Sustainable, Gender-Responsive Programs, which include: Regular group meetings; address social and institutional barriers; Formalization of groups through Village Government Decrees (SK); | Number Participation of women and persons with disabilities meets targets, with their voices heard and acted upon. They gain confidence and engage more in public and development activities, while GEDSI is integrated into climate and | <u>Mid-term</u> : 259 women and persons with disabilities actively participate and benefit, with women representatives and the GEDSI agenda integrated into Musrenbang at village and district levels. <u>Project Finalization</u> : 518 women and persons with disabilities actively participate and benefit, with women representatives and the GEDSI agenda | Star by year-1 | Executing Entity | USD 17.960 | Activities: 1.2.1. Dissemination of PCRC results to the wider community through presentations by representatives of the working team in workshops for each village 1.2.2. Community Action Planning (CAP) on climate resilience through a series of community discussions and field workshops. The formulation of the CAP also takes into account input and comments in previous workshops on PCRC results 1.2.3. Facilitate the integration of the Community Action Plan (CAP) with the annual plan and budget of the village government through a series of discussions with the village government 1.2.4. Facilitate the annual village development planning forum to decide on priority village development programs in the current year including the CAP on climate disaster resilience 1.2.5. Advocacy of the CAP on local government policies at both |

| No | Activities | Indicators | Targets | Timeline | Responsibilities | Costs | Aligned with Project Budget |
|----|--|---|---|----------------|------------------------------|-------------|--|
| | Advocacy for integration of action plans into village and district development policies | disaster planning through inclusive <i>Musrenbang</i> consultations. | integrated into Musrenbang at village and district levels. | | | | the district and provincial levels through lobbying and a series of discussions by inviting representatives of local governments at both the district and provincial levels. |
| 3 | Ensuring GEDSI Groups' Access to Knowledge Enhancement and Capacity-Building for Inclusive Program Participation and Benefit. | Number participation of women and persons with disabilities is achieved, with increased confidence and active involvement in public and development initiatives. | <u>Mid-term</u> : 259 women and persons with disabilities engage in and benefit from the programs. <u>Project Finalization</u> : 518 women and persons with disabilities engage in and benefit from the programs. | Star by year-1 | Executing Entity | USD 115.176 | Activities: 2.1.1. Training for targeted communities on climate adaptation and resilience. 2.1.2. Organizing climate field schools on adaptation actions in coastal areas (mangroves, coastal dryland farming, salt cultivation),; in class for 6 times in each targeted community, and preparing demonstration plots for climate adaptation (field practice). 2.1.3. Conducting simulations/drills to respond to climate disasters by testing contingency plans and early warning systems 2.1.4. Developing and implementing learning platforms and processes for communities on climate adaptation actions through regular learning forums in each village and cross-visits to other areas 2.1.6. Documenting knowledge and best practices of community actions on climate change by producing Stories of Change (SoC) |
| 4 | SME development will offer training on growth, credit, and product improvement, with sustainability ensured through group formation, stakeholder connections, and Village Government Decrees (SK). | The participation of women and individuals with disabilities in training will meet targets, with at least 40% of their SMEs expanding market reach and using digital marketing. | <u>Mid-term</u> : 60 beneficiaries (30% women and youth) will actively participate, with 20% of them becoming independent SME champions, expanding markets, and using digital marketing. <u>Project Finalization</u> : 120 beneficiaries (60% women and youth) will actively participate, with 40% of them becoming independent SME champions, expanding markets, and using digital marketing. | Star by year-2 | Executing Entity, Government | USD 33.908 | Activities: 3.2.2. Facilitate training packages for fisheries and sustainable smallholder livelihoods: good practices in fisheries cultivation; product/processing diversification; marketing. 3.2.3. Facilitate small business licensing & product certification 3.2.4. Procurement of equipment for productive economy and business, i.e. production machines, packaging machines, etc. 3.2.5. Technical assistance to develop commodities and products in market demand 3.2.6. Facilitate access to finance (including venture capital) to support community businesses by developing networks or collaboration with banks or the private sector |

Annex-9. Risk Identification in Activities That Have a Significant Impact

| Activities | Risk | Risk Mitigation |
|--|--|---|
| Mangrove planting in an area of 20 hectares in selected locations; | Environmental risks <ol style="list-style-type: none"> 1. The growth of mangrove planting is very slow due to low community participation in plant maintenance 2. The presence of pests such as caterpillars that cause mangrove seedlings to die 3. Tritip pest attack (Balanus amphitrite), which results in the death of mangrove stems 4. The tides with a height of more than 1 meter, which results in mangrove seedlings sinking in the long term 5. Dominance of certain mangrove species over other species | <ol style="list-style-type: none"> 1. The use of certified mangrove seeds and community assistance in conducting maintenance and monitoring evaluations 2. Mangrove pest control through vegetable pesticide spraying 3. Tritip pest control 4. The need to use planting techniques such as checkered clumps or protrusion to reduce the risk of seedling death due to tides 5. Cultivation of mangrove seedlings consisting of several species that are suitable for the habitat conditions at the project site |
| | Social Risk The local community does not want to be involved in the project activities | Ensure consistent participation of local communities in all project activities at a proportional level. |
| Provision of infrastructure packages for climate disaster risk reduction in mangrove areas; Infrastructure: rob-resistant embankment | Environmental risks <ol style="list-style-type: none"> 1. Greenhouse gases derived from vehicles transporting project materials 2. Dust pollution due to the entry and exit of operational vehicles carrying project materials | Environmental mitigation <ol style="list-style-type: none"> 1. The use of vehicles that emit low emissions is based on the results of emission tests from the Transportation Agency. 2. Carry out regular watering at the project site exposed to dust. |
| | Social risks <ol style="list-style-type: none"> 1. The local community does not want to be involved in the project activities 2. Local communities will not get access to jobs for the improvement of the project's infrastructure | <ul style="list-style-type: none"> ▪ Ensure consistent participation of local communities in all project activities at a proportional level. ▪ Develop SOPs regarding the involvement of local communities in the development of project infrastructure |
| Facilitation of fisheries training packages and sustainable smallholder livelihoods: fisheries aquaculture good practices; product diversification/ processing; marketing. | Environmental risks <ol style="list-style-type: none"> 1. Soil pollution due to additional plastic waste from training activities 2. The use of preservatives in food that can cause health problems. | <ul style="list-style-type: none"> ▪ Limiting the use of plastics in project activities ▪ Assistance, monitoring and laboratory analysis of the use of preservatives |
| | Social Risks <ol style="list-style-type: none"> 1. Women get fewer opportunities than men due to the influence of society's culture 2. Beneficiaries do not have access to adequate capital and markets as a follow-up to their need for business development for project interventions | <ul style="list-style-type: none"> ▪ Implement consistency in the proportion of women's and men's involvement in project activities ▪ Connect beneficiaries with banks and facilitate business licensing and facilitate product marketing |
